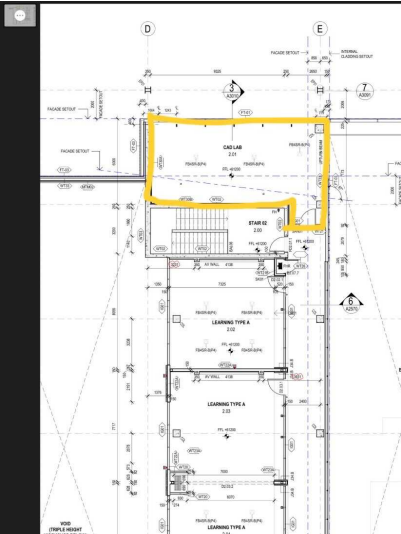


(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

94 - CAD Lab - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.01 CAD LAB
Status	Closed
Due Date	
Created by	George Awad on Wednesday 01 March, 2023, 9:37:46 am
Modified by	George Awad on Thursday 24 August, 2023, 7:11:41 am
Downloaded	Thursday 24 August, 2023, 7:11:45 am
Template	NSW TAFE IATC – Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 1:40:42 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 1:40:53 PM	

2

Utech – Is the power installed per drawings?

Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 1:40:42 pm

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Level 1 South Rooms ITP.pdf	2023/08/24, 7:11:23 AM	George Awad	–
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/08/24, 7:11:19 AM	George Awad	–

3

Utech – Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:42:28 pm

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Level 1 South Rooms ITP.pdf	2023/08/24, 7:11:24 AM	George Awad	–
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/08/24, 7:11:21 AM	George Awad	–

4

Utech – Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:42:28 pm

5

Foran – Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:07:51 pm

6

Foran – Is the drainage installed as per drawings? Attached evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:07:51 pm

7 Foran – Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Monday 10 July, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:07:51 pm
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Thursday 24 August, 2023  George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:11:27 am
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:11:27 am
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:11:27 am
11 ZipClad – Water Test Conducted on Facade * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:11:27 am
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:11:27 am
Photos (1)	



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 7:11:20 AM**

13

Is the acoustic insulation installed as per specification/drawings? Attache evidence *
Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:11:27 am

14

Are the mechanical works installed as per drawings? Attach evidence *
Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:11:26 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB SN installation ITP.pdf	2023/08/24, 7:11:25 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [0].pdf	2023/08/24, 7:11:25 AM	George Awad	-
MSSB NN installation itp.pdf	2023/08/24, 7:11:24 AM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/08/24, 7:11:23 AM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *
Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:11:26 am

16

Dunrite Accepts walls are ready for sheet *
Hold Point



Hills Pan
Thursday 24 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:11:27 am

17 North Image * Hold Point

Tuesday 30 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:11:28 am

Photos (1)



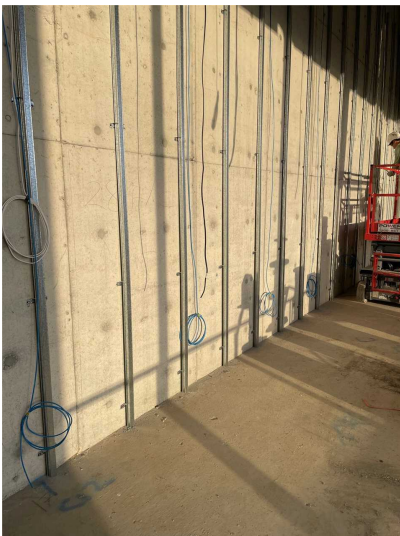
Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/08/24, 7:11:19 AM

18 East Image * Hold Point

Tuesday 30 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:11:26 am

Photos (1)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/08/24, 7:11:21 AM

19 South Image * Hold Point

Tuesday 30 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:11:26 am

Photos (1)



Captured by: **George Awad ADCO
CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 7:11:22 AM**

20 West Image * Hold Point

Tuesday 30 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:11:26 am

Name

Signature

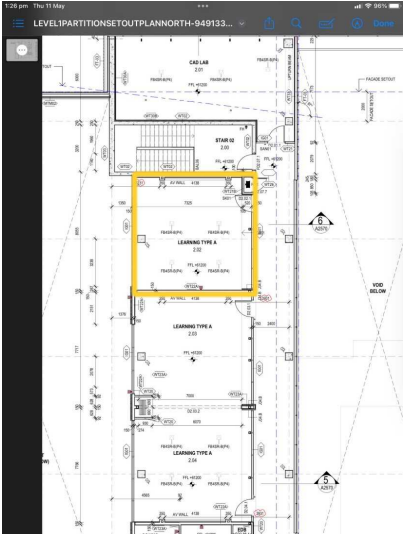
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

95 - Learning Type A - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.02
LEARNING TYPE A	
Status	Closed
Due Date	
Created by	George Awad on Wednesday 01 March, 2023, 9:39:03 am
Modified by	George Awad on Thursday 24 August, 2023, 7:19:11 am
Downloaded	Thursday 24 August, 2023, 7:19:15 am
Template	NSW TAFE IATC – Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. *	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 1:45:26 pm
Hold Point	
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 2:25:07 PM	

2

Utech – Is the power installed per drawings?

Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 1:45:26 pm

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Level 1 South Rooms ITP.pdf	2023/08/24, 7:17:50 AM	George Awad	–
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/08/24, 7:17:44 AM	George Awad	–

3

Utech – Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:42:54 pm

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/08/24, 7:17:47 AM	George Awad	–
Level 1 South Rooms ITP.pdf	2023/08/24, 7:17:54 AM	George Awad	–

4

Utech – Electrical services roughed in according to approved room layout drawings. *

Hold Point

George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:42:54 pm

5

Foran – Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:08:42 pm

6

Foran – Is the drainage installed as per drawings? Attached evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:08:42 pm

95 - Learning Type A - Pre Sheet-ITP

7 Foran – Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Monday 10 July, 2023 <i>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:08:42 pm</i>
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Thursday 24 August, 2023 <i>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:17:58 am</i>
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes <i>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:17:57 am</i>
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes <i>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:17:57 am</i>
11 ZipClad – Water Test Conducted on Facade * Hold Point	N/A <i>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:17:57 am</i>
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes <i>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:17:57 am</i>
Photos (1)	



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 7:17:49 AM**

13

Is the acoustic insulation installed as per specification/drawings? Attache evidence *
Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:17:57 am

14

Are the mechanical works installed as per drawings? Attach evidence *
Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:17:57 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB NN installation itp.pdf	2023/08/24, 7:17:55 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [0].pdf	2023/08/24, 7:17:55 AM	George Awad	-
Kingswood Tafe_LLP ITPs 16 MAY 23.pdf	2023/08/24, 7:17:54 AM	George Awad	-
MSSB SN installation ITP.pdf	2023/08/24, 7:17:55 AM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *
Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:17:57 am

16

Dunrite Accepts walls are ready for sheet *
Hold Point

Hills Pan
Thursday 24 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:17:58 am

17 North Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:17:56 am

18 East Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:17:56 am

Photos (1)



Captured by: **George Awad ADCO
CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 7:17:54 AM**

19 South Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:17:56 am

20 West Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:17:56 am

Photos (1)



Captured by: **George Awad ADCO
CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 7:17:47 AM**

Name

Signature

Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

96 - Learning Type A - Pre Sheet-ITP

Details

Project

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

Organization

ADCO CONSTRUCTIONS PTY LIMITED

Location

TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.03

LEARNING TYPE A

Status

Closed

Due Date

Created by

George Awad on Wednesday 01 March, 2023, 9:40:44 am

Modified by

George Awad on Thursday 24 August, 2023, 8:18:31 am

Downloaded

Thursday 24 August, 2023, 8:18:48 am

Template

NSW TAFE IATC – Pre Sheet ITP

Description

Date: Room / Location:

Progress

100%

Question

Response

1

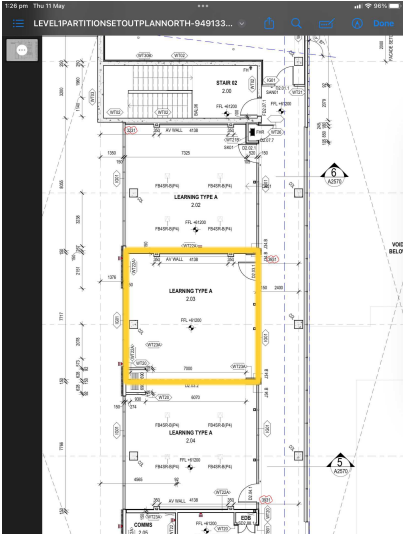
Mark up plan of walls to be sheeted. *

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:15:56 pm

Hold Point

Photos (1)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/05/11, 4:15:56 PM

2

Utech – Is the power installed per drawings?

Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:26:54 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Level 1 South Rooms ITP.pdf	2023/08/24, 7:26:50 AM	George Awad	–
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/08/24, 7:26:47 AM	George Awad	–

3

Utech – Are the communications and security cabling installed as per the drawings? Attach

evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:26:53 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Level 1 South Rooms ITP.pdf	2023/08/24, 7:26:51 AM	George Awad	–
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/08/24, 7:26:47 AM	George Awad	–

4

Utech – Electrical services roughed in according to approved room layout drawings. *

Hold Point

George Joannou
Thursday 24 August, 2023George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:26:54 am

5

Foran – Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:26:53 am

6

Foran – Is the drainage installed as per drawings? Attached evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:26:53 am

96 - Learning Type A - Pre Sheet-ITP

7 Foran – Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Thursday 24 August, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:26:54 am
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Thursday 24 August, 2023  George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:26:54 am
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:26:53 am
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:26:53 am
11 ZipClad – Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:26:53 am
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:26:53 am
Photos (1)	



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 7:26:49 AM**

13

Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:26:53 am

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:26:53 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [0].pdf	2023/08/24, 7:26:51 AM	George Awad	-
MSSB NN installation itp.pdf	2023/08/24, 7:26:50 AM	George Awad	-
Kingswood Tafe_LL P ITPs 16 MAY 23.pdf	2023/08/24, 7:26:47 AM	George Awad	-
MSSB SN installation ITP.pdf	2023/08/24, 7:26:50 AM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:26:52 am

16

Dunrite Accepts walls are ready for sheet *

Hold Point

Hills Pan
Thursday 24 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 7:26:55 am

96 - Learning Type A - Pre Sheet-ITP

17 North Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:18:08 am

18 East Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:18:07 am

19 South Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:18:07 am

20 West Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:18:06 am

Photos (2)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 8:18:04 AM**



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 8:18:00 AM**

Name

Signature

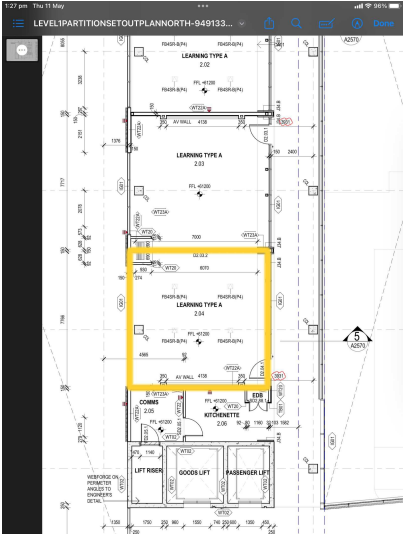
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

97 - Learning Type A - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.04
LEARNING TYPE A	
Status	Closed
Due Date	
Created by	George Awad on Wednesday 01 March, 2023, 9:41:16 am
Modified by	George Awad on Thursday 24 August, 2023, 8:32:38 am
Downloaded	Thursday 24 August, 2023, 8:32:46 am
Template	NSW TAFE IATC – Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:16:22 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:16:22 PM	

2

Utech – Is the power installed per drawings?

Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:32:23 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Level 1 South Rooms ITP.pdf	2023/08/24, 8:32:19 AM	George Awad	–
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/08/24, 8:32:06 AM	George Awad	–

3

Utech – Are the communications and security cabling installed as per the drawings? Attach

evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:32:23 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/08/24, 8:32:19 AM	George Awad	–
Level 1 South Rooms ITP.pdf	2023/08/24, 8:32:16 AM	George Awad	–

4

Utech – Electrical services roughed in according to approved room layout drawings. *

Hold Point


George Joannou
Thursday 24 August, 2023George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:32:23 am

5

Foran – Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:32:22 am

6

Foran – Is the drainage installed as per drawings? Attached evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:32:22 am

97 - Learning Type A - Pre Sheet-ITP

7 Foran – Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Thursday 24 August, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 8:32:23 am
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Thursday 24 August, 2023  George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 8:32:24 am
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 8:32:22 am
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 8:32:22 am
11 ZipClad – Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 8:32:22 am
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 8:32:22 am
Photos (1)	



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 8:32:13 AM**

13

Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:32:22 am

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:32:22 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [0].pdf	2023/08/24, 8:32:19 AM	George Awad	-
MSSB SN installation ITP.pdf	2023/08/24, 8:32:20 AM	George Awad	-
MSSB NN installation itp.pdf	2023/08/24, 8:32:20 AM	George Awad	-
Kingswood Tafe_LL P ITPs 16 MAY 23.pdf	2023/08/24, 8:32:19 AM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:32:22 am

16

Dunrite Accepts walls are ready for sheet *

Hold Point

Hills Pan
Thursday 24 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:32:25 am

17 North Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:32:22 am

18 East Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:32:21 am

Photos (4)



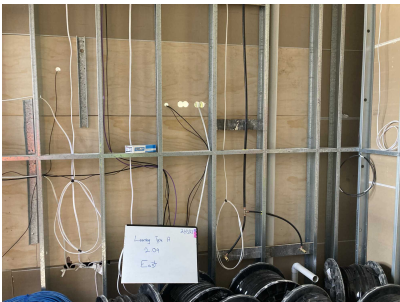
Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 8:32:18 AM**



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 8:32:11 AM**



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 8:32:10 AM**



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 8:32:15 AM**

19 South Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:32:25 am

20 West Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:32:21 am

Name

Signature

Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

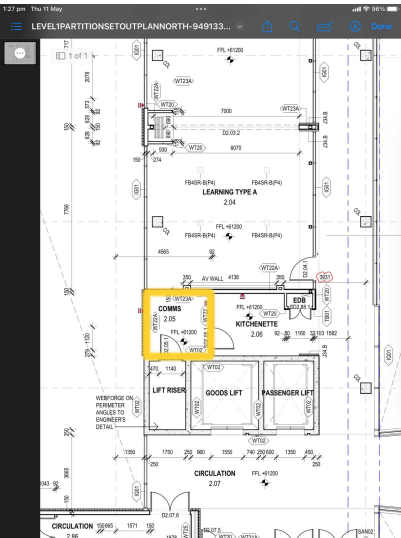
TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

98 - COMMS - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.05 COMMS
Status	Closed
Due Date	
Created by	George Awad on Wednesday 01 March, 2023, 9:41:45 am
Modified by	George Awad on Thursday 24 August, 2023, 8:38:50 am
Downloaded	Thursday 24 August, 2023, 8:38:53 am
Template	NSW TAFE IATC – Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. *	Yes
Hold Point	George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:17:16 pm

Photos (1)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/05/11, 4:17:16 PM

2

Utech – Is the power installed per drawings?

Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:38:41 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Level 1 South Rooms ITP.pdf	2023/08/24, 8:38:37 AM	George Awad	–
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/08/24, 8:38:24 AM	George Awad	–

3

Utech – Are the communications and security cabling installed as per the drawings? Attach

evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:38:41 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Level 1 South Rooms ITP.pdf	2023/08/24, 8:38:37 AM	George Awad	–
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/08/24, 8:38:33 AM	George Awad	–

4

Utech – Electrical services roughed in according to approved room layout drawings. *

Hold Point


George Joannou
Thursday 24 August, 2023George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:38:41 am

5

Foran – Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:38:40 am

6

Foran – Is the drainage installed as per drawings? Attached evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:38:40 am

98 - COMMS - Pre Sheet-ITP

7 Foran – Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Thursday 24 August, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 8:38:41 am
8 AV service roughened in according to approved room layout drawing. * Hold Point	N/A Thursday 24 August, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 8:38:41 am
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 8:38:40 am
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 8:38:40 am
11 ZipClad – Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 8:38:40 am
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 8:38:40 am
Photos (1)	



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 8:38:26 AM**

13

Is the acoustic insulation installed as per specification/drawings? Attache evidence *
Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:38:40 am

14

Are the mechanical works installed as per drawings? Attach evidence *
Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:38:39 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB SN installation ITP.pdf	2023/08/24, 8:38:38 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [0].pdf	2023/08/24, 8:38:37 AM	George Awad	-
Kingswood Tafe_LLP ITPs 16 MAY 23.pdf	2023/08/24, 8:38:38 AM	George Awad	-
MSSB NN installation itp.pdf	2023/08/24, 8:38:38 AM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *
Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:38:39 am

16

Dunrite Accepts walls are ready for sheet *
Hold Point

Hills Pan
Thursday 24 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:38:41 am

17 North Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:38:39 am

18 East Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:38:39 am

19 South Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:38:39 am

Photos (1)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/08/24, 8:38:28 AM

20 West Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 8:38:39 am

Photos (3)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/08/24, 8:38:36 AM



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/08/24, 8:38:33 AM



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/08/24, 8:38:31 AM

Name

Signature

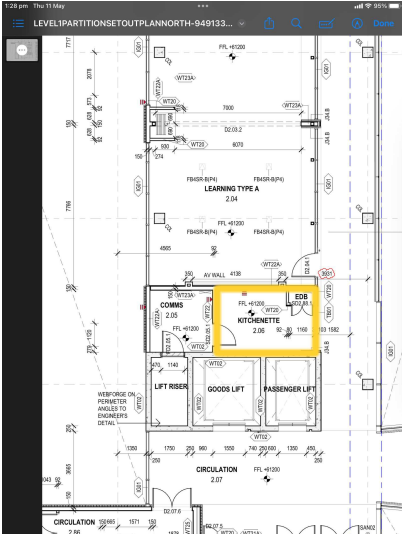
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

99 - Kitchenette - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.06 KITCHENETTE
Status	Closed
Due Date	
Created by	George Awad on Wednesday 01 March, 2023, 9:42:41 am
Modified by	George Awad on Monday 28 August, 2023, 3:01:21 pm
Downloaded	Monday 28 August, 2023, 3:01:24 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:17:44 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:17:44 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:10 pm

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Level 1 South Rooms ITP.pdf	2023/08/28, 3:01:05 PM	George Awad	-
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/08/28, 3:01:05 PM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:10 pm

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/08/28, 3:01:06 PM	George Awad	-
Level 1 South Rooms ITP.pdf	2023/08/28, 3:01:06 PM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Monday 28 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:10 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:09 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 3:00:52 PM

6

Foran - Is the drainage installed as per drawings?

Attached evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:09 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 3:00:54 PM

7

Foran - Hydraulic services roughed in according to approved room layout drawings. *

Hold Point

Matt Foran

Monday 28 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:10 pm

99 - Kitchenette - Pre Sheet-ITP

8

AV service roughened in according to approved room layout drawing. *

Hold Point

N/A

Monday 28 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:10 pm

9

Is fire stopping applied as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:09 pm

10

Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:09 pm

11 ZipClad - Water Test Conducted on Facade *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:09 pm

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:09 pm

Photos (1)



Captured by: George Awad ADCO

99 - Kitchenette - Pre Sheet-ITP

CONSTRUCTIONS PTY LIMITED

Date: 2023/08/28, 3:00:56 PM

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:09 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:09 pm

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB SN installation ITP.pdf	2023/08/28, 3:01:07 PM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/08/28, 3:01:06 PM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/08/28, 3:01:07 PM	George Awad	-
MSSB NN installation itp.pdf	2023/08/28, 3:01:07 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:09 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan
Monday 28 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:10 pm

17 North Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:08 pm

18 East Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:08 pm

19 South Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:08 pm

20 West Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 3:01:08 pm

Photos (4)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 3:01:00 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 3:00:58 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 3:01:02 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 3:01:05 PM

Name

Signature

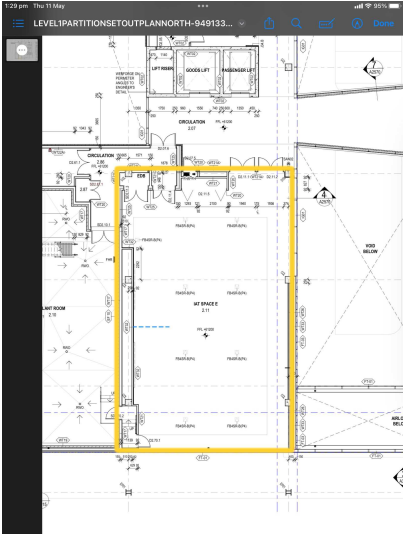
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

101 - IAT Space E - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.11 IAT SPACE E
Status	Closed
Due Date	
Created by	George Awad on Wednesday 01 March, 2023, 9:52:19 am
Modified by	George Awad on Monday 28 August, 2023, 4:25:18 pm
Downloaded	Monday 28 August, 2023, 4:25:46 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:18:51 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:18:50 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:12:45 pm

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/08/28, 4:12:37 PM	George Awad	-
Level 1 South Rooms ITP.pdf	2023/08/28, 4:12:35 PM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:12:45 pm

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Level 1 South Rooms ITP.pdf	2023/08/28, 4:12:43 PM	George Awad	-
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/08/28, 4:12:43 PM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Monday 28 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:12:45 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:12:45 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:12:37 PM

6

Foran - Is the drainage installed as per drawings?
Attached evidence *
Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:12:44 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:12:43 PM

7

Foran - Hydraulic services roughed in according to approved room layout drawings. *
Hold Point

Matt Foran
Monday 28 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:12:45 pm

8

AV service roughened in according to approved room layout drawing. *
Hold Point

As Per ITP
Monday 28 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:12:45 pm

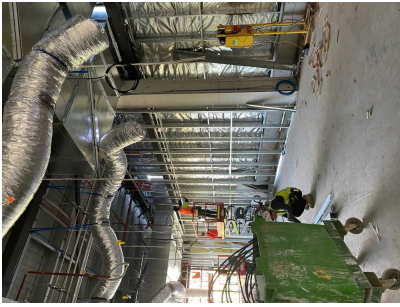
9

Is fire stopping applied as per drawings? Attach evidence *
Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:12:44 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/28, 4:12:35 PM**

10

Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:12:44 pm

11 ZipClad - Water Test Conducted on Facade *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:12:44 pm

12

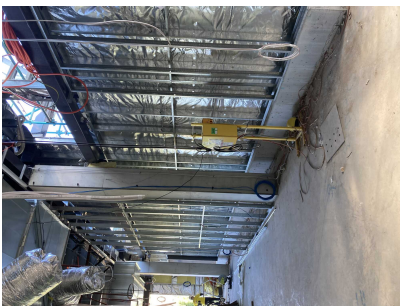
Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:12:44 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/28, 4:12:39 PM**

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:12:44 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:12:41 PM

14

Are the mechanical works installed as per drawings?
Attach evidence *
Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:25:06 pm

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/08/28, 4:25:01 PM	George Awad	-
MSSB NN installation itp.pdf	2023/08/28, 4:25:04 PM	George Awad	-
Kingswood Tafe_LLP ITPs 16 MAY 23.pdf	2023/08/28, 4:25:04 PM	George Awad	-
MSSB SN installation ITP.pdf	2023/08/28, 4:25:05 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *
Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:25:06 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point

Hills Pan
Monday 28 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:25:06 pm

17 North Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:25:06 pm

Photos (3)

101 - IAT Space E - Pre Sheet-ITP



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:24:48 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:24:53 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:24:55 PM

18 East Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:25:05 pm

19 South Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:25:05 pm

Photos (2)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:24:50 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:24:47 PM

20 West Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:25:05 pm

Photos (4)

101 - IAT Space E - Pre Sheet-ITP



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:24:57 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:24:59 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:25:01 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:25:04 PM

Name

Signature

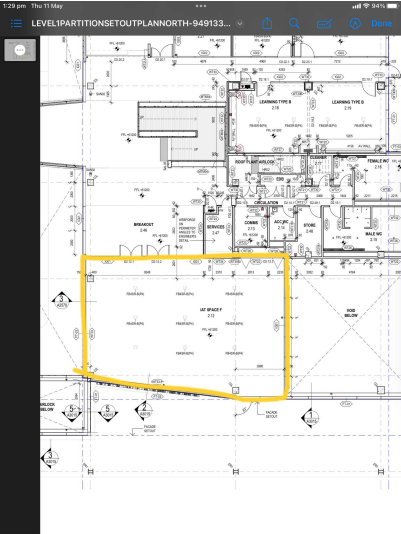
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

102 - IAT Space F - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.12 IAT SPACE F
Status	Closed
Due Date	
Created by	George Awad on Wednesday 01 March, 2023, 9:53:48 am
Modified by	George Awad on Monday 28 August, 2023, 4:41:17 pm
Downloaded	Monday 28 August, 2023, 4:41:22 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:19:31 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:19:30 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 10:53:51 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 10:53:49 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 10:53:51 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 10:53:45 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 10:53:51 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 10:53:47 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 10:53:48 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 10:53:45 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:43:45 pm

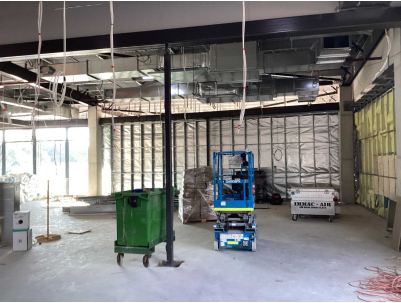
5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 26 May, 2023, 2:52:02 pm

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 26 May, 2023, 2:52:02 pm
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Friday 26 May, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 26 May, 2023, 2:52:02 pm
8 AV service roughened in according to approved room layout drawing. * Hold Point	N/A Monday 28 August, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:41:05 pm
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:41:05 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/08/28, 4:40:55 PM	
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:41:05 pm

11 ZipClad - Water Test Conducted on Facade *

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:41:05 pm

Hold Point

12

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:41:05 pm

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/28, 4:40:57 PM

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:41:05 pm

Hold Point

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/28, 4:40:58 PM

14

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:41:05 pm

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Photos (0)

Files (4)

102 - IAT Space F - Pre Sheet-ITP

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/08/28, 4:41:03 PM	George Awad	-
MSSB SN installation ITP.pdf	2023/08/28, 4:41:03 PM	George Awad	-
MSSB NN installation itp.pdf	2023/08/28, 4:41:03 PM	George Awad	-
Kingswood Tafe_LL P ITPs 16 MAY 23.pdf	2023/08/28, 4:41:02 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:41:04 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan
Monday 28 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:41:06 pm

17 North Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:41:04 pm

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/28, 4:40:59 PM

18 East Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:41:04 pm

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED

Date: 2023/08/28, 4:41:01 PM

19 South Image * Hold Point

Tuesday 02 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:41:06 pm

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/28, 4:41:02 PM

20 West Image * Hold Point

Tuesday 09 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:41:04 pm

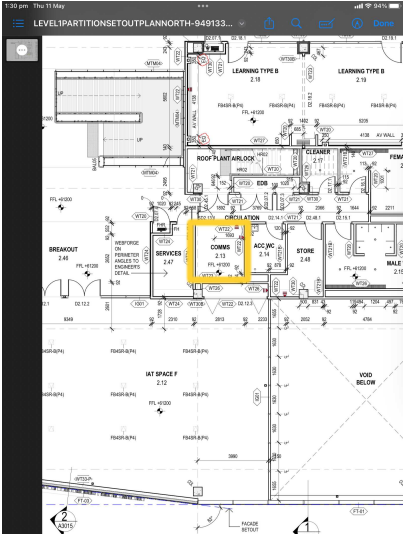
Name _____ Signature _____ Date _____

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

104 - COMMS - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.13 COMMS
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:05:09 am
Modified by	George Awad on Monday 28 August, 2023, 4:42:01 pm
Downloaded	Monday 28 August, 2023, 4:42:12 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:20:03 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:20:03 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 10:54:43 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 10:54:31 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 10:54:33 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 10:54:42 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 10:54:43 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 10:54:32 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 10:54:36 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 10:54:34 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:44:27 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:50:24 pm

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:50:24 pm
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Monday 10 July, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:50:25 pm
8 AV service roughened in according to approved room layout drawing. * Hold Point	N/A Monday 10 July, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:50:25 pm
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:50:24 pm
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:50:24 pm
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:50:24 pm
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:50:24 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/07/10, 3:50:15 PM**

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:50:24 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:50:24 pm

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB SN installation ITP.pdf	2023/07/10, 3:50:22 PM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/07/10, 3:50:20 PM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/07/10, 3:50:22 PM	George Awad	-
MSSB NN installation itp.pdf	2023/07/10, 3:50:22 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:50:23 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point

Hills Pan
Monday 10 July, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:50:25 pm

17 North Image * Hold Point

Tuesday 02 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:50:23 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 3:50:16 PM

18 East Image * Hold Point

Tuesday 02 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:50:23 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 3:50:13 PM

19 South Image * Hold Point

Tuesday 02 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 3:50:23 pm

Photos (3)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 3:50:19 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 3:50:21 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 3:50:18 PM

20 West Image * Hold Point

Tuesday 02 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10
July, 2023, 3:50:23 pm

Name

Signature

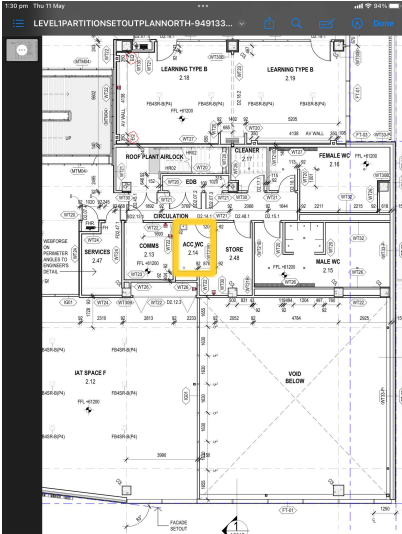
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

105 - ACC WC - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.14 ACC WC
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:08:22 am
Modified by	George Awad on Monday 10 July, 2023, 5:13:51 pm
Downloaded	Monday 10 July, 2023, 5:13:55 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:21:23 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:21:23 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 10:55:17 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720 LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 10:55:15 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 10:55:10 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 10:55:13 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 10:55:17 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 10:55:17 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 10:55:11 AM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 10:55:11 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:45:02 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:22 pm

Photos (2)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 4:05:59 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 4:05:51 PM

6

Foran - Is the drainage installed as per drawings?

Attached evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:22 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 4:06:03 PM

7

Foran - Hydraulic services roughed in according to approved room layout drawings. *

Hold Point

Matt Foran
Monday 10 July, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:23 pm

8

AV service roughened in according to approved room layout drawing. *

Hold Point

N/A
Monday 10 July, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:23 pm

105 - ACC WC - Pre Sheet-ITP

9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:22 pm																
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:22 pm																
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:22 pm																
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:22 pm																
13 Is the acoustic insulation installed as per specification/drawings? Attache evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:22 pm																
14 Are the mechanical works installed as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:22 pm																
Photos (0) Files (3) <table border="1"> <thead> <tr> <th>Filename</th> <th>Date</th> <th>Attached by</th> <th>Comments</th> </tr> </thead> <tbody> <tr> <td>MSSB SN installation ITP.pdf</td> <td>2023/07/10, 4:06:14 PM</td> <td>George Awad</td> <td>-</td> </tr> <tr> <td>MSSB NN installation itp.pdf</td> <td>2023/07/10, 4:06:16 PM</td> <td>George Awad</td> <td>-</td> </tr> <tr> <td>Kingswood Tafe LLP ITPs 16 MAY 23.pdf</td> <td>2023/07/10, 4:06:16 PM</td> <td>George Awad</td> <td>-</td> </tr> </tbody> </table>		Filename	Date	Attached by	Comments	MSSB SN installation ITP.pdf	2023/07/10, 4:06:14 PM	George Awad	-	MSSB NN installation itp.pdf	2023/07/10, 4:06:16 PM	George Awad	-	Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/07/10, 4:06:16 PM	George Awad	-
Filename	Date	Attached by	Comments														
MSSB SN installation ITP.pdf	2023/07/10, 4:06:14 PM	George Awad	-														
MSSB NN installation itp.pdf	2023/07/10, 4:06:16 PM	George Awad	-														
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/07/10, 4:06:16 PM	George Awad	-														

15

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:21 pm

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

16

Dunrite Accepts walls are ready for sheet *



Hills Pan
Monday 10 July, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:23 pm

Hold Point

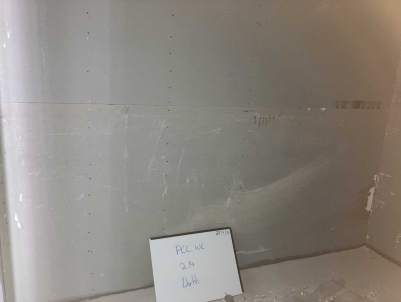
17

North Image * Hold Point

Tuesday 02 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:21 pm

Photos (2)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 4:05:57 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 4:06:01 PM

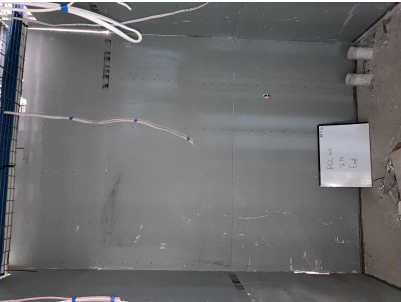
18

East Image * Hold Point

Tuesday 02 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:21 pm

Photos (2)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 4:06:07 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 4:06:05 PM

19

South Image * Hold Point

Tuesday 02 May, 2023

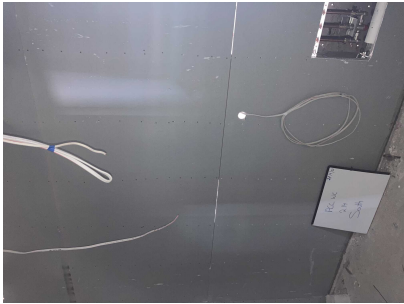
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:21 pm

Photos (2)

105 - ACC WC - Pre Sheet-ITP



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 4:06:09 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 4:06:12 PM

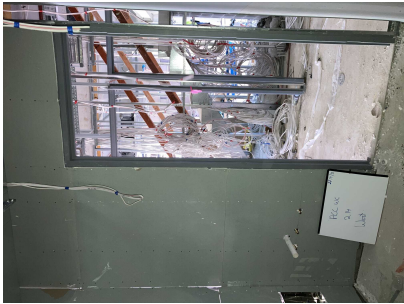
20 West Image * Hold Point

Tuesday 02 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 4:06:21 pm

Photos (2)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 4:06:14 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 4:06:16 PM

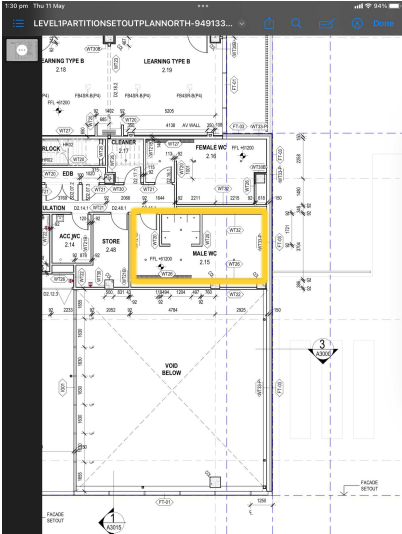
Name _____ Signature _____ Date _____

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

106 - Male WC - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.15 MALE WC
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:09:19 am
Modified by	George Awad on Monday 28 August, 2023, 4:49:27 pm
Downloaded	Monday 28 August, 2023, 4:49:31 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:22:01 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:22:01 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 10:55:55 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 10:55:47 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 10:55:46 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 10:55:55 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 10:55:55 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 10:55:49 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 10:55:48 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 10:55:47 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:45:41 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:58 pm

Photos (0)

Files (1)

Filename	Date	Attached by	Comments
level 1 amenities.pdf	2023/08/28, 4:48:49 PM	George Awad	-

106 - Male WC - Pre Sheet-ITP

6

Foran - Is the drainage installed as per drawings?

Attached evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:58 pm

Photos (0)

Files (1)

Filename	Date	Attached by	Comments
level 1 amenities.pdf	2023/08/28, 4:48:49 PM	George Awad	-

7

Foran - Hydraulic services roughed in according to approved room layout drawings. *

Hold Point

As Per Above ITPs
Monday 28 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:59 pm

8

AV service roughened in according to approved room layout drawing. *

Hold Point

N/A
Monday 28 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:59 pm

9

Is fire stopping applied as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:58 pm

10

Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:58 pm

11 ZipClad - Water Test Conducted on Facade *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:58 pm

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:58 pm

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/28, 4:48:18 PM

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:58 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:59 pm

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:57 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point

Hills Pan
Monday 28 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:59 pm

17 North Image * Hold Point

Monday 24 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:57 pm

Photos (3)

106 - Male WC - Pre Sheet-ITP



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:48:22 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:48:34 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:48:25 PM

18 East Image * Hold Point

Monday 24 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:57 pm

Photos (3)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:48:20 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:48:28 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:48:30 PM

19 South Image * Hold Point

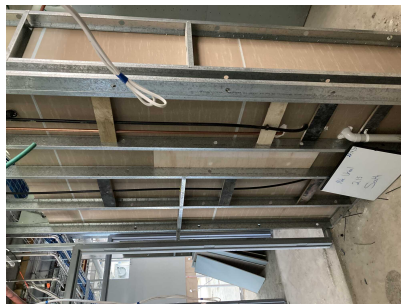
Monday 24 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:57 pm

Photos (3)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:48:32 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:48:36 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:48:38 PM

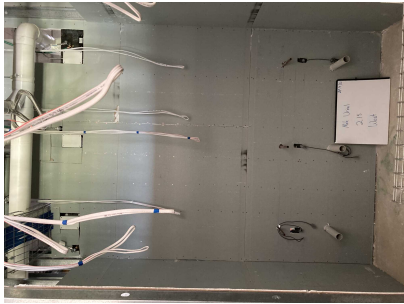
20 West Image * Hold Point

Monday 24 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:48:57 pm

Photos (5)

106 - Male WC - Pre Sheet-ITP



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:48:40 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:48:42 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:48:44 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:48:46 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:48:48 PM

Name

Signature

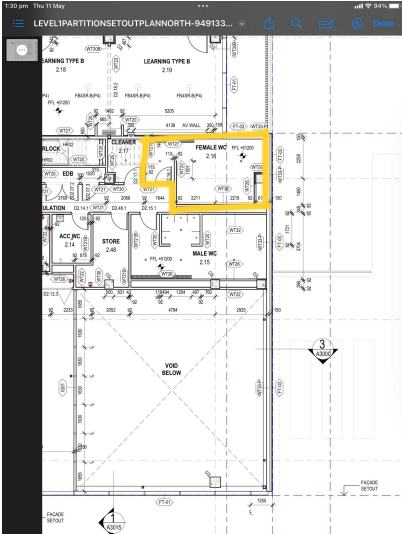
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

107 - Female WC - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.16 FEMALE WC
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:10:17 am
Modified by	George Awad on Monday 28 August, 2023, 4:56:31 pm
Downloaded	Monday 28 August, 2023, 4:57:20 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:23:16 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:23:16 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 10:58:48 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 10:58:48 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 10:58:47 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 10:58:43 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 10:58:48 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 10:58:44 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 10:58:46 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 10:58:47 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:46:21 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:54 pm

Photos (0)

Files (1)

Filename	Date	Attached by	Comments
level 1 amenities.pdf	2023/08/28, 4:55:46 PM	George Awad	-

6

Foran - Is the drainage installed as per drawings?

Attached evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:54 pm

Photos (0)

Files (1)

Filename	Date	Attached by	Comments
level 1 amenities.pdf	2023/08/28, 4:55:48 PM	George Awad	-

7

Foran - Hydraulic services roughed in according to approved room layout drawings. *

Hold Point

As Per ITP

Monday 28 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:54 pm

8

AV service roughened in according to approved room layout drawing. *

Hold Point

N/A

Monday 28 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:54 pm

9

Is fire stopping applied as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:54 pm

10

Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:54 pm

11 ZipClad - Water Test Conducted on Facade *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:54 pm

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:54 pm

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/28, 4:55:35 PM

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:53 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:53 pm

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:53 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point

Hills Pan
Monday 28 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:55 pm

17 North Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:53 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:55:37 PM

18 East Image * Hold Point

Thursday 27 April, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:53 pm

Photos (2)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:55:41 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:55:39 PM

19 South Image * Hold Point

Thursday 27 April, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:53 pm

Photos (2)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:55:45 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:55:43 PM

20 West Image * Hold Point

Thursday 27 April, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 28 August, 2023, 4:55:53 pm

Photos (2)

107 - Female WC - Pre Sheet-ITP



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:55:48 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/08/28, 4:55:51 PM

Name

Signature

Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

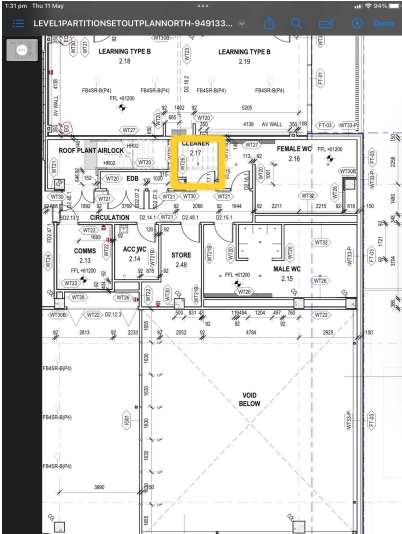
108 - Cleaner - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.17 CLEANER
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:11:05 am
Modified by	George Awad on Wednesday 30 August, 2023, 11:30:51 am
Downloaded	Wednesday 30 August, 2023, 11:30:54 am
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. *	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:24:20 pm

Hold Point

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/05/11, 4:24:20 PM

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 10:59:26 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 10:59:21 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 10:59:26 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 10:59:25 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 10:59:26 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 10:59:22 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 10:59:24 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 10:59:20 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:47:04 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:35 am

Photos (0)

Files (1)

Filename	Date	Attached by	Comments
level 1 amenities.pdf	2023/08/30, 11:30:33 AM	George Awad	-

6

Foran - Is the drainage installed as per drawings?

Attached evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:35 am

Photos (0)

Files (1)

Filename	Date	Attached by	Comments
level 1 amenities.pdf	2023/08/30, 11:30:28 AM	George Awad	-

7

Foran - Hydraulic services roughed in according to approved room layout drawings. *

Hold Point

Matt Foran

Wednesday 30 August, 2023,

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:35 am

8

AV service roughened in according to approved room layout drawing. *

Hold Point

N/A

Wednesday 30 August, 2023,

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:36 am

9

Is fire stopping applied as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:35 am

10

Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:35 am

11 ZipClad - Water Test Conducted on Facade *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:35 am

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:35 am

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/30, 11:30:19 AM

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:34 am

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:36 am

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:34 am

16 Dunrite Accepts walls are ready for sheet *

Hold Point

 Hills Pan
Wednesday 30 August, 2023,
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:36 am

17 North Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:34 am

Photos (2)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/30, 11:30:23 AM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/30, 11:30:25 AM

18 East Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:34 am

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/30, 11:30:33 AM

19 South Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:34 am

Photos (1)



Captured by: George Awad ADCO

CONSTRUCTIONS PTY LIMITED

Date: 2023/08/30, 11:30:28 AM

20 West Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:30:34 am

Photos (1)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED

Date: 2023/08/30, 11:30:31 AM

Name

Signature

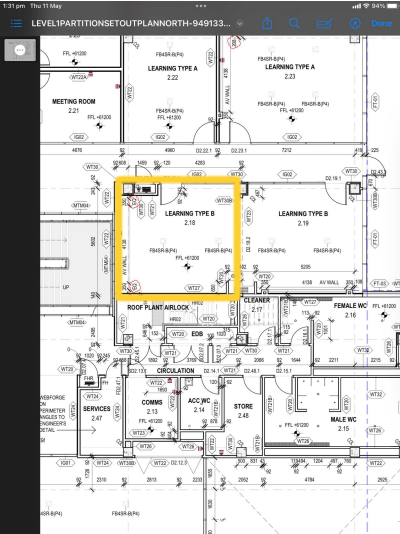
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

109 - Learning Type B - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.18 LEARNING TYPE B
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:12:01 am
Modified by	George Awad on Wednesday 30 August, 2023, 11:38:50 am
Downloaded	Wednesday 30 August, 2023, 11:38:56 am
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:25:18 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:25:18 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:00:06 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 11:00:05 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:00:00 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:00:06 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:00:06 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:00:02 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:00:04 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:00:02 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:48:28 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:36 am

109 - Learning Type B - Pre Sheet-ITP

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:36 am
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Wednesday 30 August, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:36 am
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Wednesday 30 August, 2023,  George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:36 am
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:36 am
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:35 am
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:35 am
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:35 am

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/30, 11:38:20 AM**

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:35 am

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:35 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/08/30, 11:38:32 AM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/08/30, 11:38:31 AM	George Awad	-
MSSB SN installation ITP.pdf	2023/08/30, 11:38:32 AM	George Awad	-
MSSB NN installation itp.pdf	2023/08/30, 11:38:33 AM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:35 am

16 Dunrite Accepts walls are ready for sheet *

Hold Point

Hills Pan
Wednesday 30 August, 2023,

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:37 am

17 North Image * Hold Point

Wednesday 24 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:35 am

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/30, 11:38:25 AM

18 East Image * Hold Point

Wednesday 24 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:35 am

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/30, 11:38:24 AM

19 South Image * Hold Point

Wednesday 24 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:34 am

Photos (3)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/30, 11:38:30 AM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/30, 11:38:27 AM

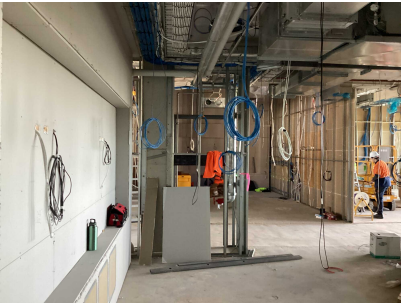


Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/30, 11:38:22 AM

20 West Image * Hold Point

Wednesday 24 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:38:34 am

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/30, 11:38:32 AM**

Name

Signature

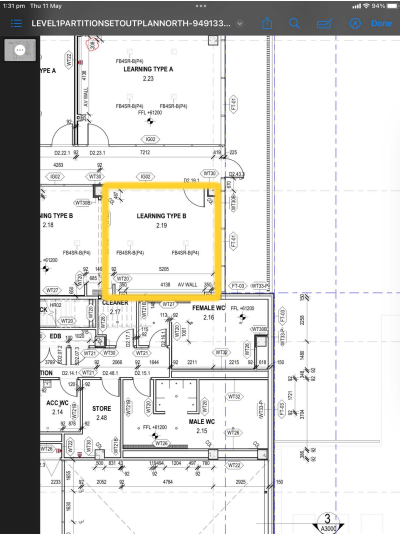
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

110 - Learning Type B - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.19 LEARNING TYPE B
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:13:18 am
Modified by	George Awad on Wednesday 30 August, 2023, 11:42:40 am
Downloaded	Wednesday 30 August, 2023, 11:45:06 am
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:25:45 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:25:45 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:00:46 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:00:41 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:00:45 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:00:43 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:00:46 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:00:42 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:00:41 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:00:45 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:48:58 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:31 am

110 - Learning Type B - Pre Sheet-ITP

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:31 am
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Wednesday 30 August, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:31 am
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Wednesday 30 August, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:31 am
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:30 am
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:30 am
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:30 am
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:30 am

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:30 am

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:30 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/08/30, 11:42:28 AM	George Awad	-
MSSB NN installation itp.pdf	2023/08/30, 11:42:26 AM	George Awad	-
MSSB SN installation ITP.pdf	2023/08/30, 11:42:26 AM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/08/30, 11:42:25 AM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:31 am

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Wednesday 30 August, 2023,

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:31 am

17 North Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:30 am

18 East Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:29 am

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/30, 11:42:28 AM**

19 South Image * Hold Point

Wednesday 24 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:29 am

20 West Image * Hold Point

Wednesday 24 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:42:29 am

Name

Signature

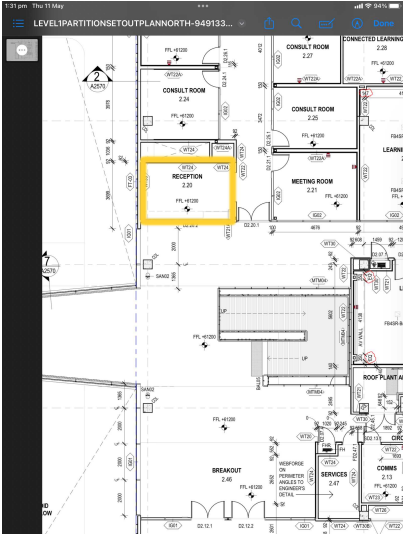
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

111 - Reception - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.20 RECEPTION
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:13:51 am
Modified by	George Awad on Wednesday 30 August, 2023, 11:56:52 am
Downloaded	Wednesday 30 August, 2023, 11:57:05 am
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:31:05 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:31:04 PM	

111 - Reception - Pre Sheet-ITP

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:01:24 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 11:01:23 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:01:19 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:01:23 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:01:24 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 11:01:24 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:01:20 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:01:21 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:49:34 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:41 am

111 - Reception - Pre Sheet-ITP

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:41 am
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Wednesday 30 August, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:41 am
8 AV service roughened in according to approved room layout drawing. * Hold Point	N/A Wednesday 30 August, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:42 am
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:41 am
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:41 am
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:41 am
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:41 am

111 - Reception - Pre Sheet-ITP

13	Is the acoustic insulation installed as per specification/drawings? Attache evidence *	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:40 am
	Hold Point	
14	Are the mechanical works installed as per drawings? Attach evidence *	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:40 am
	Hold Point	
15	Door Frames installed in plumb and have correct allowance for finish *	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:42 am
	Hold Point	
16	Dunrite Accepts walls are ready for sheet *	 Hills Pan Wednesday 30 August, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:42 am
	Hold Point	
17	North Image * Hold Point	Wednesday 19 April, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:40 am
18	East Image * Hold Point	Wednesday 19 April, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:40 am
19	South Image * Hold Point	Wednesday 19 April, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:40 am
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/08/30, 11:56:35 AM		

20 West Image * Hold Point

Wednesday 19 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 30 August, 2023, 11:56:40 am

Photos (1)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/08/30, 11:56:33 AM

Name

Signature

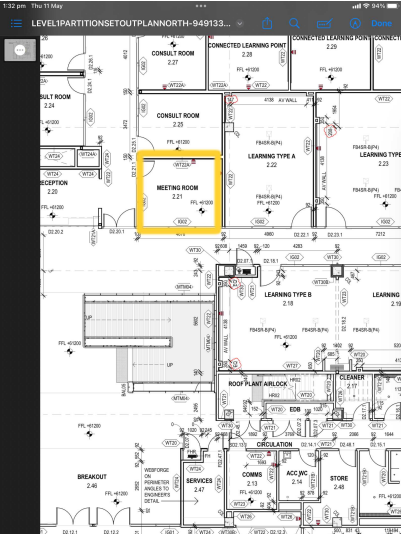
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

112 - Meeting Room - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.21 MEETING ROOM
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:14:40 am
Modified by	George Awad on Monday 04 September, 2023, 10:21:47 am
Downloaded	Monday 04 September, 2023, 10:21:51 am
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:31:45 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:31:45 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:02:07 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 11:02:03 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:01:58 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:02:00 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:02:07 am

Photos (0)


Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:02:00 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:02:07 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:01:59 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:49:59 pm

5


Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:33 am

112 - Meeting Room - Pre Sheet-ITP

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:33 am
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Monday 04 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:33 am
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Monday 04 September, 2023,  George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:33 am
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:33 am
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:33 am
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:32 am

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:32 am

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/04, 10:19:26 AM

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:32 am

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:32 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB SN installation ITP.pdf	2023/09/04, 10:19:28 AM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/04, 10:19:25 AM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/04, 10:19:28 AM	George Awad	-
MSSB NN installation itp.pdf	2023/09/04, 10:19:30 AM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:32 am

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Monday 04 September, 2023,

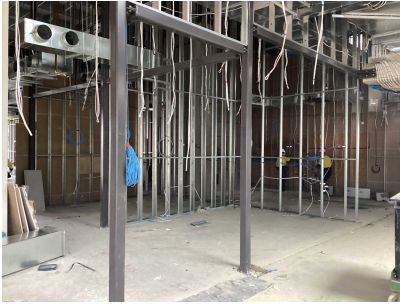
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:33 am

17 North Image * Hold Point

Tuesday 02 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:32 am

Photos (1)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/09/04, 10:19:28 AM

18 East Image * Hold Point

Tuesday 02 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:32 am

19 South Image * Hold Point

Tuesday 02 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:32 am

20 West Image * Hold Point

Tuesday 02 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:19:31 am

Photos (1)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/09/04, 10:19:30 AM

Name

Signature

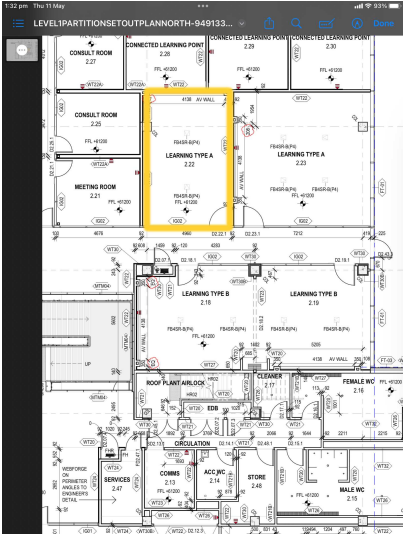
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

113 - Learning Type A - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.22 LEARNING TYPE A
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:16:05 am
Modified by	George Awad on Monday 04 September, 2023, 10:30:08 am
Downloaded	Monday 04 September, 2023, 10:30:14 am
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:33:39 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:33:39 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:03:17 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 11:03:15 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:03:11 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:03:13 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:03:17 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:03:14 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:03:12 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:03:17 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:50:17 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:30 am

113 - Learning Type A - Pre Sheet-ITP

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:30 am
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Monday 04 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:30 am
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Monday 04 September, 2023,  George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:30 am
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:30 am
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:29 am
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:29 am
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:29 am

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:29 am

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:29 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB NN installation itp.pdf	2023/09/04, 10:29:21 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/04, 10:29:27 AM	George Awad	-
MSSB SN installation ITP.pdf	2023/09/04, 10:29:26 AM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/04, 10:29:17 AM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:29 am

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Monday 04 September, 2023,

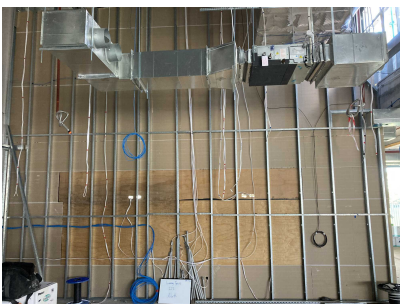
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:31 am

17 North Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:29 am

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED

Date: 2023/09/04, 10:29:21 AM

18 East Image * Hold Point

Thursday 27 April, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:28 am

19 South Image * Hold Point

Thursday 27 April, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:28 am

20 West Image * Hold Point

Thursday 27 April, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:29:28 am

Photos (2)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/04, 10:29:26 AM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/04, 10:29:23 AM

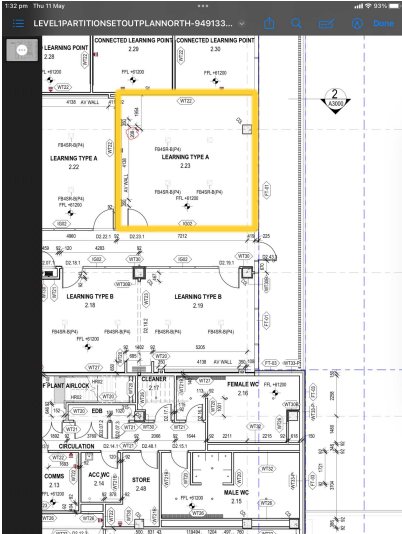
Name _____ Signature _____ Date _____

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

114 - Learning Type A - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.23 LEARNING TYPE A
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:16:45 am
Modified by	George Awad on Monday 04 September, 2023, 10:40:11 am
Downloaded	Monday 04 September, 2023, 10:40:16 am
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:34:27 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:34:27 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:04:09 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720 LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:04:04 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:04:08 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:04:04 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:04:08 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 11:04:08 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:04:02 AM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:04:06 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:50:53 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:52 am

114 - Learning Type A - Pre Sheet-ITP

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:52 am
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Monday 04 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:52 am
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Monday 04 September, 2023,  George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:52 am
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:51 am
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:51 am
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:51 am
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:51 am

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/09/04, 10:39:46 AM**

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:50 am

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:50 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB NN installation itp.pdf	2023/09/04, 10:39:46 AM	George Awad	-
MSSB SN installation ITP.pdf	2023/09/04, 10:39:47 AM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/04, 10:39:47 AM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/04, 10:39:33 AM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:50 am

16 Dunrite Accepts walls are ready for sheet *

Hold Point

Hills Pan
Monday 04 September, 2023,

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:53 am

17 North Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:50 am

18 East Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:49 am

19 South Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:49 am

Photos (2)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/09/04, 10:39:40 AM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/09/04, 10:39:32 AM

20 West Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:39:49 am

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/09/04, 10:39:35 AM

Name

Signature

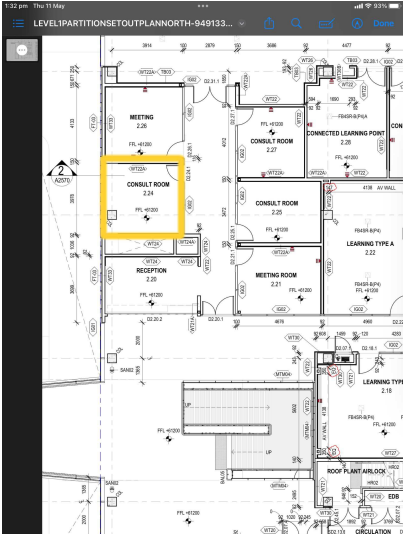
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

115 - Consult Room - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.24 CONSULT ROOM
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:18:47 am
Modified by	George Awad on Monday 04 September, 2023, 10:45:39 am
Downloaded	Monday 04 September, 2023, 10:45:43 am
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:35:46 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:35:46 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:04:58 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:04:53 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:04:57 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:04:51 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:04:58 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:04:51 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:04:53 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:04:55 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:51:13 pm

5


Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:26 am

115 - Consult Room - Pre Sheet-ITP

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:26 am
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Monday 04 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:26 am
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Monday 04 September, 2023,  George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:26 am
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:25 am
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:25 am
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:25 am

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:25 am

13

Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:25 am

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:25 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB NN installation itp.pdf	2023/09/04, 10:45:20 AM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/04, 10:45:20 AM	George Awad	-
MSSB SN installation ITP.pdf	2023/09/04, 10:45:20 AM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/04, 10:45:23 AM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:25 am

16

Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Monday 04 September, 2023,

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:26 am

17

North Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:24 am

18 East Image * Hold Point

Tuesday 09 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:24 am

19 South Image * Hold Point

Tuesday 09 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:24 am

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/04, 10:45:23 AM

20 West Image * Hold Point

Tuesday 09 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:45:24 am

Name

Signature

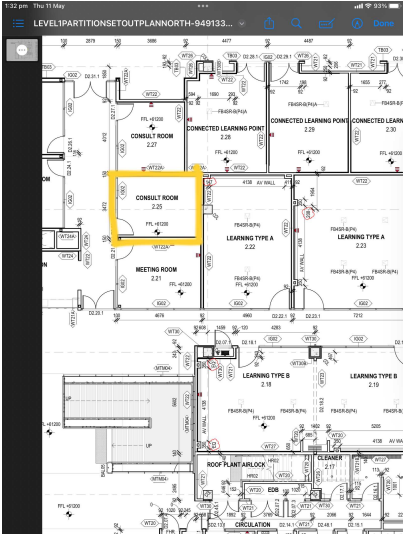
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

116 - Consult Room - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.25 CONSULT ROOM
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:19:16 am
Modified by	George Awad on Monday 04 September, 2023, 10:51:48 am
Downloaded	Monday 04 September, 2023, 10:52:04 am
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:36:33 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:36:33 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:05:41 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 11:05:39 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:05:34 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:05:34 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:05:40 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 11:05:40 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:05:35 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:05:33 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point

George Joannou
Wednesday 17 May, 2023



George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:52:01 pm


5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:30 am

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:29 am
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Monday 04 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:30 am
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Monday 04 September, 2023,  George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:30 am
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:29 am
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:29 am
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:29 am

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:29 am

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/04, 10:51:23 AM

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:28 am

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:28 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/04, 10:51:25 AM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/04, 10:51:18 AM	George Awad	-
MSSB NN installation itp.pdf	2023/09/04, 10:51:23 AM	George Awad	-
MSSB SN installation ITP.pdf	2023/09/04, 10:51:26 AM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:28 am

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Monday 04 September, 2023,

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:31 am

17 North Image * Hold Point

Wednesday 03 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:28 am

Photos (1)



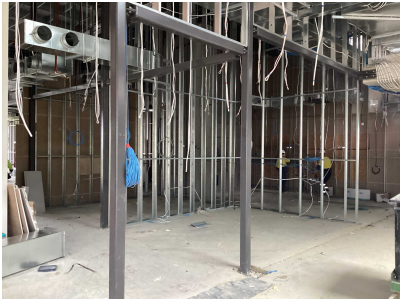
Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/09/04, 10:51:20 AM

18 East Image * Hold Point

Wednesday 03 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:28 am

Photos (1)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/09/04, 10:51:21 AM

19 South Image * Hold Point

Wednesday 03 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:27 am

Notes

Southern Elevation Is Glazing, No Pre-sheet Required

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:27 am

20 West Image * Hold Point

Wednesday 03 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 10:51:27 am

Photos (1)



Captured by: **George Awad ADCO**
CONSTRUCTIONS PTY LIMITED
Date: **2023/09/04, 10:51:25 AM**

Name

Signature

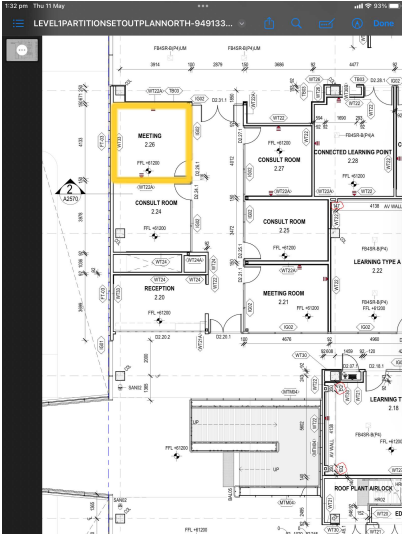
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

117 - Meeting - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.26 MEETING
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:20:12 am
Modified by	George Awad on Monday 04 September, 2023, 1:55:00 pm
Downloaded	Monday 04 September, 2023, 1:55:07 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:37:33 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:37:32 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:06:17 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:06:11 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:06:16 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:06:14 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:06:17 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:06:12 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:06:15 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:06:13 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:53:15 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:38 pm

117 - Meeting - Pre Sheet-ITP

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:38 pm
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Monday 04 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:38 pm
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Monday 04 September, 2023  George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:38 pm
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:38 pm
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:37 pm
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:37 pm
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:37 pm

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:37 pm

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/04, 1:54:30 PM

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:37 pm

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/04, 1:54:28 PM	George Awad	-
MSSB SN installation ITP.pdf	2023/09/04, 1:54:35 PM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/04, 1:54:34 PM	George Awad	-
MSSB NN installation itp.pdf	2023/09/04, 1:54:35 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:37 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point

Hills Pan
Monday 04 September, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:39 pm

17 North Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:37 pm

Notes

Northern elevation is glazing, no pre-sheet required.

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:37 pm

18 East Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:36 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/09/04, 1:54:29 PM

19 South Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:36 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/09/04, 1:54:34 PM

20 West Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 04 September, 2023, 1:54:36 pm

Photos (1)



Captured by: **George Awad ADCO**
CONSTRUCTIONS PTY LIMITED
Date: 2023/09/04, 1:54:32 PM

Name

Signature

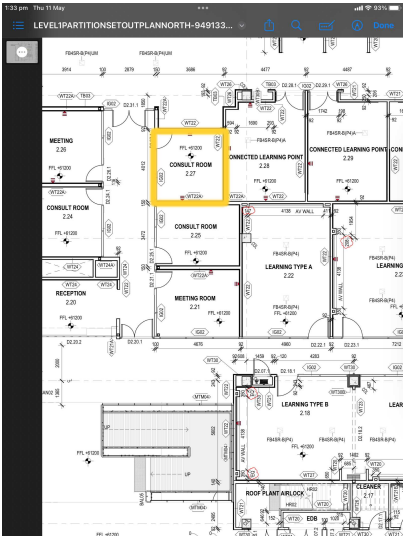
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

118 - Consult Room - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.27 CONSULT ROOM
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:20:42 am
Modified by	George Awad on Wednesday 06 September, 2023, 12:03:18 pm
Downloaded	Wednesday 06 September, 2023, 12:03:21 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:38:56 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:38:55 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:06:56 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 11:06:54 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:06:50 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:06:53 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:06:56 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:06:53 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:06:55 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:06:51 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:54:04 pm


5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:34 pm

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:34 pm
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Wednesday 06 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:34 pm
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Wednesday 06 September, 2023,  George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:34 pm
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:34 pm
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:33 pm
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:33 pm

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:33 pm

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/06, 12:02:25 PM

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:33 pm

Notes

As Above Photo

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:33 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:33 pm

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/06, 12:02:28 PM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/06, 12:02:31 PM	George Awad	-
MSSB SN installation ITP.pdf	2023/09/06, 12:02:31 PM	George Awad	-

118 - Consult Room - Pre Sheet-ITP

[MSSB NN installation itp.pdf](#)

2023/09/06, 12:02:30 PM

George Awad

-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:33 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan
Wednesday 06 September,
2023,

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:34 pm

17 North Image * Hold Point

Tuesday 30 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:33 pm

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/06, 12:02:27 PM

18 East Image * Hold Point

Tuesday 30 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:32 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/09/06, 12:02:30 PM**

19 South Image * Hold Point

Tuesday 30 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:32 pm

Notes

Southern elevation is glazing. Pre-Sheet not required.
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:32 pm

20 West Image * Hold Point

Tuesday 30 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 12:02:32 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/09/06, 12:02:23 PM**

Name

Signature

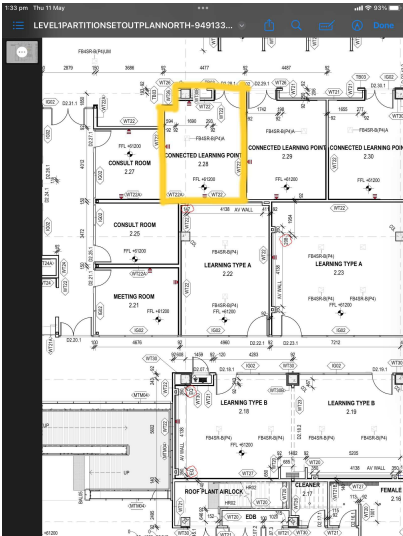
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

119 - Connected Learning Point - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.28 CONNECTED LEARNING POINT
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:21:29 am
Modified by	George Awad on Wednesday 06 September, 2023, 2:22:29 pm
Downloaded	Wednesday 06 September, 2023, 2:22:34 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:39:33 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:39:33 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:07:35 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:07:29 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:07:35 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:07:32 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:07:35 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:07:30 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:07:32 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:07:34 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:54:27 pm

5


Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:04 pm

119 - Connected Learning Point - Pre Sheet-ITP

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:04 pm
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Wednesday 06 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:04 pm
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Wednesday 06 September, 2023  George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:04 pm
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:04 pm
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:03 pm
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:03 pm

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:03 pm

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/06, 2:21:54 PM

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:03 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:03 pm

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB NN installation itp.pdf	2023/09/06, 2:21:56 PM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/06, 2:21:51 PM	George Awad	-
MSSB SN installation ITP.pdf	2023/09/06, 2:21:56 PM	George Awad	-
GP-AR~1.PDF	2023/09/06, 2:21:57 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:03 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Wednesday 06 September, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:04 pm

17 North Image * Hold Point

Tuesday 23 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:03 pm

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/06, 2:21:59 PM

18 East Image * Hold Point

Tuesday 23 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:02 pm

Photos (1)



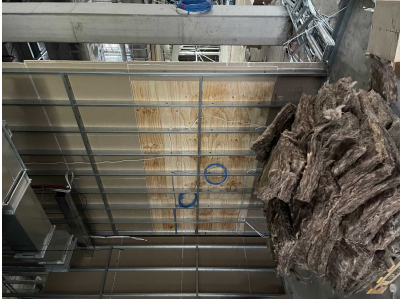
Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/06, 2:21:56 PM

19 South Image * Hold Point

Tuesday 23 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:02 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/09/06, 2:22:01 PM**

20 West Image * Hold Point

Tuesday 23 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:22:02 pm

Name

Signature

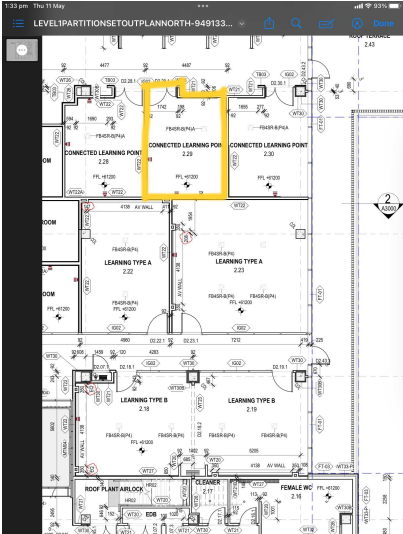
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

120 - Connected Learning Point- Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.29 CONNECTED LEARNING POINT
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:22:19 am
Modified by	George Awad on Wednesday 06 September, 2023, 2:26:30 pm
Downloaded	Wednesday 06 September, 2023, 2:26:33 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:40:44 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:40:42 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:08:15 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 11:08:12 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:08:08 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:08:09 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:08:15 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 11:08:15 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:08:10 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:08:09 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:54:54 pm

5


Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:20 pm

120 - Connected Learning Point- Pre Sheet-ITP

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:20 pm
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Wednesday 06 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:20 pm
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Wednesday 06 September, 2023  George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:21 pm
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:20 pm
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:20 pm
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:20 pm

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:20 pm

13

Is the acoustic insulation installed as per specification/drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:19 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:19 pm

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB SN installation ITP.pdf	2023/09/06, 2:26:11 PM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/06, 2:26:13 PM	George Awad	-
GP-AR~1.PDF	2023/09/06, 2:26:13 PM	George Awad	-
MSSB NN installation itp.pdf	2023/09/06, 2:26:12 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:19 pm

16

Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Wednesday 06 September, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:21 pm

17

North Image * Hold Point

Tuesday 23 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:19 pm

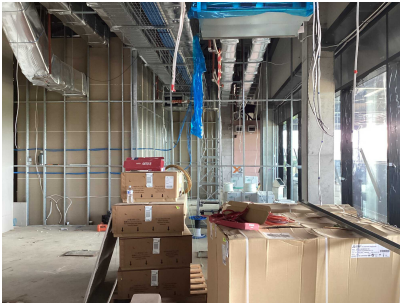
18

East Image * Hold Point

Tuesday 23 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:19 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/09/06, 2:26:16 PM**

19 South Image * Hold Point

Tuesday 23 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:19 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/09/06, 2:26:18 PM**

20 West Image * Hold Point

Tuesday 23 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:26:19 pm

Name

Signature

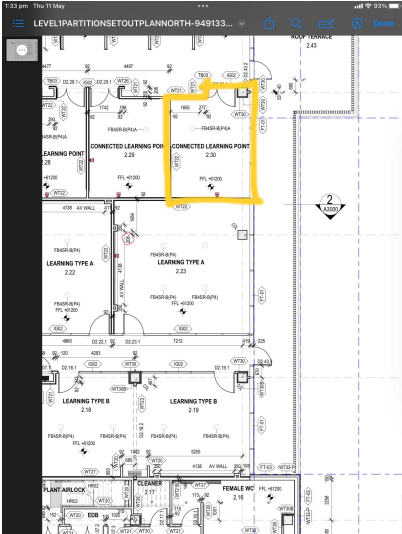
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

121 - Connected Learning Point - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.30 CONNECTED LEARNING POINT
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:23:08 am
Modified by	George Awad on Wednesday 06 September, 2023, 2:36:38 pm
Downloaded	Wednesday 06 September, 2023, 2:36:41 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:42:37 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:42:37 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:11:44 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:11:38 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:11:44 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:11:41 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:11:44 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:11:39 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:11:42 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:11:40 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:55:35 pm


5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:27 pm

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:27 pm
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Wednesday 06 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:27 pm
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Wednesday 06 September, 2023  George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:27 pm
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:27 pm
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:27 pm
11 ZipClad - Water Test Conducted on Facade * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:27 pm

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:27 pm

13

Is the acoustic insulation installed as per specification/drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:26 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:26 pm

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
GP-AR~1.PDF	2023/09/06, 2:36:25 PM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/06, 2:36:18 PM	George Awad	-
MSSB SN installation ITP.pdf	2023/09/06, 2:36:19 PM	George Awad	-
MSSB NN installation itp.pdf	2023/09/06, 2:36:23 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:26 pm

16

Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Wednesday 06 September, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:28 pm

17

North Image * Hold Point

Tuesday 23 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:26 pm

18

East Image * Hold Point

Tuesday 23 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:26 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/09/06, 2:36:22 PM**

19 South Image * Hold Point

Tuesday 23 May, 2023

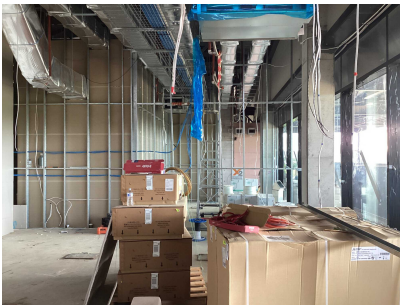
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:26 pm

20 West Image * Hold Point

Tuesday 23 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:36:26 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/09/06, 2:36:24 PM**

Name

Signature

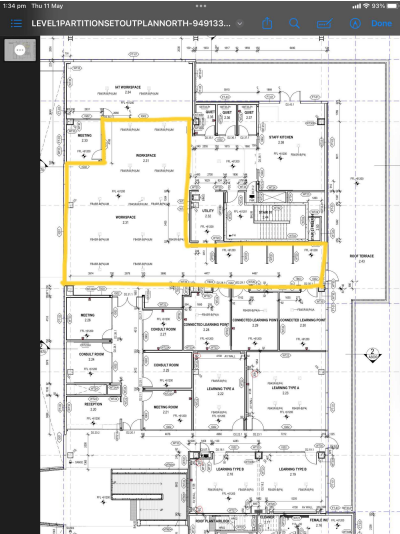
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

122 - Workspace - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.31 WORKSPACE
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:27:17 am
Modified by	George Awad on Wednesday 06 September, 2023, 2:48:15 pm
Downloaded	Wednesday 06 September, 2023, 2:48:21 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:44:03 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:44:02 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:12:20 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 11:12:18 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:12:15 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:12:16 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:12:20 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:12:17 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:12:19 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:12:17 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:56:03 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:51 pm

122 - Workspace - Pre Sheet-ITP

6	Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:51 pm
7	Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Wednesday 06 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:51 pm
8	AV service roughened in according to approved room layout drawing. * Hold Point	N/A Wednesday 06 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:51 pm
9	Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:50 pm
10	Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:50 pm
11	ZipClad - Water Test Conducted on Facade * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:50 pm
12	Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:50 pm

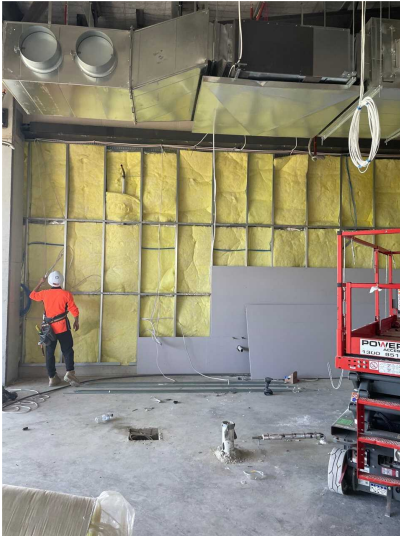
13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:50 pm

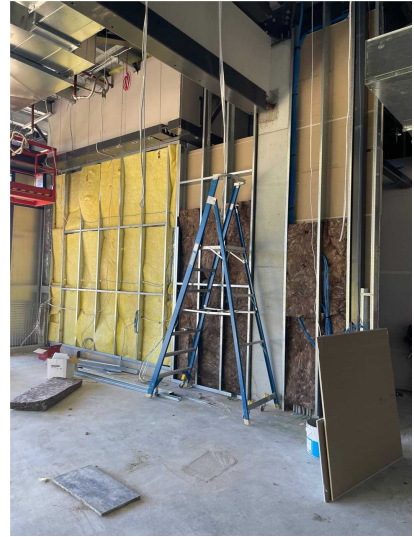
Photos (3)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/06, 2:47:38 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/06, 2:47:39 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/06, 2:47:39 PM

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:50 pm

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB NN installation itp.pdf	2023/09/06, 2:47:45 PM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/06, 2:47:48 PM	George Awad	-
MSSB SN installation ITP.pdf	2023/09/06, 2:47:47 PM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/06, 2:47:47 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:50 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan
Wednesday 06 September, 2023

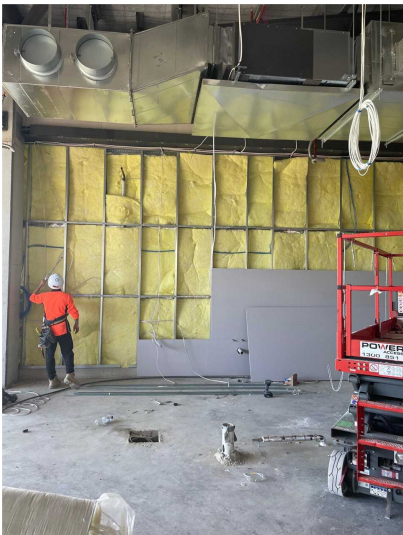
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:51 pm

17 North Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:49 pm

Photos (3)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/06, 2:47:43 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/06, 2:47:46 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/06, 2:47:47 PM

18 East Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:49 pm

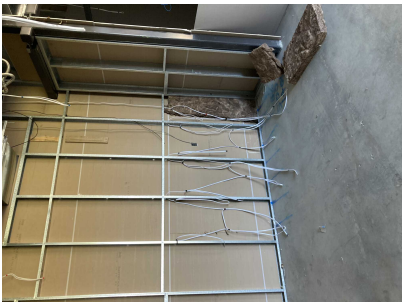
Photos (3)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/06, 2:47:41 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/06, 2:47:42 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/06, 2:47:45 PM

19 South Image * Hold Point

Tuesday 09 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:49 pm

Notes

Southern elevation is glazing. Pre-Sheet not required
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:49 pm

20 West Image * Hold Point

Tuesday 09 May, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:49 pm

Notes

Western elevation is glazing. Pre-Sheet not required.
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:47:49 pm

Name

Signature

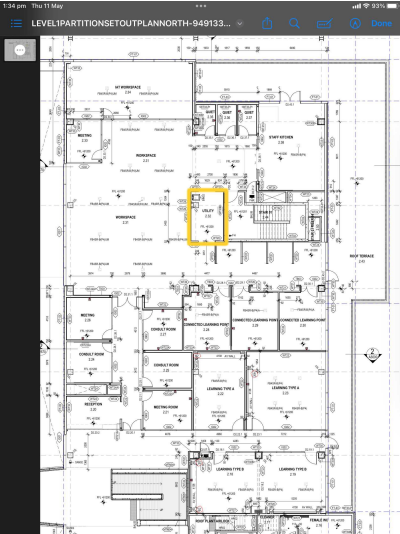
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

123 - Utility - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.32 UTILITY
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:27:45 am
Modified by	George Awad on Wednesday 06 September, 2023, 2:54:51 pm
Downloaded	Wednesday 06 September, 2023, 2:54:55 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:45:07 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:45:03 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:12:48 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:12:45 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:12:47 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:12:42 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:12:47 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:12:46 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:12:46 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:12:43 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:56:22 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:38 pm

123 - Utility - Pre Sheet-ITP

6	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:38 pm
Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	
7	N/A Wednesday 06 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:39 pm
Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	
8	N/A Wednesday 06 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:39 pm
AV service roughened in according to approved room layout drawing. * Hold Point	
9	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:38 pm
Is fire stopping applied as per drawings? Attach evidence * Hold Point	
10	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:38 pm
Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:38 pm
12	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:38 pm
Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	

123 - Utility - Pre Sheet-ITP

13	Is the acoustic insulation installed as per specification/drawings? Attache evidence *	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:38 pm
Hold Point		
14	Are the mechanical works installed as per drawings? Attach evidence *	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:37 pm
Hold Point		
Notes Part of Workspace ITP George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:37 pm		
15	Door Frames installed in plumb and have correct allowance for finish *	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:37 pm
Hold Point		
16	Dunrite Accepts walls are ready for sheet *	 Hills Pan Wednesday 06 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:39 pm
Hold Point		
17	North Image * Hold Point	Tuesday 09 May, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:37 pm
18	East Image * Hold Point	Tuesday 09 May, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:37 pm
19	South Image * Hold Point	Tuesday 09 May, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:37 pm
Photos (2)		

123 - Utility - Pre Sheet-ITP



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/09/06, 2:54:34 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/09/06, 2:54:36 PM

20 West Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 2:54:37 pm

Name

Signature

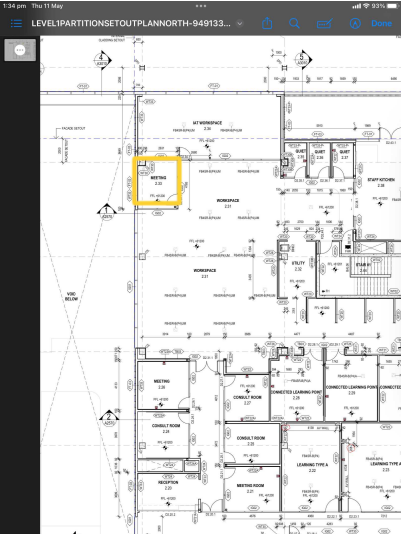
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

124 - Meeting - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.33 MEETING
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:28:20 am
Modified by	George Awad on Wednesday 06 September, 2023, 3:00:32 pm
Downloaded	Wednesday 06 September, 2023, 3:00:35 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:46:03 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:45:58 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:13:31 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:13:25 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:13:31 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:13:28 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:13:31 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:13:26 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:13:29 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:13:28 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:56:44 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:14 pm

124 - Meeting - Pre Sheet-ITP

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:14 pm
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Wednesday 06 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:14 pm
8 AV service roughened in according to approved room layout drawing. * Hold Point	 As Per ITP Wednesday 06 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:15 pm
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:14 pm
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:14 pm
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:14 pm
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:14 pm

124 - Meeting - Pre Sheet-ITP

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:13 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:13 pm

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB NN installation itp.pdf	2023/09/06, 3:00:11 PM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/06, 3:00:12 PM	George Awad	-
MSSB SN installation ITP.pdf	2023/09/06, 3:00:09 PM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/06, 3:00:09 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:13 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Wednesday 06 September, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:15 pm

17 North Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:13 pm

Notes

Northern elevation is glazing. Pre-Sheet not required

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:13 pm

18 East Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:13 pm

Notes

124 - Meeting - Pre Sheet-ITP

Eastern elevation is glazing. Pre-Sheet not required

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:13 pm

19 South Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:13 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/09/06, 3:00:11 PM**

20 West Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:12 pm

Notes

Western elevation is glazing. Pre-Sheet not required

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:00:12 pm

Name

Signature

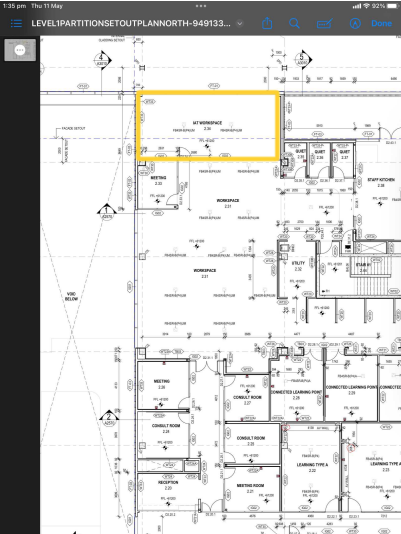
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

125 - IAT Workspace - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.34 IAT WORKSPACE
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:29:01 am
Modified by	George Awad on Wednesday 06 September, 2023, 3:07:42 pm
Downloaded	Wednesday 06 September, 2023, 3:07:51 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:48:02 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:48:01 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:14:46 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:14:37 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:14:39 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:14:43 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:14:46 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 11:14:46 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:14:38 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:14:40 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:57:23 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:15 pm

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:15 pm
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Wednesday 06 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:15 pm
8 AV service roughened in according to approved room layout drawing. * Hold Point	As Per ITP Wednesday 06 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:15 pm
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:15 pm
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:15 pm
11 ZipClad - Water Test Conducted on Facade * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:15 pm
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:14 pm

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:14 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:14 pm

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/06, 3:07:08 PM	George Awad	-
MSSB NN installation itp.pdf	2023/09/06, 3:07:08 PM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/06, 3:07:13 PM	George Awad	-
MSSB SN installation ITP.pdf	2023/09/06, 3:07:08 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:14 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Wednesday 06 September, 2023

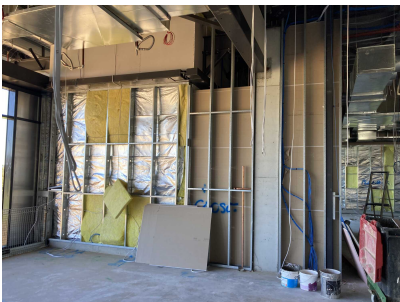
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:16 pm

17 North Image * Hold Point

Saturday 13 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:14 pm

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/06, 3:07:12 PM

18 East Image * Hold Point

Saturday 13 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:14 pm

Notes

Eastern elevation is glazing. Pre-Sheet not required

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:14 pm

19 South Image * Hold Point

Saturday 13 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:14 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/09/06, 3:07:10 PM**

20 West Image * Hold Point

Saturday 13 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:13 pm

Notes

Western elevation is glazing. Pre-Sheet not required

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:07:13 pm

Name

Signature

Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

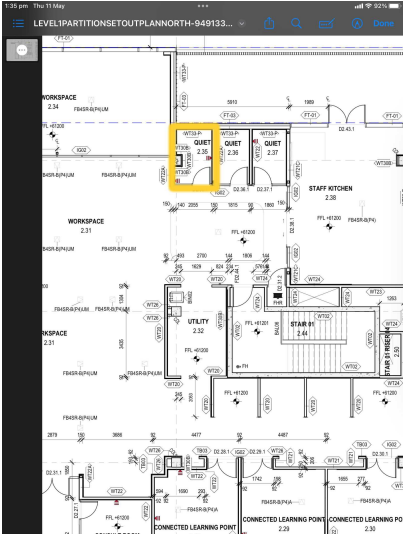
126 - Quiet - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.35 QUIET
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:29:41 am
Modified by	George Awad on Wednesday 06 September, 2023, 3:58:35 pm
Downloaded	Wednesday 06 September, 2023, 3:58:38 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. *	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:50:49 pm

Hold Point

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/05/11, 4:50:48 PM

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:15:19 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:15:12 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:15:18 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:15:13 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:15:19 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:15:14 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:15:17 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:15:13 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:57:56 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:29 pm

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:29 pm
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Wednesday 06 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:30 pm
8 AV service roughened in according to approved room layout drawing. * Hold Point	N/A Wednesday 06 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:30 pm
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:29 pm
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:29 pm
11 ZipClad - Water Test Conducted on Facade * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:29 pm
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:29 pm

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:29 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:28 pm

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/06, 3:57:20 PM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/06, 3:57:25 PM	George Awad	-
MSSB NN installation itp.pdf	2023/09/06, 3:57:23 PM	George Awad	-
MSSB SN installation ITP.pdf	2023/09/06, 3:57:23 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:28 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Wednesday 06 September, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:30 pm

17 North Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:28 pm

18 East Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:28 pm

19 South Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:28 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/09/06, 3:57:25 PM

20 West Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 06 September, 2023, 3:57:28 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/09/06, 3:57:22 PM

Name

Signature

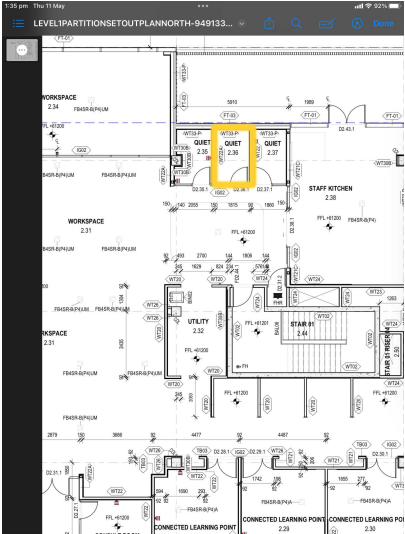
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

127 - Quiet - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.36 QUIET
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:30:01 am
Modified by	George Awad on Thursday 07 September, 2023, 11:44:01 am
Downloaded	Thursday 07 September, 2023, 11:44:06 am
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:51:38 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:51:32 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:16:03 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720 LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:15:59 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:16:02 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:15:57 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:16:03 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 11:16:02 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:15:57 AM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:15:58 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:58:11 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:42:04 am

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:42:04 am
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Thursday 07 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:42:04 am
8 AV service roughened in according to approved room layout drawing. * Hold Point	N/A Thursday 07 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:42:04 am
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:42:04 am
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:42:04 am
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:42:04 am
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:42:03 am

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:42:03 am

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:42:03 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB NN installation itp.pdf	2023/09/07, 11:42:02 AM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/07, 11:42:01 AM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/07, 11:42:02 AM	George Awad	-
MSSB SN installation ITP.pdf	2023/09/07, 11:42:01 AM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:42:03 am

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Thursday 07 September, 2023,

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:42:04 am

17 North Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:43:45 am

18 East Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:43:45 am

19 South Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:43:45 am

20 West Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 11:43:44 am

Photos (1)



Captured by: **George Awad ADCO
CONSTRUCTIONS PTY LIMITED**
Date: **2023/09/07, 11:43:44 AM**

Name

Signature

Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

128 - Quiet - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.37 QUIET
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:30:23 am
Modified by	George Awad on Thursday 07 September, 2023, 11:46:40 am
Downloaded	Thursday 07 September, 2023, 11:46:45 am
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:52:15 pm
Photos (1) Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:52:13 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:16:48 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:16:42 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:16:48 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:16:41 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:16:48 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:16:42 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:16:44 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:16:46 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:58:32 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:46:31 am

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:46:31 am
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Thursday 07 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:46:31 am
8 AV service roughened in according to approved room layout drawing. * Hold Point	N/A Thursday 07 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:46:31 am
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:46:31 am
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:46:31 am
11 ZipClad - Water Test Conducted on Facade * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:46:30 am
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:46:30 am

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:46:30 am

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:46:30 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB SN installation ITP.pdf	2023/09/07, 11:46:25 AM	George Awad	-
MSSB NN installation itp.pdf	2023/09/07, 11:46:26 AM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/07, 11:46:25 AM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/07, 11:46:26 AM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:46:30 am

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Thursday 07 September, 2023,

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:46:31 am

17 North Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:46:30 am

18 East Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:46:30 am

19 South Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:46:29 am

20 West Image * Hold Point

Monday 12 June, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 11:46:29 am

Photos (1)



Captured by: **George Awad ADCO
CONSTRUCTIONS PTY LIMITED**
Date: **2023/09/07, 11:46:29 AM**

Name

Signature

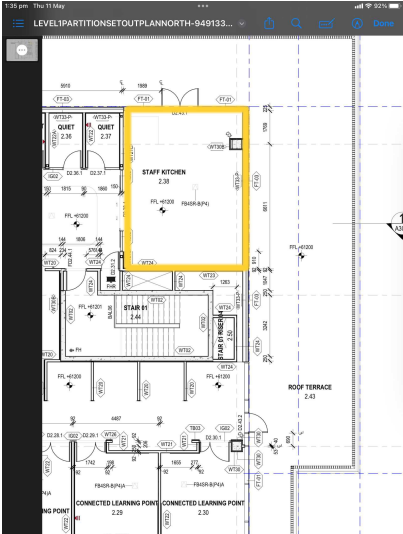
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

129 - Staff Kitchen - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.38 STAFF KITCHEN
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:30:53 am
Modified by	George Awad on Monday 18 September, 2023, 4:33:38 pm
Downloaded	Monday 18 September, 2023, 4:33:49 pm
Template	NSW TAFE IATC – Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:53:33 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:53:31 PM	

2

Utech - Is the power installed per drawings?

Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:17:25 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:17:22 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:17:19 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:17:25 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:17:25 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:17:20 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:17:23 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:17:20 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point


George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:59:00 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:55:22 am

Photos (0)

Files (1)

Filename	Date	Attached by	Comments
STAFF KITCHEN ITP.pdf	2023/09/18, 4:33:10 PM	George Awad	-

6 Foran – Is the drainage installed as per drawings? Attached evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:55:21 am								
Photos (0) Files (1) <table border="1"> <thead> <tr> <th>Filename</th> <th>Date</th> <th>Attached by</th> <th>Comments</th> </tr> </thead> <tbody> <tr> <td>STAFF KITCHEN ITP.pdf</td> <td>2023/09/18, 4:33:11 PM</td> <td>George Awad</td> <td>-</td> </tr> </tbody> </table>		Filename	Date	Attached by	Comments	STAFF KITCHEN ITP.pdf	2023/09/18, 4:33:11 PM	George Awad	-
Filename	Date	Attached by	Comments						
STAFF KITCHEN ITP.pdf	2023/09/18, 4:33:11 PM	George Awad	-						
7 Foran – Hydraulic services roughed in according to approved room layout drawings. * Hold Point	Matt Foran Monday 18 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 18 September, 2023, 4:33:20 pm								
8 AV service roughened in according to approved room layout drawing. * Hold Point	N/A Monday 18 September, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 18 September, 2023, 4:33:20 pm								
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 18 September, 2023, 4:33:20 pm								
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 18 September, 2023, 4:33:20 pm								
11 ZipClad – Water Test Conducted on Facade * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 18 September, 2023, 4:33:20 pm								

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 18 September, 2023, 4:33:20 pm

Photos (1)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/18, 4:33:12 PM

13

Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 18 September, 2023, 4:33:19 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 18 September, 2023, 4:33:19 pm

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB SN installation ITP.pdf	2023/09/18, 4:33:18 PM	George Awad	-
MSSB NN installation itp.pdf	2023/09/18, 4:33:18 PM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/18, 4:33:17 PM	George Awad	-
Kingswood Tafe_LL P ITPs 16 MAY 23.pdf	2023/09/18, 4:33:16 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 18 September, 2023, 4:33:20 pm

16

Dunrite Accepts walls are ready for sheet *
Hold Point



Hills Pan

Monday 18 September, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 18 September, 2023, 4:33:21 pm

17 North Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 18 September, 2023, 4:33:19 pm

Photos (3)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/18, 4:33:15 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/18, 4:33:17 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/18, 4:33:14 PM

18 East Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 18 September, 2023, 4:33:19 pm

19 South Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 18 September, 2023, 4:33:19 pm

20 West Image * Hold Point

Tuesday 09 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 18 September, 2023, 4:33:19 pm

Name

Signature

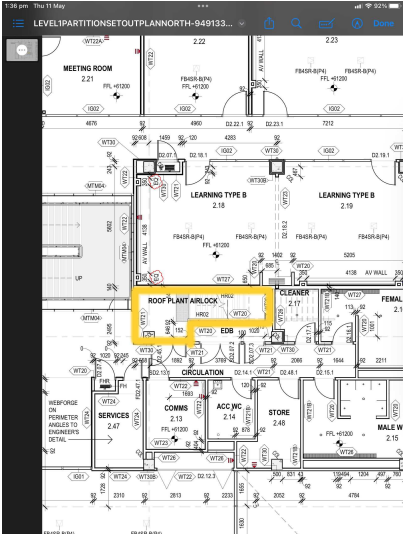
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

130 - Roof Plant Airlock - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.45 ROOF PLANT AIRLOCK
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:31:47 am
Modified by	George Awad on Thursday 07 September, 2023, 11:58:08 am
Downloaded	Thursday 07 September, 2023, 11:58:11 am
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:54:42 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:54:36 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:18:08 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Level 1 Northern Photos.pdf	2023/05/15, 11:18:07 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:18:02 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:18:04 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:18:08 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:18:05 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:18:08 AM	George Awad	-
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:18:02 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 2:59:25 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:57:56 am

130 - Roof Plant Airlock - Pre Sheet-ITP

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:57:56 am
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Thursday 07 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:57:57 am
8 AV service roughened in according to approved room layout drawing. * Hold Point	N/A Thursday 07 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:57:57 am
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:57:56 am
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:57:56 am
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:57:56 am
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:57:56 am

130 - Roof Plant Airlock - Pre Sheet-ITP

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:57:56 am
14 Are the mechanical works installed as per drawings? Attach evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:57:57 am
15 Door Frames installed in plumb and have correct allowance for finish * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:57:56 am
16 Dunrite Accepts walls are ready for sheet * Hold Point	 Hills Pan Thursday 07 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:57:57 am
17 North Image * Hold Point	Wednesday 24 May, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:57:55 am
18 East Image * Hold Point	Wednesday 24 May, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:57:55 am
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/09/07, 11:57:52 AM	
19 South Image * Hold Point	Wednesday 24 May, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 11:57:55 am

20 West Image * Hold Point

Wednesday 24 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 11:57:55 am

Photos (1)



Captured by: **George Awad ADCO
CONSTRUCTIONS PTY LIMITED**
Date: **2023/09/07, 11:57:49 AM**

Name

Signature

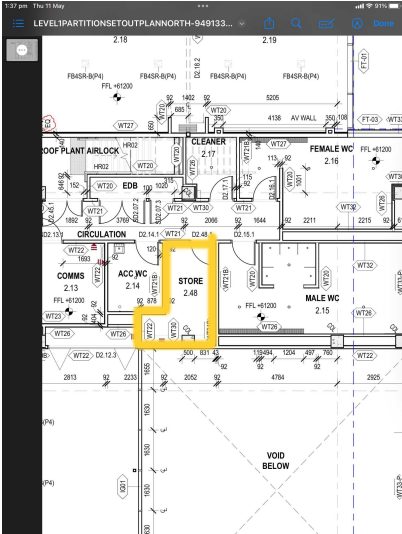
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

132 - Store - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.48 STORE
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:32:53 am
Modified by	George Awad on Thursday 07 September, 2023, 12:06:51 pm
Downloaded	Thursday 07 September, 2023, 12:07:03 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:56:59 pm
Photos (1)  Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:56:54 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:19:09 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:19:04 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:19:09 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:19:06 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 15 May, 2023, 11:19:09 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
16 #, Level 1 Northern Side ITP Rough In.pdf	2023/05/15, 11:19:05 AM	George Awad	-
Level 1 Northern Photos.pdf	2023/05/15, 11:19:08 AM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - Wall Mark-Up.pdf	2023/05/15, 11:19:06 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 17 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 17 May, 2023, 3:00:07 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:06:04 pm

132 - Store - Pre Sheet-ITP

6 Foran - Is the drainage installed as per drawings? Attached evidence * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:06:04 pm
7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Thursday 07 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:06:04 pm
8 AV service roughened in according to approved room layout drawing. * Hold Point	N/A Thursday 07 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:06:04 pm
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:06:04 pm
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:06:03 pm
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:06:03 pm
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:06:03 pm

132 - Store - Pre Sheet-ITP

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:06:03 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:06:03 pm

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB NN installation itp.pdf	2023/09/07, 12:05:56 PM	George Awad	-
MSSB SN installation ITP.pdf	2023/09/07, 12:05:58 PM	George Awad	-
GP-AR-DWG-A1720 LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/07, 12:06:01 PM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/07, 12:06:01 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:06:03 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Thursday 07 September, 2023,

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:06:04 pm

17 North Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:06:03 pm

Photos (3)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/07, 12:05:56 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/07, 12:05:58 PM



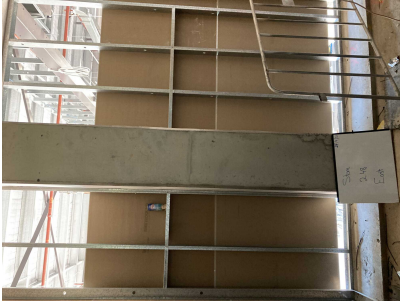
Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/07, 12:05:52 PM

18 East Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 12:06:03 pm

Photos (1)



Captured by: **George Awad ADCO
CONSTRUCTIONS PTY LIMITED**
Date: 2023/09/07, 12:05:54 PM

19 South Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 12:06:02 pm

Photos (1)



Captured by: **George Awad ADCO
CONSTRUCTIONS PTY LIMITED**
Date: 2023/09/07, 12:05:50 PM

20 West Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 12:06:02 pm

Photos (1)



Captured by: **George Awad ADCO**
CONSTRUCTIONS PTY LIMITED
Date: **2023/09/07, 12:06:01 PM**

Name

Signature

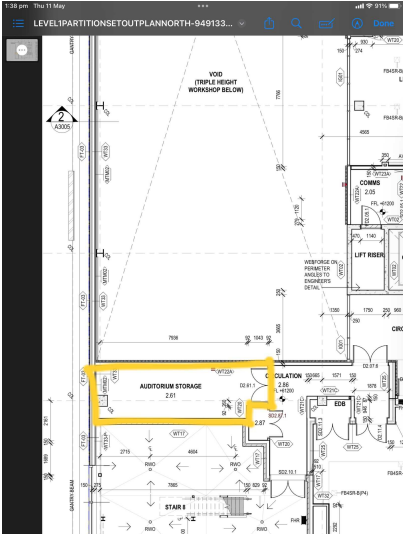
Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

134 - Auditorium Storage - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LEVEL 1 > 2.61 AUDITORIUM STORAGE
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 11:34:28 am
Modified by	George Awad on Thursday 07 September, 2023, 12:55:53 pm
Downloaded	Thursday 07 September, 2023, 12:56:00 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 11 May, 2023, 4:59:32 pm
Photos (1)  The image is a screenshot of a mobile application displaying an architectural floor plan for Level 1. The plan shows various rooms and corridors. A specific area labeled 'AUDITORIUM STORAGE' is highlighted with a yellow rectangular box. Other labels visible on the plan include 'VOID (TRIPLE HEIGHT WORKSHOP BELT)', 'CORRIDOR', 'LIFT RISER', 'CIRC', 'STAIR 1', and 'STAIR 2'. The plan also shows dimensions and structural elements like walls and doors. Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/05/11, 4:59:26 PM	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:20 pm

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Level 1 South Rooms ITP.pdf	2023/09/07, 12:55:17 PM	George Awad	-
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/09/07, 12:55:10 PM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:20 pm

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Level 1 South Rooms ITP.pdf	2023/09/07, 12:55:17 PM	George Awad	-
ITC & ITR Lighting & Power Rough Level 1 South.docx	2023/09/07, 12:55:11 PM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Thursday 07 September, 2023,

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:20 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:20 pm

6

Foran - Is the drainage installed as per drawings? Attached evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:20 pm

134 - Auditorium Storage - Pre Sheet-ITP

7 Foran - Hydraulic services roughed in according to approved room layout drawings. * Hold Point	N/A Thursday 07 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:20 pm
8 AV service roughened in according to approved room layout drawing. * Hold Point	N/A Thursday 07 September, 2023, George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:20 pm
9 Is fire stopping applied as per drawings? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:20 pm
10 Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:19 pm
11 ZipClad - Water Test Conducted on Facade * Hold Point	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:19 pm
12 Are the noggings installed as required to suit fitments etc? Attach evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:19 pm
13 Is the acoustic insulation installed as per specification/drawings? Attache evidence * Hold Point	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:19 pm

134 - Auditorium Storage - Pre Sheet-ITP

14

Are the mechanical works installed as per drawings?

Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:19 pm

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
MSSB NN installation itp.pdf	2023/09/07, 12:55:16 PM	George Awad	-
GP-AR-DWG-A1720_LEVEL 1 - FURNITURE AND EQUIPMENT PLAN [O].pdf	2023/09/07, 12:55:18 PM	George Awad	-
Kingswood Tafe LLP ITPs 16 MAY 23.pdf	2023/09/07, 12:55:11 PM	George Awad	-
MSSB SN installation ITP.pdf	2023/09/07, 12:55:16 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:19 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Thursday 07 September, 2023,

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:21 pm

17 North Image * Hold Point

Wednesday 12 July, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:19 pm

18 East Image * Hold Point

Wednesday 12 July, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:19 pm

19 South Image * Hold Point

Wednesday 12 July, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:19 pm

Photos (1)

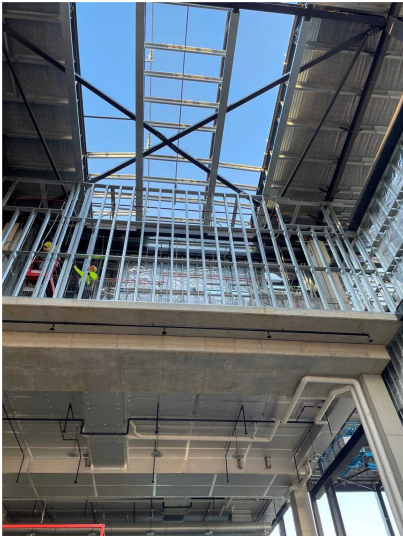


Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/09/07, 12:55:13 PM

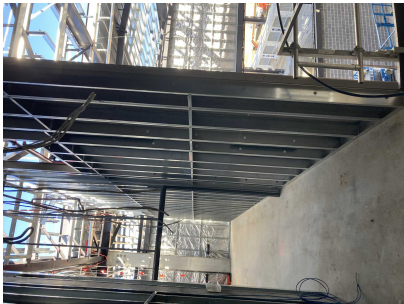
20 West Image * Hold Point

Wednesday 12 July, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 12:55:19 pm

Photos (2)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/09/07, 12:55:10 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/09/07, 12:55:16 PM

Name _____ Signature _____ Date _____
