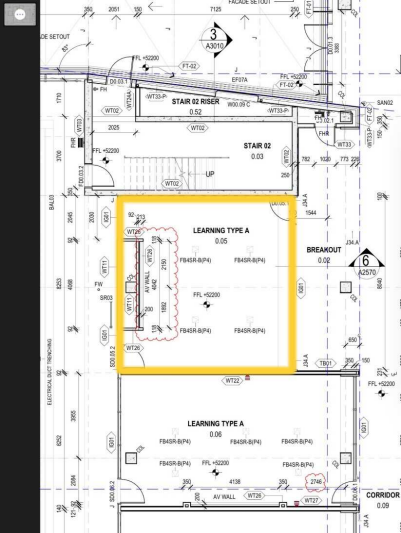


(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

138 - Learning Type A- Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > 0.05 LEARNING TYPE A
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 12:13:05 pm
Modified by	George Awad on Friday 30 June, 2023, 1:39:44 pm
Downloaded	Friday 30 June, 2023, 1:39:49 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
<div>1</div> <div>Mark up plan of walls to be sheeted. *</div> <div>Hold Point</div>	<div>Yes</div> <div>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 14 March, 2023, 10:43:57 am</div>
<div>Photos (1)</div> <div></div> <div>Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/03/14, 10:44:00 AM</div>	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday
14 March, 2023, 11:26:38 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
Lower Ground Floor Zone 2 Photos.pdf	2023/03/14, 11:26:35 AM	George Awad	-
Lower Ground Floor Wall Mark Up.pdf	2023/03/14, 11:26:35 AM	George Awad	-
15 #, Lower Ground Floor Zone 2 ITP Rough In.pdf	2023/03/14, 11:26:31 AM	George Awad	-
ITC & ITR Lighting & Power Rough in Lower Ground floor 09-03-2023.docx	2023/03/14, 11:26:30 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday
14 March, 2023, 11:26:38 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
Lower Ground Floor Wall Mark Up.pdf	2023/03/14, 11:26:37 AM	George Awad	-
Lower Ground Floor Zone 2 Photos.pdf	2023/03/14, 11:26:38 AM	George Awad	-
15 #, Lower Ground Floor Zone 2 ITP Rough In.pdf	2023/03/14, 11:26:32 AM	George Awad	-
ITC & ITR Lighting & Power Rough in Lower Ground floor 09-03-2023.docx	2023/03/14, 11:26:31 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 29 March, 2023

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday
29 March, 2023, 2:09:37 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
20 April, 2023, 2:11:29 pm

138 - Learning Type A- Pre Sheet-ITP

<p>6</p> <p>Foran - Is the drainage installed as per drawings? Attached evidence *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:11:29 pm</p>
<p>7</p> <p>Foran - Hydraulic services roughed in according to approved room layout drawings. *</p> <p>Hold Point</p>	<p>GA</p> <p>N/a</p> <p>Thursday 20 April, 2023</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:11:29 pm</p>
<p>8</p> <p>AV service roughened in according to approved room layout drawing. *</p> <p>Hold Point</p>	<p>Complete as Per ITPs</p> <p>Thursday 20 April, 2023</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:11:29 pm</p>
<p>9</p> <p>Is fire stopping applied as per drawings? Attach evidence *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:11:29 pm</p>
<p>10</p> <p>Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:11:29 pm</p>
<p>11 ZipClad - Water Test Conducted on Facade *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:11:29 pm</p>
<p>Notes</p> <p>Room is internal of building. Water testing not required.</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:11:29 pm</p>	

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:11:29 pm

Photos (3)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/04/20, 2:11:21 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/04/20, 2:11:24 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/04/20, 2:11:26 PM

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:11:28 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:11:28 pm

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Lower Ground BMS Mark-up - 28.2.23.pdf	2023/04/20, 2:11:27 PM	George Awad	-
KERFOOT ITC - 14.2.23.pdf	2023/04/20, 2:11:27 PM	George Awad	-
GP-AR~1.PDF	2023/04/20, 2:11:28 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:11:28 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan
Friday 26 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 26 May, 2023, 2:45:46 pm

17 North Image * Hold Point

Tuesday 28 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 12:50:15 pm

Notes

No Pre- Sheet Required. Glazed Wall is installed to the Northern Elevation


George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 12:50:15 pm

18 East Image * Hold Point

Tuesday 28 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 12:50:15 pm

Photos (1)

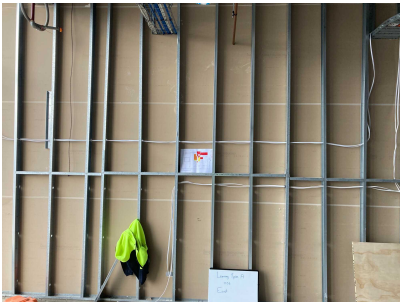

Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 12:50:09 PM

19 South Image * Hold Point

Wednesday 29 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 12:50:15 pm

Photos (3)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/06/30, 12:50:12 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/06/30, 12:50:11 PM




Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/06/30, 12:50:14 PM

20 West Image * Hold Point

Wednesday 29 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 12:50:15 pm

Photos (1)

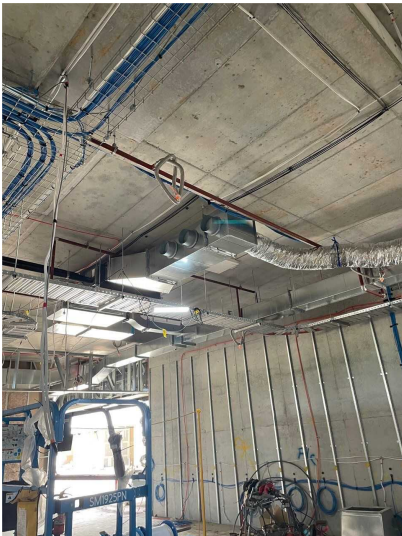

Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/06/30, 12:50:09 PM

Name

Signature

Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

139 - Learning Type A - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > 0.06 LEARNING TYPE A
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 12:13:40 pm
Modified by	George Awad on Friday 30 June, 2023, 1:22:22 pm
Downloaded	Friday 30 June, 2023, 1:22:26 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
<div>1</div> <div>Mark up plan of walls to be sheeted. *</div> <div>Hold Point</div>	<div>Yes</div> <div>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 14 March, 2023, 10:44:25 am</div>
<div>Photos (1)</div> <div></div> <div>Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/03/14, 10:44:30 AM</div>	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 14 March, 2023, 11:27:30 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
Lower Ground Floor Wall Mark Up.pdf	2023/03/14, 11:27:23 AM	George Awad	-
ITC & ITR Lighting & Power Rough in Lower Ground floor 09-03-2023.docx	2023/03/14, 11:27:18 AM	George Awad	-
15 #, Lower Ground Floor Zone 2 ITP Rough In.pdf	2023/03/14, 11:27:18 AM	George Awad	-
Lower Ground Floor Zone 2 Photos.pdf	2023/03/14, 11:27:24 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 14 March, 2023, 11:27:30 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
Lower Ground Floor Zone 2 Photos.pdf	2023/03/14, 11:27:23 AM	George Awad	-
ITC & ITR Lighting & Power Rough in Lower Ground floor 09-03-2023.docx	2023/03/14, 11:27:19 AM	George Awad	-
Lower Ground Floor Wall Mark Up.pdf	2023/03/14, 11:27:29 AM	George Awad	-
15 #, Lower Ground Floor Zone 2 ITP Rough In.pdf	2023/03/14, 11:27:21 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Wednesday 29 March, 2023

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 29 March, 2023, 2:11:11 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:24:11 pm

139 - Learning Type A - Pre Sheet-ITP

<p>6</p> <p>Foran - Is the drainage installed as per drawings? Attached evidence *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:24:11 pm</p>
<p>7</p> <p>Foran - Hydraulic services roughed in according to approved room layout drawings. *</p> <p>Hold Point</p>	<p>Not Required Thursday 20 April, 2023</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:24:11 pm</p>
<p>8</p> <p>AV service roughened in according to approved room layout drawing. *</p> <p>Hold Point</p>	<p>As per Complete ITP Thursday 20 April, 2023</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:24:12 pm</p>
<p>9</p> <p>Is fire stopping applied as per drawings? Attach evidence *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:24:11 pm</p>
<p>10</p> <p>Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:24:11 pm</p>
<p>11 ZipClad - Water Test Conducted on Facade *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:24:11 pm</p>
<p>Notes</p> <p>Water Test not required as room is internal.</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:24:11 pm</p>	

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
20 April, 2023, 2:24:11 pm

Photos (2)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/04/20, 2:24:08 PM



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/04/20, 2:24:06 PM

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
20 April, 2023, 2:24:11 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
20 April, 2023, 2:24:10 pm

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1700_LOWER GROUND - Mark Up.pdf	2023/04/20, 2:24:10 PM	George Awad	-
KERFOOT ITC - 14.2.23.pdf	2023/04/20, 2:24:09 PM	George Awad	-
Lower Ground BMS Mark-up - 28.2.23.pdf	2023/04/20, 2:24:09 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
20 April, 2023, 2:24:10 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan
Friday 26 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 26 May, 2023, 2:46:07 pm

17 North Image * Hold Point

Tuesday 28 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 1:21:14 pm

Notes

No Pre-Sheet Required. Glazed wall is installed to the Northern Elevation

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 1:21:14 pm

18 East Image * Hold Point


Tuesday 28 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 1:21:14 pm

Photos (4)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 1:21:05 PM

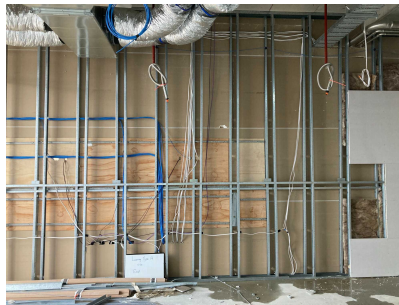

Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 1:21:07 PM



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 1:21:10 PM



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 1:21:08 PM

19 South Image * Hold Point

Tuesday 28 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 1:21:14 pm

Notes

No Pre-Sheet Required. Glazed wall is installed to the Southern Elevation

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 1:21:14 pm

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747


140 - Learning Type A - Pre Sheet-ITP

Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > 0.07 LEARNING TYPE A
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 1:02:56 pm
Modified by	George Awad on Friday 30 June, 2023, 2:23:47 pm
Downloaded	Friday 30 June, 2023, 2:23:54 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Response

Yes
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday
14 March, 2023, 10:44:49 am

Photos (1)

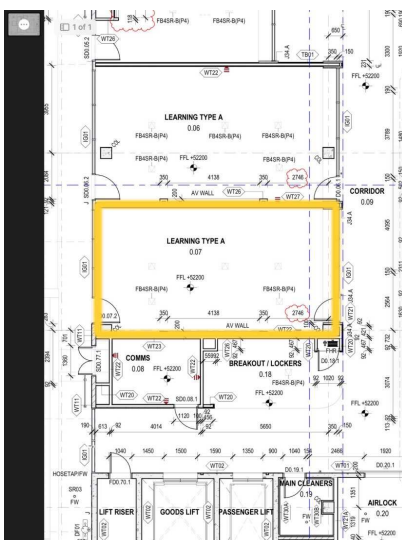

Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/03/14, 10:44:53 AM**

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday
14 March, 2023, 11:28:19 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
Lower Ground Floor Zone 2 Photos.pdf	2023/03/14, 11:28:16 AM	George Awad	-
15 #, Lower Ground Floor Zone 2 ITP Rough In.pdf	2023/03/14, 11:28:11 AM	George Awad	-
ITC & ITR Lighting & Power Rough in Lower Ground floor 09-03-2023.docx	2023/03/14, 11:28:10 AM	George Awad	-
Lower Ground Floor Wall Mark Up.pdf	2023/03/14, 11:28:14 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday
14 March, 2023, 11:28:19 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
ITC & ITR Lighting & Power Rough in Lower Ground floor 09-03-2023.docx	2023/03/14, 11:28:12 AM	George Awad	-
15 #, Lower Ground Floor Zone 2 ITP Rough In.pdf	2023/03/14, 11:28:11 AM	George Awad	-
Lower Ground Floor Zone 2 Photos.pdf	2023/03/14, 11:28:19 AM	George Awad	-
Lower Ground Floor Wall Mark Up.pdf	2023/03/14, 11:28:15 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point

George Joannou
Wednesday 29 March, 2023

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday
29 March, 2023, 2:11:42 pm

5


Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
20 April, 2023, 2:32:30 pm

140 - Learning Type A - Pre Sheet-ITP

<p>6</p> <p>Foran - Is the drainage installed as per drawings? Attached evidence *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:32:30 pm</p>
<p>7</p> <p>Foran - Hydraulic services roughed in according to approved room layout drawings. *</p> <p>Hold Point</p>	<p>N/A</p> <p>Thursday 20 April, 2023</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:32:30 pm</p>
<p>8</p> <p>AV service roughened in according to approved room layout drawing. *</p> <p>Hold Point</p>	<p></p> <p>As per completed ITP</p> <p>Thursday 20 April, 2023</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:32:31 pm</p>
<p>9</p> <p>Is fire stopping applied as per drawings? Attach evidence *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:32:30 pm</p>
<p>10</p> <p>Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:32:30 pm</p>
<p>11 ZipClad - Water Test Conducted on Facade *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:32:30 pm</p>
<p>Notes</p> <p>Not required as room is internal of building.</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:32:30 pm</p>	

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:32:30 pm

Photos (2)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/04/20, 2:32:24 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/04/20, 2:32:27 PM

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:32:30 pm

Notes

As per WT22 & WT27

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:32:30 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:32:29 pm

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
Lower Ground BMS Mark-up - 28.2.23.pdf	2023/04/20, 2:32:29 PM	George Awad	-
GP-AR-DWG-A1700 LOWER GROUND - Mark Up.pdf	2023/04/20, 2:32:28 PM	George Awad	-
KERFOOT ITC - 14.2.23.pdf	2023/04/20, 2:32:28 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:32:29 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan
Friday 26 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 26 May, 2023, 2:48:00 pm

17 North Image * Hold Point

Wednesday 29 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 2:23:31 pm

Notes

No-Pre- Sheet Required. Glazed Wall is installed to the Northern Elevation

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 2:23:31 pm

18 East Image * Hold Point

Wednesday 29 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 2:23:31 pm

Photos (3)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 2:23:24 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 2:23:21 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 2:23:31 PM

19 South Image * Hold Point

Wednesday 29 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 2:23:31 pm

Notes

No-Pre- Sheet Required. Glazed Wall is installed to the Southern Elevation

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 2:23:31 pm

20 West Image * Hold Point

Wednesday 29 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 2:23:31 pm

Photos (2)

140 - Learning Type A - Pre Sheet-ITP



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/06/30, 2:23:29 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/06/30, 2:23:27 PM

Name

Signature


Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

141 - COMMS - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > 0.08 COMMS
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 2:48:54 pm
Modified by	George Awad on Friday 30 June, 2023, 3:46:16 pm
Downloaded	Friday 30 June, 2023, 3:46:21 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
<div>1</div> <div>Mark up plan of walls to be sheeted. *</div> <div>Hold Point</div>	<div>Yes</div> <div>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 14 March, 2023, 10:45:16 am</div>
<div>Photos (1)</div> <div></div> <div>Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/03/14, 10:45:20 AM</div>	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 14 March, 2023, 11:31:34 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
15 #, Lower Ground Floor Zone 2 ITP Rough In.pdf	2023/03/14, 11:31:27 AM	George Awad	-
Lower Ground Floor Zone 2 Photos.pdf	2023/03/14, 11:31:34 AM	George Awad	-
ITC & ITR Lighting & Power Rough in Lower Ground floor 09-03-2023.docx	2023/03/14, 11:31:26 AM	George Awad	-
Lower Ground Floor Wall Mark Up.pdf	2023/03/14, 11:31:32 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 14 March, 2023, 11:31:34 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
Lower Ground Floor Zone 2 Photos.pdf	2023/03/14, 11:31:32 AM	George Awad	-
Lower Ground Floor Wall Mark Up.pdf	2023/03/14, 11:31:29 AM	George Awad	-
ITC & ITR Lighting & Power Rough in Lower Ground floor 09-03-2023.docx	2023/03/14, 11:31:27 AM	George Awad	-
15 #, Lower Ground Floor Zone 2 ITP Rough In.pdf	2023/03/14, 11:31:28 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point

George Joannou
Wednesday 29 March, 2023


Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 29 March, 2023, 2:10:38 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:40:05 pm

<p>6</p> <p>Foran - Is the drainage installed as per drawings? Attached evidence *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:40:05 pm</p>
<p>7</p> <p>Foran - Hydraulic services roughed in according to approved room layout drawings. *</p> <p>Hold Point</p>	<p>N/A</p> <p>Thursday 20 April, 2023</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:40:05 pm</p>
<p>8</p> <p>AV service roughened in according to approved room layout drawing. *</p> <p>Hold Point</p>	<p>N/A</p> <p>Thursday 20 April, 2023</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:40:05 pm</p>
<p>9</p> <p>Is fire stopping applied as per drawings? Attach evidence *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:40:05 pm</p>
<p>10</p> <p>Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:40:05 pm</p>
<p>11 ZipClad - Water Test Conducted on Facade *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:40:05 pm</p>
<p>Notes</p> <p>Not required as room is internally to building.</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:40:05 pm</p>	

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:40:04 pm

Photos (3)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/04/20, 2:40:03 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/04/20, 2:39:56 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/04/20, 2:39:59 PM

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:40:04 pm

Notes

As per partition Plan. WT22 & WT23

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:40:04 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:40:04 pm

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
GP-AR-DWG-A1700_LOWER GROUND - Mark Up.pdf	2023/04/20, 2:39:56 PM	George Awad	-
KERFOOT ITC - 14.2.23.pdf	2023/04/20, 2:40:04 PM	George Awad	-
Lower Ground BMS Mark-up - 28.2.23.pdf	2023/04/20, 2:39:57 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:40:04 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point

Hills Pan
Friday 26 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 26 May, 2023, 2:48:29 pm

17 North Image * Hold Point

Wednesday 15 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 3:42:38 pm

Photos (3)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 3:42:24 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 3:42:17 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 3:42:22 PM

18 East Image * Hold Point

Wednesday 15 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 3:42:38 pm

Photos (5)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 3:42:20 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 3:42:30 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 3:42:19 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 3:42:26 PM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/06/30, 3:42:28 PM

19 South Image * Hold Point

Wednesday 15 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 3:42:38 pm

Photos (3)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/06/30, 3:42:35 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/06/30, 3:42:31 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/06/30, 3:42:33 PM

20 West Image * Hold Point

Wednesday 15 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 30 June, 2023, 3:42:38 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/06/30, 3:42:37 PM

Name

Signature


Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

142 - Reception - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > 0.1 RECEPTION
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 2:50:06 pm
Modified by	George Awad on Thursday 07 September, 2023, 3:29:55 pm
Downloaded	Thursday 07 September, 2023, 3:29:58 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

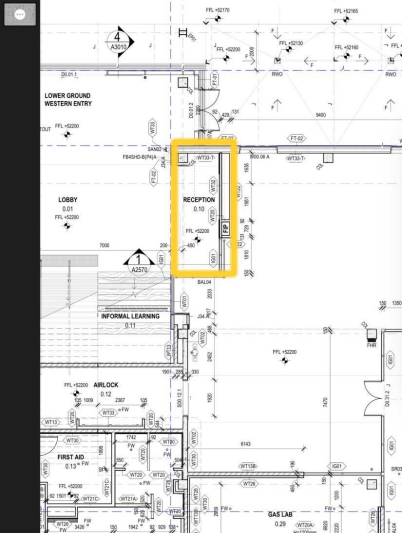Question	Response
<div>1</div> <div>Mark up plan of walls to be sheeted. *</div> <div>Hold Point</div>	<div>Yes</div> <div>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 14 March, 2023, 11:06:32 am</div>
<div>Photos (1)</div> <div></div> <div>Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/03/14, 11:06:37 AM</div>	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:40 pm

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Wall Mark UP LGF Latest (1).pdf	2023/09/07, 3:29:22 PM	George Awad	-
ITC & ITR Lighting & Power Lower Ground floor Rev.3.docx	2023/09/07, 3:29:19 PM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:40 pm

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
ITC & ITR Lighting & Power Lower Ground floor Rev.3.docx	2023/09/07, 3:29:20 PM	George Awad	-
Wall Mark UP LGF Latest (1).pdf	2023/09/07, 3:29:31 PM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Thursday 07 September, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:40 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:40 pm

6

Foran - Is the drainage installed as per drawings? Attached evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:39 pm

142 - Reception - Pre Sheet-ITP

<p>7</p> <p>Foran - Hydraulic services roughed in according to approved room layout drawings. *</p> <p>Hold Point</p>	<p>N/A</p> <p>Thursday 07 September, 2023</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:40 pm</p>
<p>8</p> <p>AV service roughened in according to approved room layout drawing. *</p> <p>Hold Point</p>	<p>As Per ITP</p> <p>Thursday 07 September, 2023</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:40 pm</p>
<p>9</p> <p>Is fire stopping applied as per drawings? Attach evidence *</p> <p>Hold Point</p>	<p>Yes</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:39 pm</p>
<p>10</p> <p>Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *</p> <p>Hold Point</p>	<p>Yes</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:39 pm</p>
<p>11 ZipClad - Water Test Conducted on Facade *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:39 pm</p>
<p>12</p> <p>Are the noggings installed as required to suit fitments etc? Attach evidence *</p> <p>Hold Point</p>	<p>Yes</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:39 pm</p>
<p>13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *</p> <p>Hold Point</p>	<p>Yes</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:39 pm</p>

142 - Reception - Pre Sheet-ITP

14

Are the mechanical works installed as per drawings?

Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:39 pm

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
KERFOOT ITC - 14.2.23.pdf	2023/09/07, 3:29:28 PM	George Awad	-
Lower Ground BMS Mark-up - 28.2.23.pdf	2023/09/07, 3:29:31 PM	George Awad	-
GP-AR~1.PDF	2023/09/07, 3:29:32 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:39 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Thursday 07 September, 2023


George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:40 pm

17 North Image * Hold Point


Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:39 pm

Photos (2)

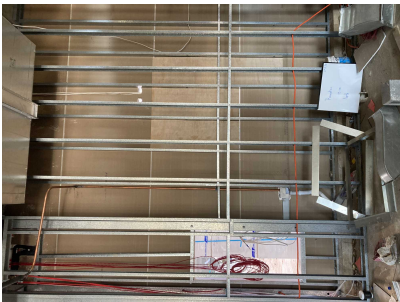

Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/07, 3:29:25 PM

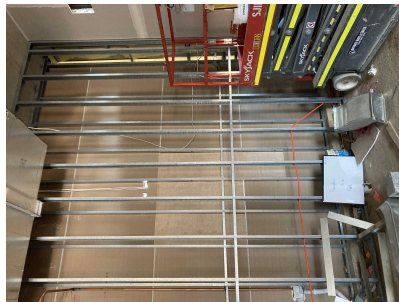

Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/09/07, 3:29:30 PM

18 East Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:29:39 pm

142 - Reception - Pre Sheet-ITP

19 South Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 3:29:38 pm

20 West Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 3:29:38 pm

Photos (1)



Captured by: **George Awad ADCO
CONSTRUCTIONS PTY LIMITED**
Date: **2023/09/07, 3:29:28 PM**

Name

Signature

Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747


143 - Airlock - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > 0.12 AIRLOCK
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 2:51:17 pm
Modified by	George Awad on Thursday 24 August, 2023, 6:27:16 am
Downloaded	Thursday 24 August, 2023, 6:27:19 am
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Mark up plan of walls to be sheeted. *	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 14 March, 2023, 10:45:52 am

Hold Point

Photos (1)

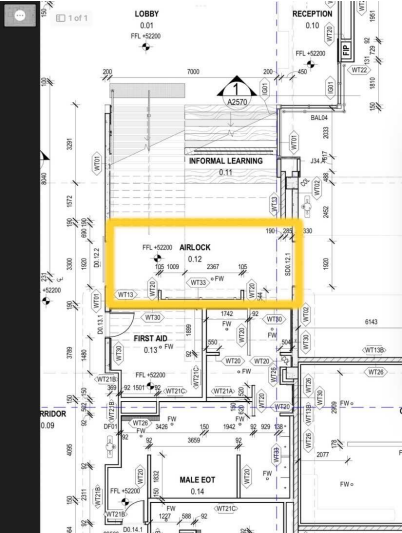

Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/03/14, 10:45:56 AM

2

Utech – Is the power installed per drawings?

Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 6:26:56 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
ITC & ITR Lighting & Power Rough in LGF.docx	2023/08/24, 6:26:52 AM	George Awad	–
Wall Mark UP LGF Latest.pdf	2023/08/24, 6:26:53 AM	George Awad	–

3

Utech – Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 6:26:55 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Wall Mark UP LGF Latest.pdf	2023/08/24, 6:26:52 AM	George Awad	–
ITC & ITR Lighting & Power Rough in LGF.docx	2023/08/24, 6:26:52 AM	George Awad	–

4

Utech – Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Thursday 24 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 6:26:56 am

5

Foran – Is the potable water installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 6:26:55 am

Photos (2)

143 - Airlock - Pre Sheet-ITP



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 6:26:36 AM**



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 6:26:42 AM**

Files (1)

Filename	Date	Attached by	Comments
lower ground amenities itp with drawing water.pdf	2023/08/24, 6:26:53 AM	George Awad	-

6 Foran – Is the drainage installed as per drawings? Attached evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:26:55 am

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 6:26:40 AM**

Files (1)

Filename	Date	Attached by	Comments
lower ground amenities itp with drawing water.pdf	2023/08/24, 6:26:53 AM	George Awad	-

7

Foran – Hydraulic services roughed in according to approved room layout drawings. *


Hold Point

Matt Foran

Thursday 24 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:26:56 am

143 - Airlock - Pre Sheet-ITP

<p>8</p> <p>AV service roughened in according to approved room layout drawing. *</p> <p>Hold Point</p>	<p>N/A</p> <p>Thursday 24 August, 2023</p> <p><i>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:26:56 am</i></p>
<p>9</p> <p>Is fire stopping applied as per drawings? Attach evidence *</p> <p>Hold Point</p>	<p>N/A</p> <p><i>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:26:55 am</i></p>
<p>10</p> <p>Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *</p> <p>Hold Point</p>	<p>N/A</p> <p><i>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:26:55 am</i></p>
<p>11</p> <p>ZipClad – Water Test Conducted on Facade *</p> <p>Hold Point</p>	<p>N/A</p> <p><i>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:26:55 am</i></p>
<p>12</p> <p>Are the noggings installed as required to suit fitments etc? Attach evidence *</p> <p>Hold Point</p>	<p>Yes</p> <p><i>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:26:55 am</i></p>
<p>Photos (1)</p>  <p>Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/08/24, 6:26:38 AM</p>	

143 - Airlock - Pre Sheet-ITP

13

Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:26:55 am

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:26:55 am

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:26:55 am

16

Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan
Thursday 24 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:26:56 am

17

North Image * Hold Point

Friday 28 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:26:54 am

18

East Image * Hold Point

Friday 28 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:26:54 am

Photos (4)



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/24, 6:26:52 AM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/24, 6:26:47 AM



Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/08/24, 6:26:45 AM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 6:26:50 AM**

19 South Image * Hold Point

Friday 28 April, 2023

*George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 6:26:54 am*

20 West Image * Hold Point

Friday 28 April, 2023

*George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
24 August, 2023, 6:26:54 am*

Name

Signature


Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

144 - First Aid - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > 0.13 FIRST AID
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 2:51:58 pm
Modified by	George Awad on Thursday 24 August, 2023, 6:37:49 am
Downloaded	Thursday 24 August, 2023, 6:37:57 am
Template	NSW TAFE IATC – Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

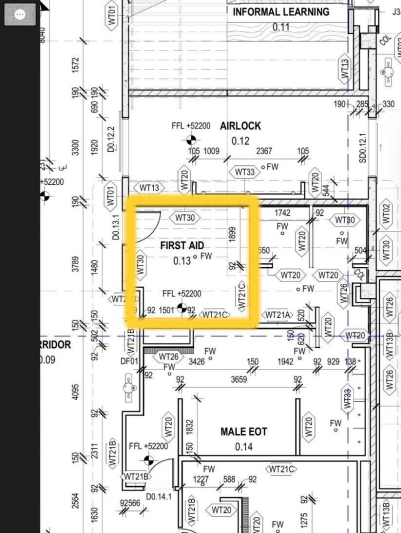Question	Response
<div>1</div> <div>Mark up plan of walls to be sheeted. *</div> <div>Hold Point</div>	<div>Yes</div> <div>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 14 March, 2023, 10:47:17 am</div>
<div>Photos (1)</div> <div></div> <div>Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/03/14, 10:47:22 AM</div>	

144 - First Aid - Pre Sheet-ITP

2

Utech – Is the power installed per drawings?

Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:27 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
ITC & ITR Lighting & Power Rough in LGF.docx	2023/08/24, 6:37:19 AM	George Awad	–
Wall Mark UP LGF Latest.pdf	2023/08/24, 6:37:24 AM	George Awad	–

3

Utech – Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:27 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Wall Mark UP LGF Latest.pdf	2023/08/24, 6:37:24 AM	George Awad	–
ITC & ITR Lighting & Power Rough in LGF.docx	2023/08/24, 6:37:19 AM	George Awad	–

4

Utech – Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Thursday 24 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:27 am

5

Foran – Is the potable water installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:27 am

Photos (0)

Files (1)

Filename	Date	Attached by	Comments
lower ground amenities itp with drawing water.pdf	2023/08/24, 6:37:23 AM	George Awad	–

144 - First Aid - Pre Sheet-ITP

6 Foran – Is the drainage installed as per drawings? Attached evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:27 am

Photos (0)

Files (1)

Filename	Date	Attached by	Comments
lower ground amenities itp with drawing water.pdf	2023/08/24, 6:37:23 AM	George Awad	–

7

Foran – Hydraulic services roughed in according to approved room layout drawings. *

Hold Point

Matt Foran

Thursday 24 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:27 am

8

AV service roughened in according to approved room layout drawing. *

Hold Point

N/A

Thursday 24 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:28 am

9

Is fire stopping applied as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:27 am

10

Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:27 am

11

ZipClad – Water Test Conducted on Facade *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:27 am

144 - First Aid - Pre Sheet-ITP

12

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:27 am

13

Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:26 am

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:26 am

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
KERFOOT ITC - 14.2.23.pdf	2023/08/24, 6:37:24 AM	George Awad	-
GP-AR~1.PDF	2023/08/24, 6:37:23 AM	George Awad	-
Lower Ground BMS Mark-up - 28.2.23.pdf	2023/08/24, 6:37:25 AM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:26 am

16

Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan
Thursday 24 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:28 am

17

North Image * Hold Point

Wednesday 31 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:26 am

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 6:37:20 AM**

18 East Image * Hold Point

Wednesday 31 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:26 am

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/08/24, 6:37:22 AM**

19 South Image * Hold Point

Wednesday 31 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:26 am

20 West Image * Hold Point

Wednesday 31 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:37:26 am

Name

Signature

Date


(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747


63 - NSW TAFE IATC - Pre Sheet ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > 0.14 MALE EOT
Status	Closed
Due Date	
Created by	Mark Zabica on Tuesday 24 January, 2023, 2:23:45 pm
Modified by	George Awad on Friday 07 July, 2023, 12:52:34 pm
Downloaded	Friday 07 July, 2023, 12:52:41 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Is the power installed per drawings? Attach evidence * Hold Point	Yes <i>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 03 March, 2023, 1:18:22 pm</i>
Notes <i>UF mark not installed</i> <i>Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Monday 30 January, 2023, 2:33:42 pm</i>	
Photos (5)	

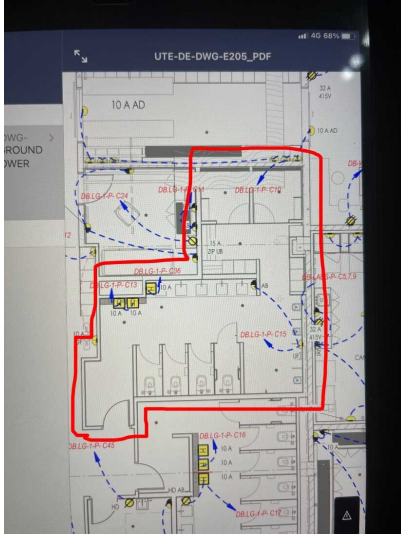

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/01/30, 2:42:49 PM**

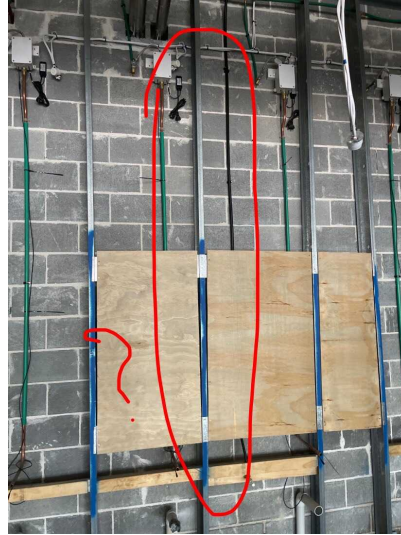

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/01/30, 2:42:09 PM**



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/01/30, 2:42:45 PM**



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/01/30, 2:42:47 PM**



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/01/30, 2:42:43 PM**

2

Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 03 March, 2023, 1:18:23 pm

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
13 #. Lower Ground Floor Amenities ITP Rough In.pdf	2023/03/03, 1:18:20 PM	George Awad	-
ITC & ITR Lighting & Power Rough in Lower Ground floor 02-03-2023.docx	2023/03/03, 1:18:20 PM	George Awad	-
LGF Amenities 02-03-2023 Photos.pdf	2023/03/03, 1:18:22 PM	George Awad	-

3


Is the potable water installed as per drawings? Attach evidence *

Hold Point

Yes

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Monday 30 January, 2023, 2:36:36 pm

Photos (5)

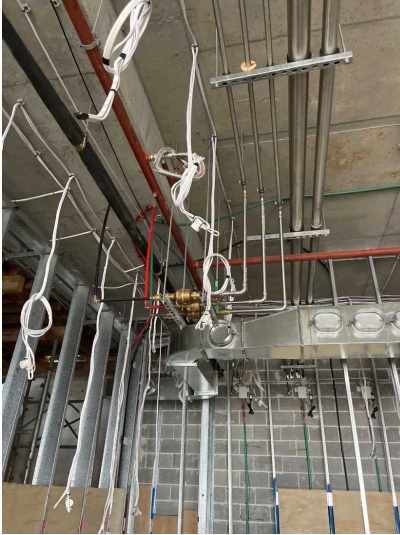

Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 4:13:53 PM




Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 5:41:27 PM



Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 5:41:25 PM



Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 4:13:53 PM

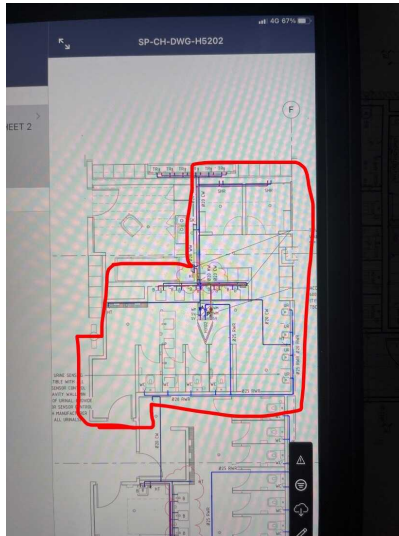

Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 2:42:41 PM

Files (2)

Filename	Date	Attached by	Comments
lower ground amenities itp with drawing water.pdf	2023/04/20, 2:43:25 PM	George Awad	-
lower ground amenities itp with drawing water.pdf	2023/03/06, 1:30:50 PM	George Awad	-

4

Is the drainage installed as per drawings? Attached evidence *

Hold Point


Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
20 April, 2023, 2:43:26 pm


Photos (5)



Captured by: Mark Zabica ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 4:13:58 PM

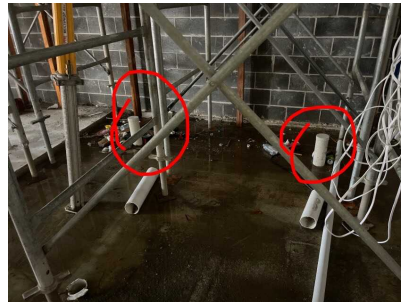

Captured by: Mark Zabica ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 5:41:22 PM

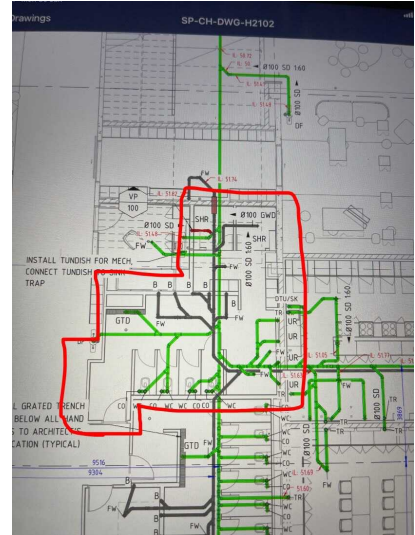

Captured by: Mark Zabica ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 4:13:54 PM



Captured by: Mark Zabica ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 4:13:56 PM



Captured by: Mark Zabica ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 4:13:57 PM

Files (2)

Filename	Date	Attached by	Comments
lower ground amenities itp with drawing water.pdf	2023/04/20, 2:43:26 PM	George Awad	-
lower ground amenities itp with drawing water.pdf	2023/03/06, 1:30:50 PM	George Awad	-

5

Is fire stopping applied as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
20 April, 2023, 2:43:26 pm

6

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point


Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
20 April, 2023, 2:43:26 pm

Photos (6)




Captured by: Mark Zabica ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 5:41:24 PM

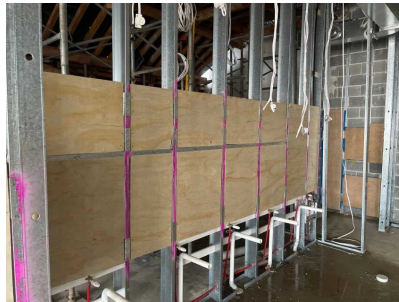

Captured by: Mark Zabica ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 5:41:20 PM




Captured by: Mark Zabica ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 5:41:21 PM

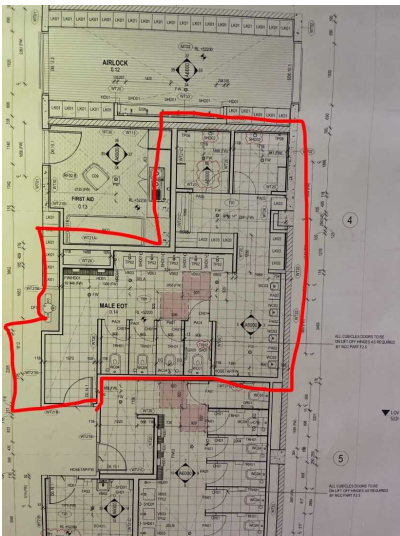

Captured by: Mark Zabica ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 5:41:22 PM



Captured by: Mark Zabica ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 5:41:25 PM

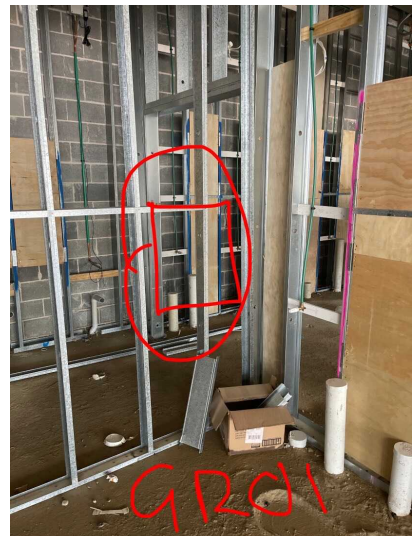

Captured by: Mark Zabica ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 5:41:26 PM

7 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

No

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:43:26 pm

8


Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

No

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:43:26 pm


Photos (3)

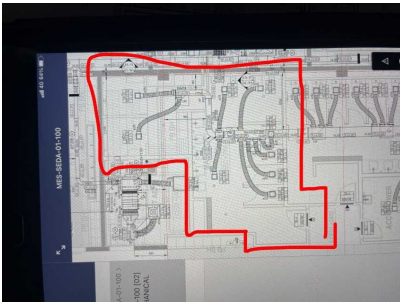

Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 5:41:20 PM



Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 5:41:26 PM

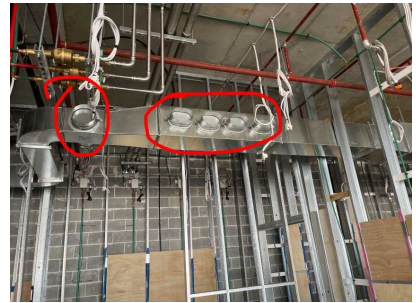

Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 5:41:27 PM

9


Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:43:26 pm

Photos (1)

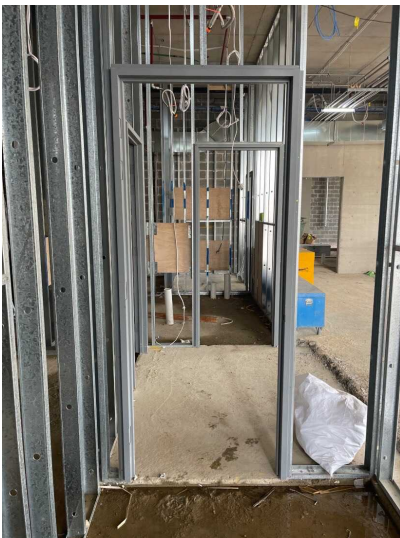

Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 5:41:28 PM

10 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan
Friday 26 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 26 May, 2023, 2:49:09 pm

11 North Image * Hold Point

Tuesday 28 February, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 07 July, 2023, 12:51:59 pm

Photos (1)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/07/07, 12:51:58 PM

12 East Image * Hold Point

Tuesday 28 February, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 07 July, 2023, 12:51:59 pm

Photos (1)




Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/07/07, 12:51:55 PM

13 South Image * Hold Point

Tuesday 28 February, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 07 July, 2023, 12:51:59 pm

Photos (1)

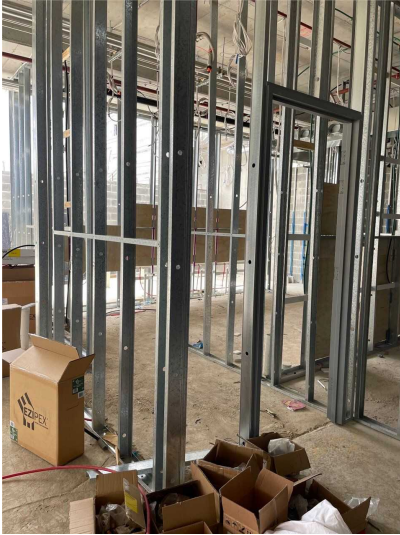

Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/07, 12:51:57 PM

14 West Image * Hold Point

Tuesday 28 February, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 07 July, 2023, 12:51:59 pm

Photos (3)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/07, 12:51:57 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/07, 12:51:55 PM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/07, 12:51:59 PM

Name

Signature

Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

64 - NSW TAFE IATC - Pre Sheet ITP


Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > 0.15 FEMALE EOT
Status	Closed
Due Date	
Created by	Mark Zabica on Tuesday 24 January, 2023, 2:24:06 pm
Modified by	George Awad on Wednesday 12 July, 2023, 3:18:29 pm
Downloaded	Wednesday 12 July, 2023, 3:18:55 pm
Template	NSW TAFE IATC – Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Is the power installed per drawings? Attach evidence * Hold Point	Yes Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Monday 30 January, 2023, 1:57:46 pm


Photos (4)



Captured by: Mark Zabica ADCO

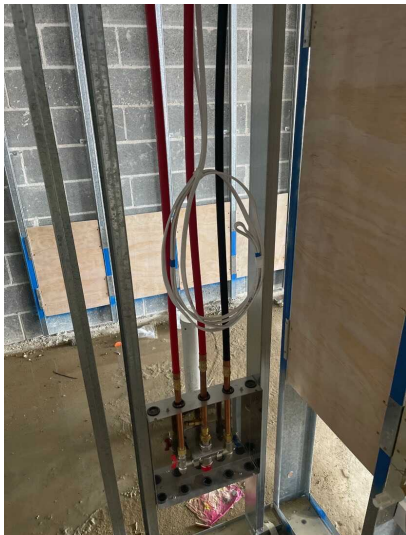

Captured by: Mark Zabica ADCO

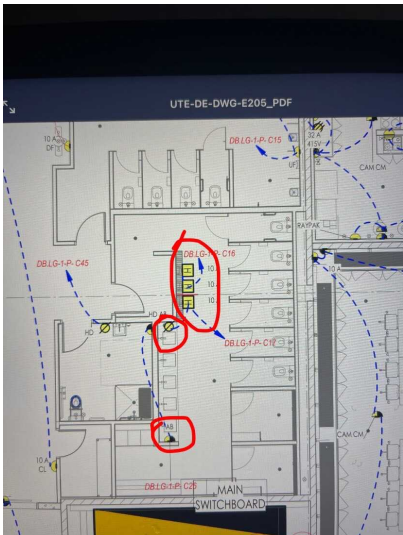

Captured by: Mark Zabica ADCO

64 - NSW TAFE IATC - Pre Sheet ITP

CONSTRUCTIONS PTY LIMITED

Date: 2023/01/30, 2:00:17 PM



Captured by: Mark Zabica ADCO

CONSTRUCTIONS PTY LIMITED

Date: 2023/01/30, 2:00:10 PM

CONSTRUCTIONS PTY LIMITED

Date: 2023/01/30, 2:00:12 PM

CONSTRUCTIONS PTY LIMITED

Date: 2023/01/30, 2:00:11 PM

2

Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 03 March, 2023, 1:19:20 pm

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
ITC & ITR Lighting & Power Rough in Lower Ground floor 02-03-2023.docx	2023/03/03, 1:19:19 PM	George Awad	-
LGF Amenities 02-03-2023 Photos.pdf	2023/03/03, 1:19:20 PM	George Awad	-
13 #, Lower Ground Floor Amenities ITP Rough In.pdf	2023/03/03, 1:19:19 PM	George Awad	-

3

Is the potable water installed as per drawings? Attach evidence *

Hold Point

Yes


George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:46:02 pm

Notes


HT when walking in not installed

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Monday 30 January, 2023, 2:08:09 pm

Photos (9)

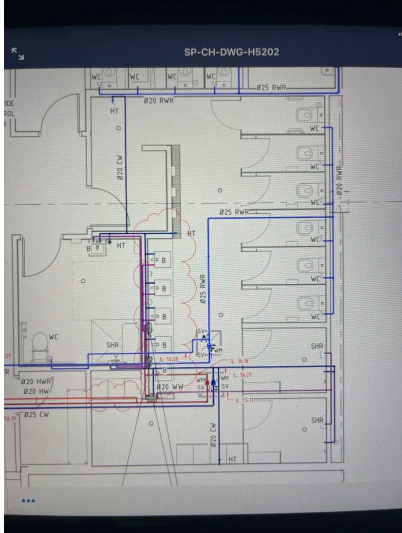


Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/01/30, 2:06:40 PM**

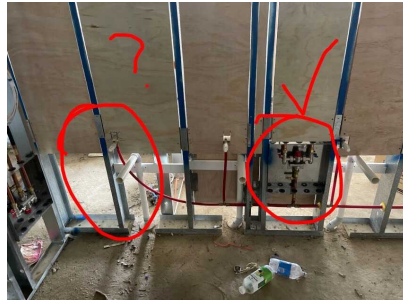


Captured by: Mark Zabica ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 2:08:25 PM




Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/01/30, 2:07:41 PM**

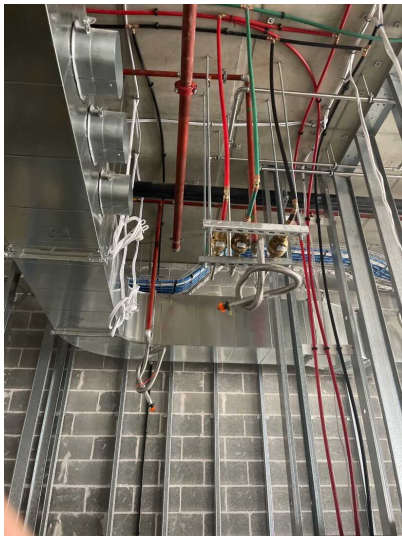

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/01/30, 2:07:40 PM**

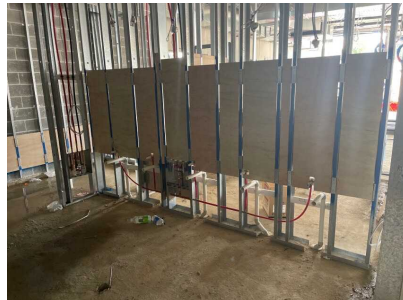


Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/01/30, 2:07:38 PM**

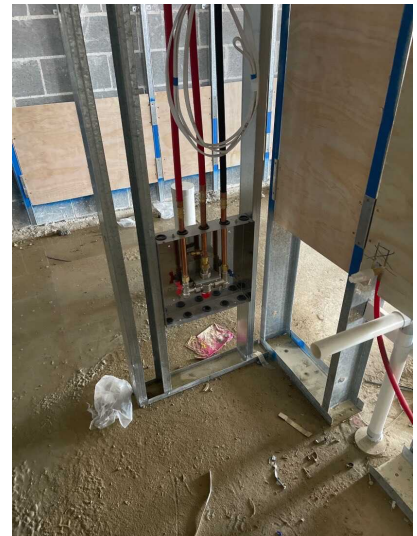

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/01/30, 2:07:19 PM**



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/01/30, 2:07:42 PM**

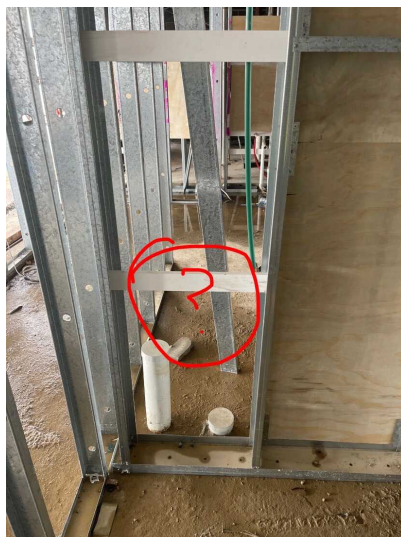

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/01/30, 2:06:54 PM**



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:06:42 PM

Files (2)

Filename	Date	Attached by	Comments
lower ground amenities itp with drawing water.pdf	2023/04/20, 2:46:01 PM	George Awad	-
lower ground amenities itp with drawing water.pdf	2023/03/06, 1:46:16 PM	George Awad	-

4

Is the drainage installed as per drawings?


Attached evidence *

Hold Point

Yes

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Monday 30 January, 2023, 2:18:00 pm


Photos (8)

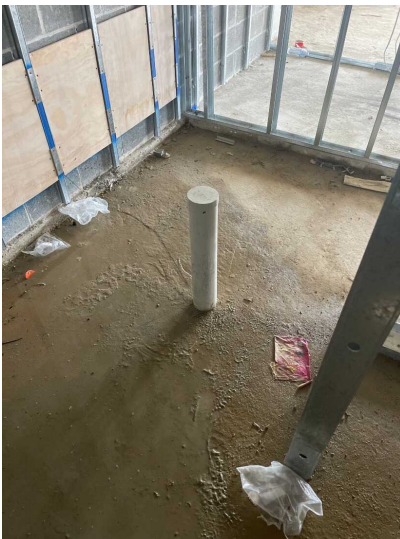

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:41:11 PM



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:39:44 PM

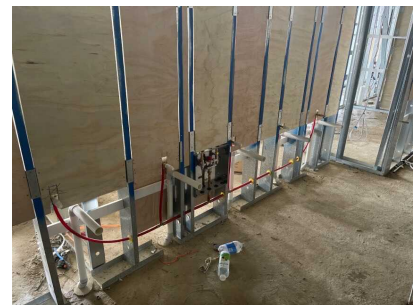


Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:41:05 PM



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:41:10 PM




Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:39:42 PM

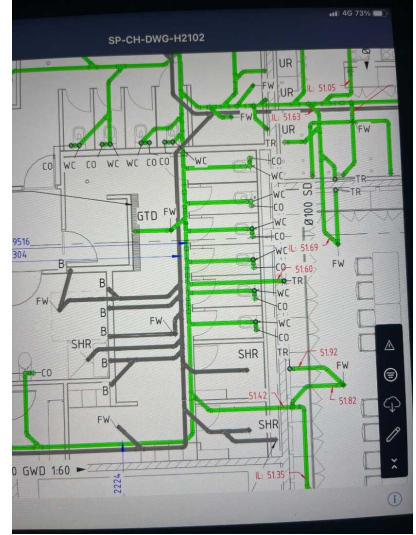

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:39:44 PM



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:36:40 PM

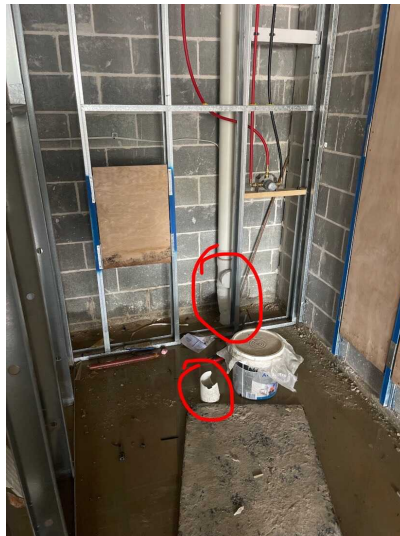

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:39:43 PM

Files (2)

Filename	Date	Attached by	Comments
lower ground amenities itp with drawing water.pdf	2023/04/20, 2:46:01 PM	George Awad	-
lower ground amenities itp with drawing water.pdf	2023/03/06, 1:46:15 PM	George Awad	-

5

Is fire stopping applied as per drawings? Attach evidence *

Hold Point

No

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Monday 30 January, 2023, 2:18:01 pm

6

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

No

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Monday 30 January, 2023, 2:18:01 pm

Notes

Plywood for toilets

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Monday 30 January, 2023, 2:18:01 pm

Photos (9)




Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 2:40:56 PM




Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 2:41:00 PM




Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 2:41:03 PM

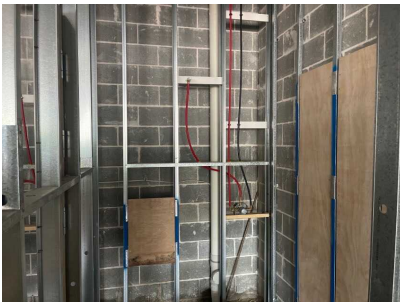


Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 2:40:58 PM

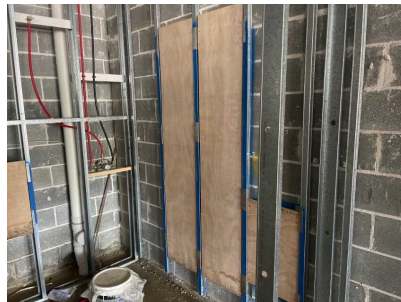

Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 2:42:37 PM

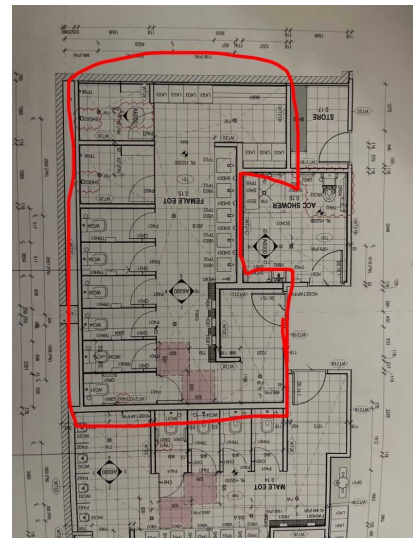

Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 2:41:09 PM

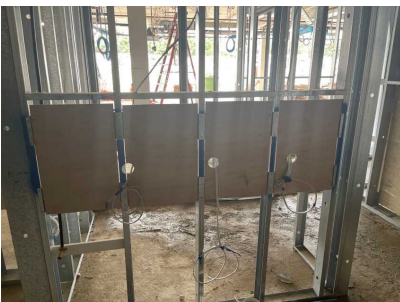

Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 2:41:09 PM



Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/30, 2:40:59 PM



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:38:54 PM

7

Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

No

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:46:02 pm

8


Are the mechanical works installed as per drawings? Attach evidence *

Hold Point


No

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:46:02 pm

Photos (5)

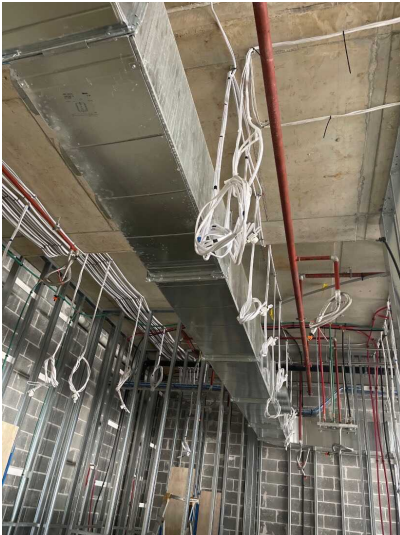


Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:42:52 PM

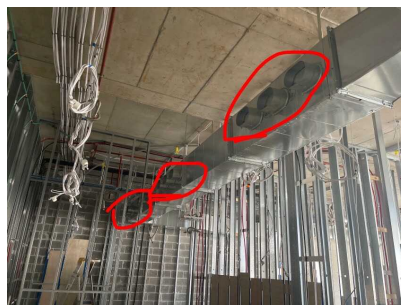


Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:42:54 PM



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:42:53 PM

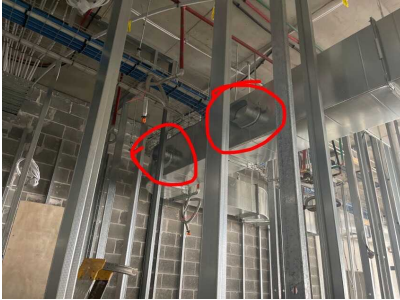

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:42:53 PM

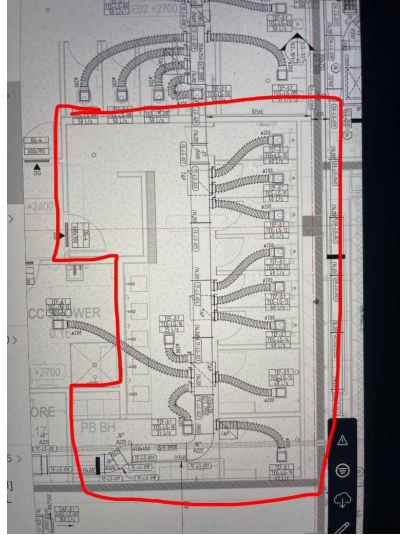

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:42:54 PM

9


Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 2:46:02 pm

Photos (1)

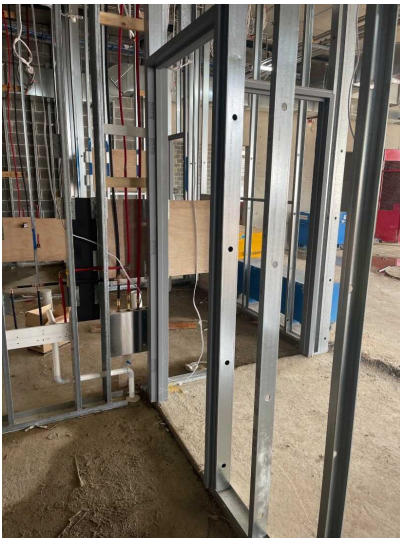

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/30, 2:42:49 PM

10

Dunrite Accepts walls are ready for sheet *

Hold Point

Hills Pan
Friday 26 May, 2023


George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 26 May, 2023, 2:49:30 pm

11 North Image * Hold Point

Tuesday 28 February, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:18:16 pm

Photos (1)

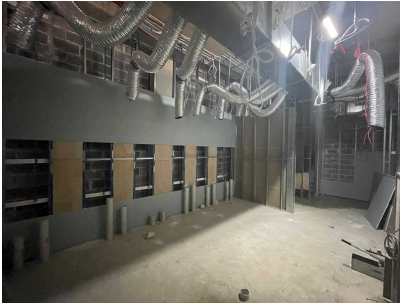


Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/07/12, 3:18:14 PM

12 East Image * Hold Point

Tuesday 28 February, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:18:16 pm

Photos (1)

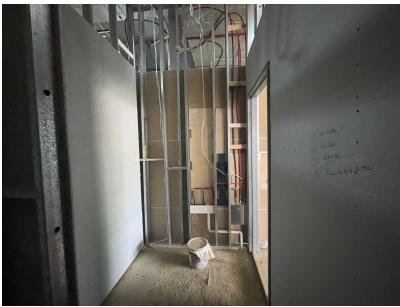


Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/07/12, 3:18:16 PM

13 South Image * Hold Point


Tuesday 28 February, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:18:16 pm

Photos (2)

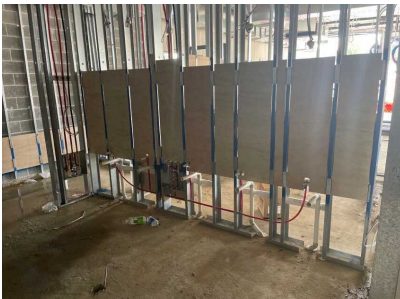

Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/07/12, 3:18:11 PM

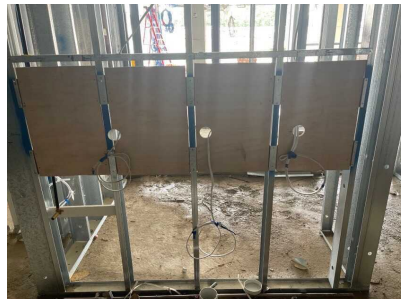

Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/07/12, 3:18:11 PM

14 West Image * Hold Point

Tuesday 28 February, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:18:16 pm

Photos (1)



Captured by: **George Awad ADCO**
CONSTRUCTIONS PTY LIMITED
Date: **2023/07/12, 3:18:12 PM**

Name

Signature

Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY


TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

65 - ACC Shower - Pre Sheet-ITP


Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > 0.16 ACC SHOWER
Status	Closed
Due Date	
Created by	Mark Zabica on Tuesday 24 January, 2023, 2:24:21 pm
Modified by	George Awad on Wednesday 12 July, 2023, 3:21:53 pm
Downloaded	Wednesday 12 July, 2023, 3:21:57 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Is the power installed per drawings? Attach evidence * Hold Point	Yes <i>Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 3:01:08 pm</i>
Notes <i>Portion seems incomplete</i> <i>Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 3:01:08 pm</i>	
Photos (3)	


65 - ACC Shower - Pre Sheet-ITP

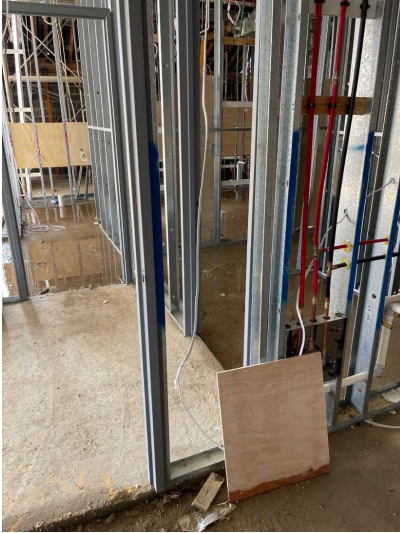

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 3:01:10 PM

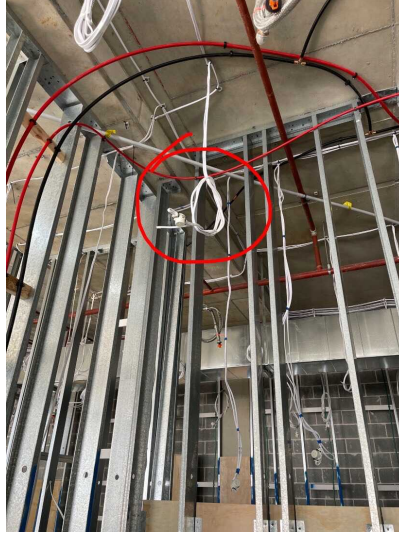

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 3:01:39 PM

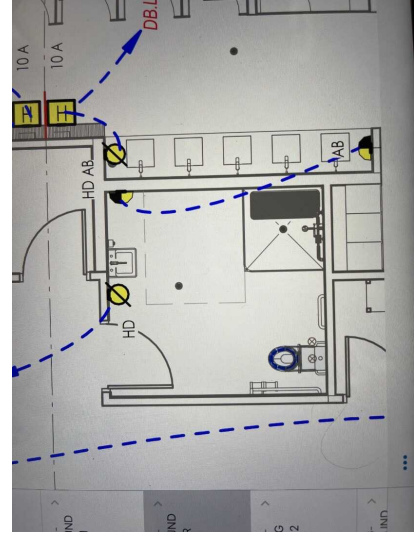

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 3:01:38 PM


2

Are the communications and security cabling installed as per the drawings? Attach evidence *
Hold Point


Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 03 March, 2023, 1:20:50 pm

Photos (3)

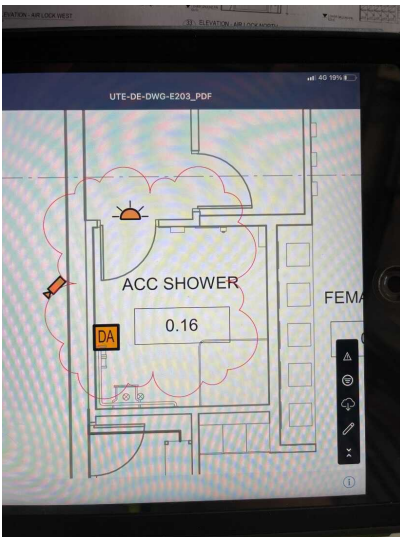

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 3:03:11 PM

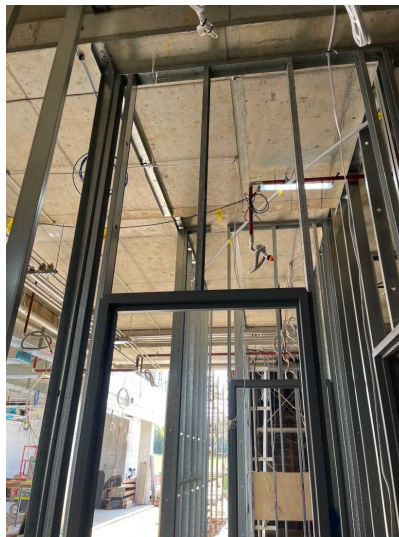

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 3:03:13 PM



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 3:03:13 PM

Files (3)

Filename	Date	Attached by	Comments
LGF Amenities 02-03-2023 Photos.pdf	2023/03/03, 1:20:50 PM	George Awad	-
13 #, Lower Ground Floor Amenities ITP Rough In.pdf	2023/03/03, 1:20:49 PM	George Awad	-
ITC & ITR Lighting & Power Rough in Lower Ground floor 02-03-2023.docx	2023/03/03, 1:20:48 PM	George Awad	-

3

Is the potable water installed as per drawings? Attach evidence *

Yes

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 3:07:48 pm


Hold Point

Notes


Potential incorrect placement of basin pipework

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 3:07:48 pm

Photos (4)

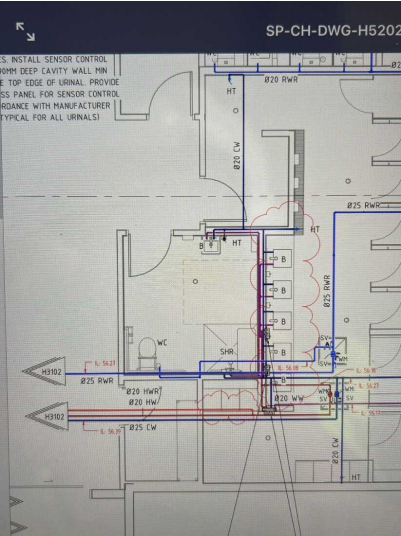

Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/24, 3:07:54 PM

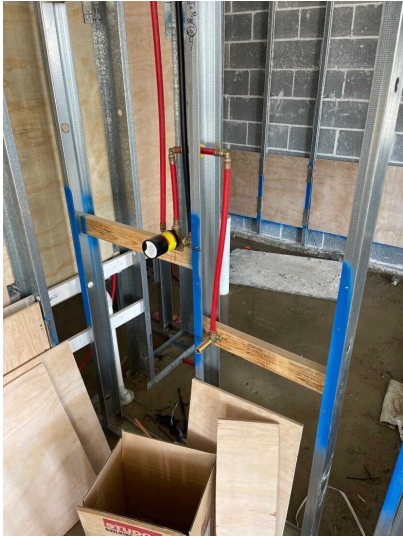

Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/24, 3:07:55 PM



Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/24, 3:07:56 PM



Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/24, 3:08:04 PM

Files (2)

Filename	Date	Attached by	Comments
lower ground amenities itp with drawing water.pdf	2023/03/06, 1:48:15 PM	George Awad	-
lower ground amenities itp with drawing water.pdf	2023/04/20, 4:16:00 PM	George Awad	-


4

Is the drainage installed as per drawings? Attached evidence *
Hold Point

Yes

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 3:11:32 pm

Photos (2)

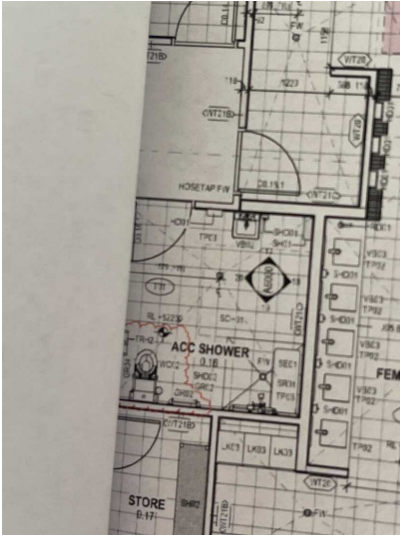

Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/24, 3:11:37 PM



Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/24, 3:11:51 PM

Files (2)

Filename	Date	Attached by	Comments
lower ground amenities itp with drawing water.pdf	2023/04/20, 4:16:01 PM	George Awad	-
lower ground amenities itp with drawing water.pdf	2023/03/06, 1:48:14 PM	George Awad	-

5

Is fire stopping applied as per drawings? Attach evidence *
Hold Point

N/A

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 3:11:32 pm

6


Are the noggings installed as required to suit fitments etc? Attach evidence *
Hold Point

Yes


George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:16:01 pm

Photos (8)

65 - ACC Shower - Pre Sheet-ITP

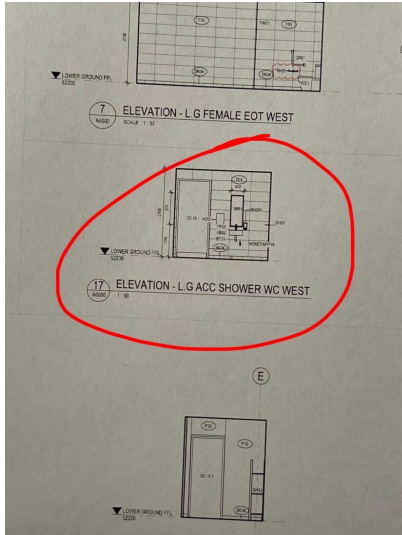


Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 3:11:38 PM

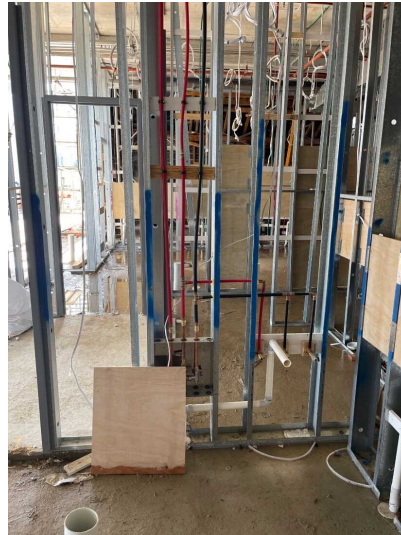


Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 3:11:39 PM



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 3:11:50 PM

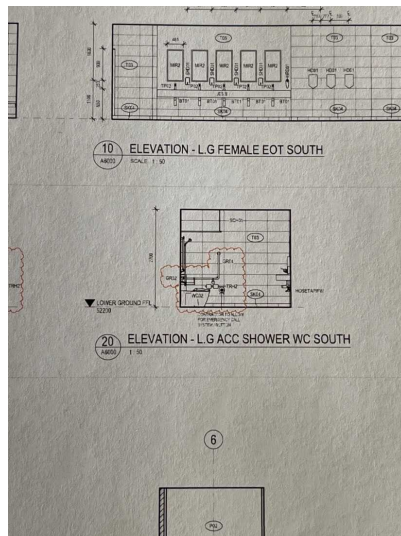


Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 3:11:57 PM

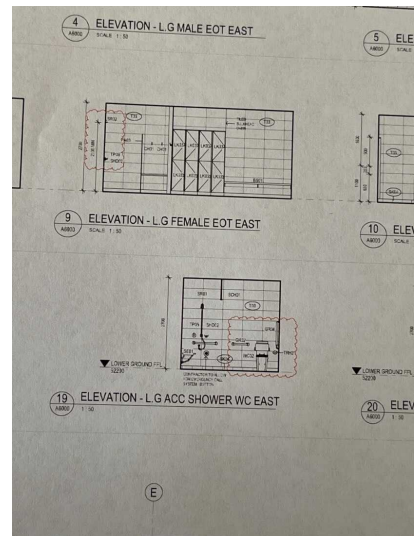

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 3:11:58 PM



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 3:11:54 PM

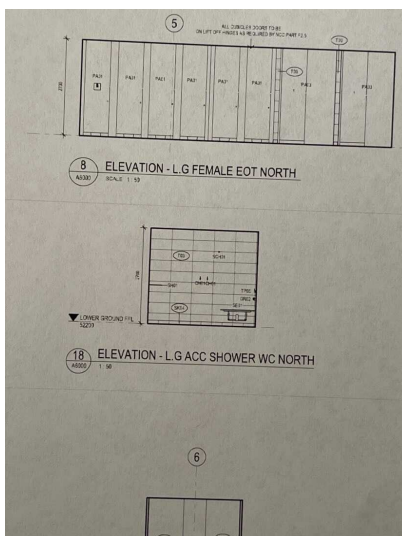

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 3:12:01 PM



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 3:12:02 PM

65 - ACC Shower - Pre Sheet-ITP

7 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

N/A

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 3:12:45 pm

8

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

N/A

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 3:12:45 pm

9


Door Frames installed in plumb and have correct allowance for finish *

Hold Point


Yes

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 3:12:46 pm

Photos (2)

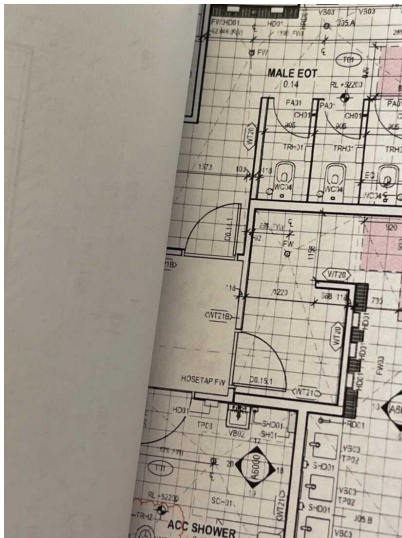

Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/24, 3:12:47 PM

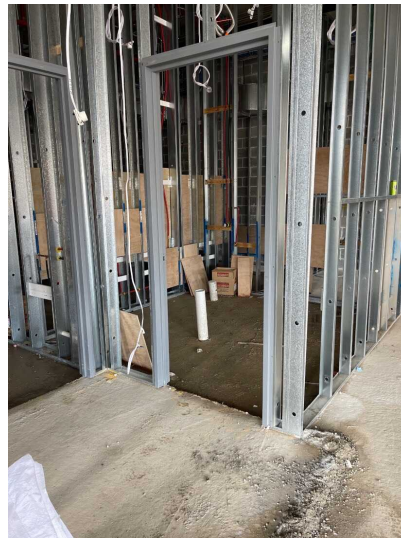

Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/24, 3:12:48 PM

10 Dunrite Accepts walls are ready for sheet *

Hold Point

Hills Pan
Friday 26 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 26 May, 2023, 2:49:52 pm

11 North Image * Hold Point

Tuesday 28 February, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:21:43 pm

Photos (1)




Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/12, 3:21:36 PM

12 East Image * Hold Point

Tuesday 28 February, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:21:43 pm

Photos (1)

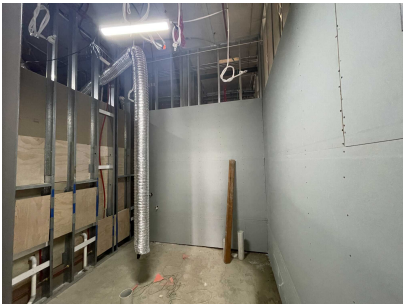

Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/12, 3:21:40 PM

13 South Image * Hold Point

Tuesday 28 February, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:21:43 pm

Photos (1)




Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/12, 3:21:36 PM


14 West Image * Hold Point

Tuesday 28 February, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:21:42 pm

Photos (2)

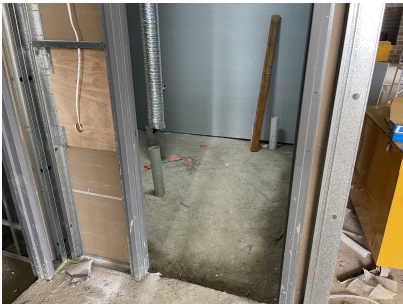

Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/12, 3:21:42 PM

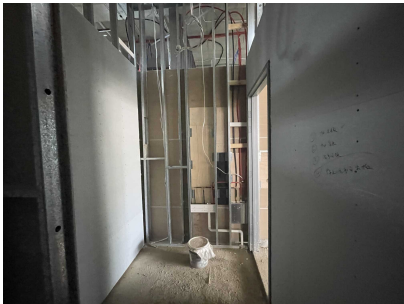

Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/12, 3:21:38 PM

Name

Signature

Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY


TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

66 - Store - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > 0.17 STORE
Status	Closed
Due Date	
Created by	Mark Zabica on Tuesday 24 January, 2023, 2:25:49 pm
Modified by	George Awad on Wednesday 12 July, 2023, 3:24:41 pm
Downloaded	Wednesday 12 July, 2023, 3:24:57 pm
Template	NSW TAFE IATC – Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

Question	Response
1 Is the power installed per drawings? Attach evidence * Hold Point	Yes <i>Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 2:49:47 pm</i>

Photos (2)

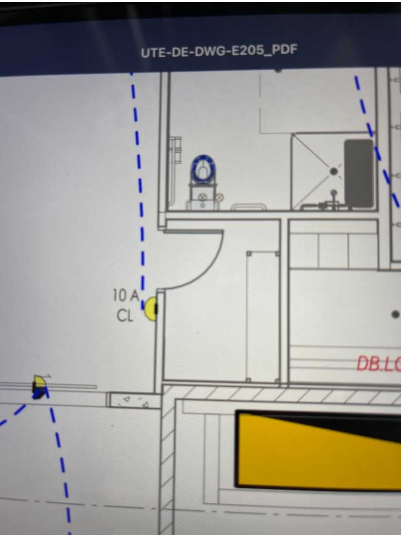

Captured by: Mark Zabica ADCO



Captured by: Mark Zabica ADCO

66 - Store - Pre Sheet-ITP

CONSTRUCTIONS PTY LIMITED
Date: 2023/01/24, 2:49:50 PM

CONSTRUCTIONS PTY LIMITED
Date: 2023/01/24, 2:49:52 PM

Files (3)

Filename	Date	Attached by	Comments
LGF Amenities 02-03-2023 Photos.pdf	2023/03/03, 1:26:28 PM	George Awad	-
13 #, Lower Ground Floor Amenities ITP Rough In.pdf	2023/03/03, 1:26:28 PM	George Awad	-
ITC & ITR Lighting & Power Rough in Lower Ground floor 02-03-2023.docx	2023/03/03, 1:26:27 PM	George Awad	-

2

Are the communications and security cabling installed as per the drawings? Attach evidence *
Hold Point

No


Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 2:49:47 pm

Notes


Card reader not installed

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 2:49:47 pm

Photos (2)

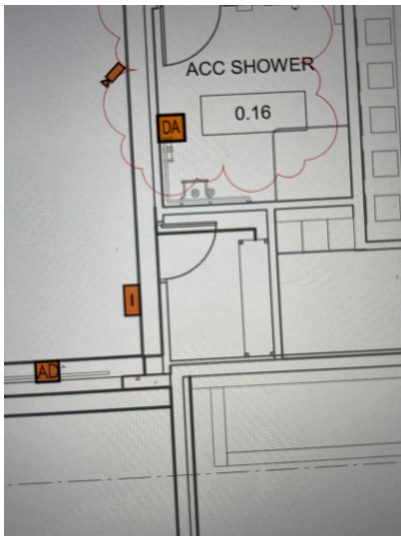

Captured by: Mark Zabica ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/01/24, 2:49:51 PM

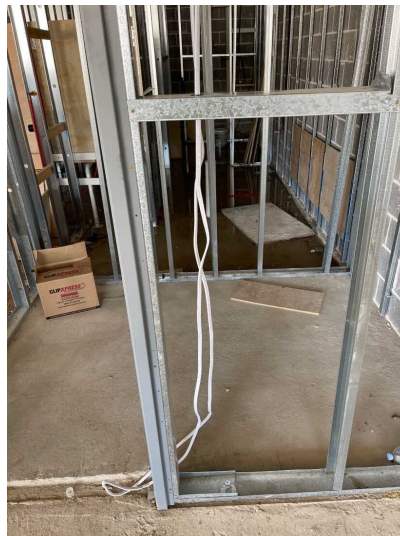

Captured by: Mark Zabica ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/01/24, 2:49:53 PM

3

Is the potable water installed as per drawings?
Attach evidence *
Hold Point

N/A

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 2:49:48 pm

4

Is the drainage installed as per drawings?

Attached evidence *

Hold Point

N/A

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 2:49:48 pm

5

Is fire stopping applied as per drawings? Attach evidence *

Hold Point

N/A

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 2:49:48 pm

6

Are the noggings installed as required to suit fitments etc? Attach evidence *

Hold Point

No


Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 2:56:14 pm

Notes

SH02 to be wall fixed

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 2:56:14 pm


Photos (3)

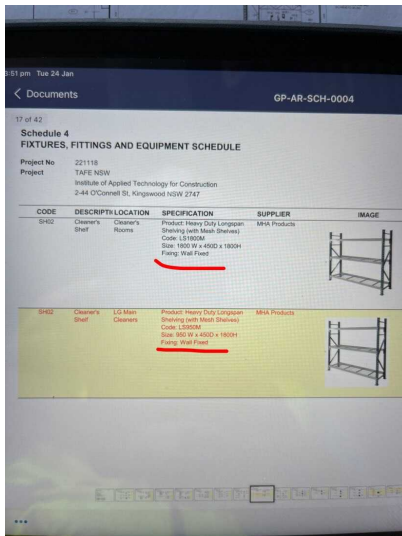

Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/24, 2:56:17 PM



Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/24, 2:56:18 PM

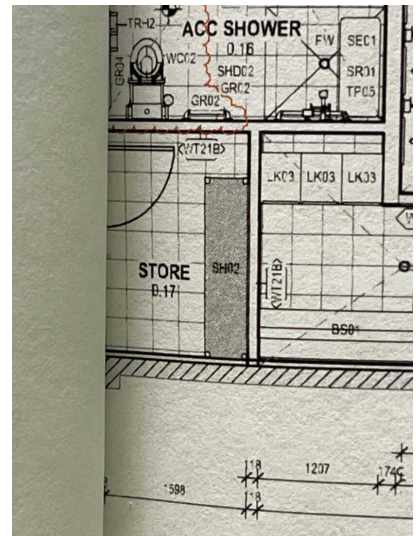

Captured by: Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED
Date: 2023/01/24, 2:56:18 PM

7

Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

N/A

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 2:56:14 pm

8

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 2:56:14 pm


Photos (4)




Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 2:56:23 PM



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 2:56:26 PM

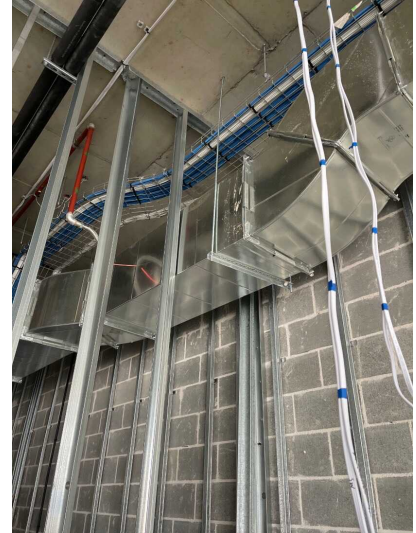

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 2:56:25 PM

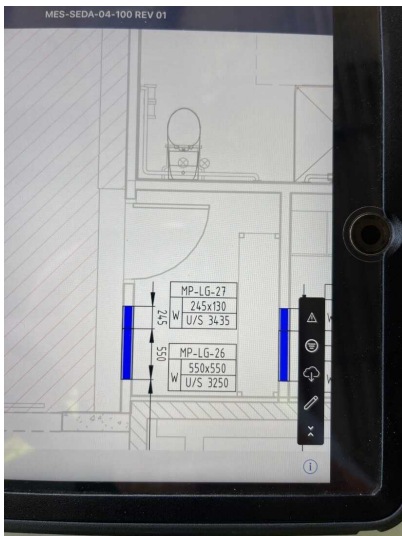

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 2:56:24 PM

9

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 24 January, 2023, 2:56:58 pm

Photos (2)

66 - Store - Pre Sheet-ITP



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 2:57:08 PM



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/01/24, 2:57:09 PM

10

Dunrite Accepts walls are ready for sheet *
Hold Point

Hills Pan
Friday 26 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 26 May, 2023, 2:50:14 pm

11 North Image * **Hold Point**

Tuesday 28 February, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:24:15 pm

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/12, 3:24:14 PM

12 East Image * **Hold Point**

Tuesday 28 February, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:24:15 pm

13 South Image * **Hold Point**

Tuesday 28 February, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:24:15 pm

Photos (1)




Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/07/12, 3:24:13 PM**

14 West Image * Hold Point

Tuesday 28 February, 2023
George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:24:15 pm

Photos (1)

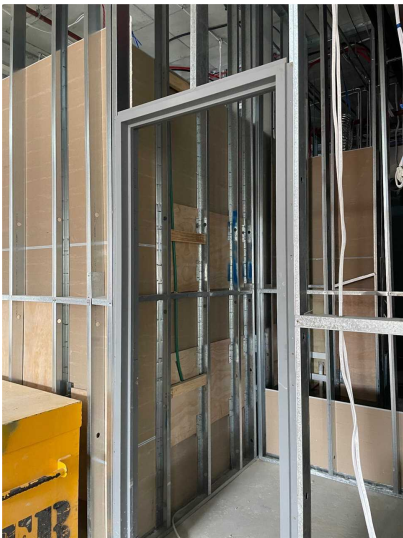

Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: **2023/07/12, 3:24:11 PM**

Name

Signature


Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

151 - Breakout/Lockers - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > BREAKOUT/LOCKERS
Status	Closed
Due Date	
Created by	George Awad on Monday 06 March, 2023, 10:13:19 am
Modified by	George Awad on Monday 10 July, 2023, 7:47:01 am
Downloaded	Monday 10 July, 2023, 7:48:09 am
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

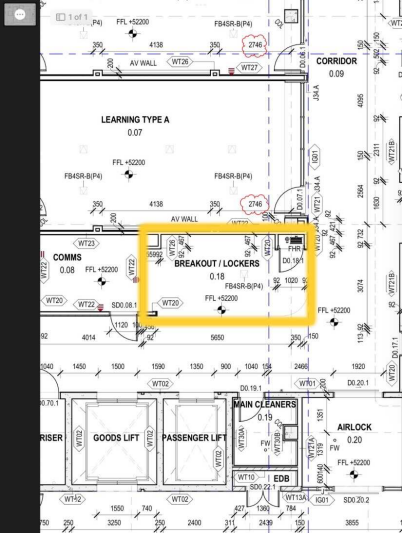Question	Response
<div>1</div> <div>Mark up plan of walls to be sheeted. *</div> <div>Hold Point</div>	<div>Yes</div> <div>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 14 March, 2023, 11:11:17 am</div>
<div>Photos (1)</div> <div></div> <div>Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/03/14, 11:11:22 AM</div>	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday
14 March, 2023, 11:32:27 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
ITC & ITR Lighting & Power Rough in Lower Ground floor 09-03-2023.docx	2023/03/14, 11:32:19 AM	George Awad	-
15 #, Lower Ground Floor Zone 2 ITP Rough In.pdf	2023/03/14, 11:32:21 AM	George Awad	-
Lower Ground Floor Zone 2 Photos.pdf	2023/03/14, 11:32:23 AM	George Awad	-
Lower Ground Floor Wall Mark Up.pdf	2023/03/14, 11:32:27 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday
14 March, 2023, 11:32:27 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
Lower Ground Floor Wall Mark Up.pdf	2023/03/14, 11:32:23 AM	George Awad	-
15 #, Lower Ground Floor Zone 2 ITP Rough In.pdf	2023/03/14, 11:32:20 AM	George Awad	-
ITC & ITR Lighting & Power Rough in Lower Ground floor 09-03-2023.docx	2023/03/14, 11:32:20 AM	George Awad	-
Lower Ground Floor Zone 2 Photos.pdf	2023/03/14, 11:32:25 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Thursday 20 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
20 April, 2023, 4:39:29 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
20 April, 2023, 4:39:28 pm

151 - Breakout/Lockers - Pre Sheet-ITP

<p>6</p> <p>Foran - Is the drainage installed as per drawings? Attached evidence *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:39:28 pm</p>
<p>7</p> <p>Foran - Hydraulic services roughed in according to approved room layout drawings. *</p> <p>Hold Point</p>	<p>N/A</p> <p>Thursday 20 April, 2023</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:39:29 pm</p>
<p>8</p> <p>AV service roughened in according to approved room layout drawing. *</p> <p>Hold Point</p>	<p>N/A</p> <p>Thursday 20 April, 2023</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:39:29 pm</p>
<p>9</p> <p>Is fire stopping applied as per drawings? Attach evidence *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:39:28 pm</p>
<p>10</p> <p>Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:39:28 pm</p>
<p>11 ZipClad - Water Test Conducted on Facade *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:39:28 pm</p>
<p>12</p> <p>Are the noggings installed as required to suit fitments etc? Attach evidence *</p> <p>Hold Point</p>	<p>Yes</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:39:28 pm</p>

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:39:28 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:39:28 pm

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
KERFOOT ITC - 14.2.23.pdf	2023/04/20, 4:39:26 PM	George Awad	-
GP-AR-DWG-A1700_LOWER GROUND - Mark Up.pdf	2023/04/20, 4:39:27 PM	George Awad	-
Lower Ground BMS Mark-up - 28.2.23.pdf	2023/04/20, 4:39:27 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:39:28 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan
Monday 10 July, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 7:46:52 am

17 North Image * Hold Point

Tuesday 28 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 7:46:52 am

Notes

No partition wall on the northern elevation of space

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 7:46:52 am

18 East Image * Hold Point

Tuesday 28 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 7:46:52 am

Notes

No partition wall on the eastern elevation of space

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 7:46:52 am

19 South Image * Hold Point

Tuesday 28 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 7:46:52 am

Photos (2)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 7:46:41 AM



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 7:46:51 AM

20 West Image * Hold Point

Tuesday 28 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Monday 10 July, 2023, 7:46:52 am

Photos (1)



Captured by: **George Awad ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/07/10, 7:46:40 AM

Name

Signature

Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

145 - Main Cleaners - Pre Sheet-ITP

Details

Project

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

Organization

ADCO CONSTRUCTIONS PTY LIMITED

Location

TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > 0.19 MAIN CLEANERS

Status

Closed

Due Date

Created by

George Awad on Friday 03 March, 2023, 2:52:37 pm

Modified by

George Awad on Wednesday 12 July, 2023, 3:27:33 pm

Downloaded

Wednesday 12 July, 2023, 3:27:38 pm

Template

NSW TAFE IATC – Pre Sheet ITP

Description

Date: Room / Location:

Progress

100%

Question

Response

1

Mark up plan of walls to be sheeted. *

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 14 March, 2023, 10:48:18 am

Hold Point

Photos (1)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/03/14, 10:48:22 AM

2

Utech - Is the power installed per drawings?

Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday
14 March, 2023, 11:35:06 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
ITC & ITR Lighting & Power Rough in Lower Ground floor 09-03-2023.docx	2023/03/14, 11:34:57 AM	George Awad	-
Lower Ground Floor Wall Mark Up.pdf	2023/03/14, 11:35:00 AM	George Awad	-
Lower Ground Floor Zone 2 Photos.pdf	2023/03/14, 11:35:03 AM	George Awad	-
15 #, Lower Ground Floor Zone 2 ITP Rough In.pdf	2023/03/14, 11:34:59 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday
14 March, 2023, 11:35:06 am

Photos (0)

Files (4)

Filename	Date	Attached by	Comments
Lower Ground Floor Zone 2 Photos.pdf	2023/03/14, 11:35:06 AM	George Awad	-
Lower Ground Floor Wall Mark Up.pdf	2023/03/14, 11:35:01 AM	George Awad	-
ITC & ITR Lighting & Power Rough in Lower Ground floor 09-03-2023.docx	2023/03/14, 11:34:58 AM	George Awad	-
15 #, Lower Ground Floor Zone 2 ITP Rough In.pdf	2023/03/14, 11:34:58 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point

George Joannou
Thursday 20 April, 2023George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
20 April, 2023, 4:34:14 pm

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
20 April, 2023, 4:34:14 pm

145 - Main Cleaners - Pre Sheet-ITP

6	Foran – Is the drainage installed as per drawings? Attached evidence *	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:34:14 pm
	Hold Point	
7	Foran – Hydraulic services roughed in according to approved room layout drawings. *	As per ITP Thursday 20 April, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:34:14 pm
	Hold Point	
8	AV service roughened in according to approved room layout drawing. *	N/A Thursday 20 April, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:34:14 pm
	Hold Point	
9	Is fire stopping applied as per drawings? Attach evidence *	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:34:13 pm
	Hold Point	
10	Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:34:13 pm
	Hold Point	
11	ZipClad – Water Test Conducted on Facade *	N/A George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:34:13 pm
	Hold Point	
12	Are the noggings installed as required to suit fitments etc? Attach evidence *	Yes George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:34:13 pm
	Hold Point	

145 - Main Cleaners - Pre Sheet-ITP

13

Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:34:13 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

No

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:34:13 pm

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 20 April, 2023, 4:34:13 pm

16

Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan
Friday 26 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Friday 26 May, 2023, 2:50:36 pm

17 North Image * Hold Point

Friday 10 March, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:27:23 pm

Photos (1)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/07/12, 3:27:22 PM

145 - Main Cleaners - Pre Sheet-ITP

18	East Image * Hold Point	Friday 10 March, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:27:23 pm
19	South Image * Hold Point	Friday 10 March, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:27:23 pm
20	West Image * Hold Point	Friday 10 March, 2023 George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 3:27:23 pm

Name

Signature

Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

181 - Backflow & TMV Workshop - Pre Sheet ITP

Details

Project

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

Organization

ADCO CONSTRUCTIONS PTY LIMITED

Location

TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > 0.28 BACKFLOW & TMV WORKSHOP

Status

Closed

Due Date

Created by

George Awad on Wednesday 12 July, 2023, 2:38:32 pm

Modified by

George Awad on Thursday 07 September, 2023, 3:42:14 pm

Downloaded

Thursday 07 September, 2023, 3:42:29 pm

Template

NSW TAFE IATC - Pre Sheet ITP

Description

Date: Room / Location:

Progress

100%

QuestionResponse

1

Mark up plan of walls to be sheeted. *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 12 July, 2023, 2:38:32 pm

Photos (0)

Files (1)

Filename	Date	Attached by	Comments
Backflow & TMV Workshop.pdf	2023/07/12, 2:38:33 PM	George Awad	-

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:40:48 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Wall Mark UP LGF Latest.pdf	2023/08/24, 6:40:46 AM	George Awad	-

181 - Backflow & TMV Workshop - Pre Sheet ITP

[ITC & ITR Lighting & Power Rough in LGF.docx](#)

2023/08/24, 6:40:45 AM

George Awad

-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:40:48 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
ITC & ITR Lighting & Power Rough in LGF.docx	2023/08/24, 6:40:45 AM	George Awad	-
Wall Mark UP LGF Latest.pdf	2023/08/24, 6:40:47 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Thursday 24 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:40:48 am

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:42:02 pm

Photos (0)

Files (14)

Filename	Date	Attached by	Comments
V3 TMV Commissioning Report.pdf	2023/09/07, 3:41:50 PM	George Awad	-
V11 TMV Commissioning Report.pdf	2023/09/07, 3:41:52 PM	George Awad	-
V6 TMV Commissioning Report.pdf	2023/09/07, 3:41:51 PM	George Awad	-
V2 TMV Commissioning Report.pdf	2023/09/07, 3:41:48 PM	George Awad	-
V8 TMV Commissioning Report.pdf	2023/09/07, 3:41:52 PM	George Awad	-
RPZD REGISTER IATC.pdf	2023/09/07, 3:41:53 PM	George Awad	-
V9 TMV Commissioning Report.pdf	2023/09/07, 3:41:51 PM	George Awad	-
TMV REGISTER IATC.pdf	2023/09/07, 3:41:48 PM	George Awad	-
Containment test report - 1728534 - 2023-09-06.pdf	2023/09/07, 3:41:52 PM	George Awad	-
V7 TMV Commissioning Report.pdf	2023/09/07, 3:41:51 PM	George Awad	-
V10 TMV Commissioning Report.pdf	2023/09/07, 3:41:52 PM	George Awad	-
V5 TMV Commissioning Report.pdf	2023/09/07, 3:41:50 PM	George Awad	-
V1 TMV Commissioning Report.pdf	2023/09/07, 3:41:48 PM	George Awad	-

181 - Backflow & TMV Workshop - Pre Sheet ITP

[V4 TMV Commissioning Report.pdf](#)

2023/09/07, 3:41:51 PM

George Awad

-

6

Foran - Is the drainage installed as per drawings?

Attached evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:42:01 pm

Photos (0)

Files (14)

Filename	Date	Attached by	Comments
V2 TMV Commissioning Report.pdf	2023/09/07, 3:41:52 PM	George Awad	-
V11 TMV Commissioning Report.pdf	2023/09/07, 3:41:55 PM	George Awad	-
V8 TMV Commissioning Report.pdf	2023/09/07, 3:41:54 PM	George Awad	-
V3 TMV Commissioning Report.pdf	2023/09/07, 3:41:53 PM	George Awad	-
Containment test report - 1728534 - 2023-09-06.pdf	2023/09/07, 3:41:55 PM	George Awad	-
V6 TMV Commissioning Report.pdf	2023/09/07, 3:41:54 PM	George Awad	-
V10 TMV Commissioning Report.pdf	2023/09/07, 3:41:55 PM	George Awad	-
V4 TMV Commissioning Report.pdf	2023/09/07, 3:41:53 PM	George Awad	-
V9 TMV Commissioning Report.pdf	2023/09/07, 3:41:54 PM	George Awad	-
RPZD REGISTER IATC.pdf	2023/09/07, 3:41:55 PM	George Awad	-
V7 TMV Commissioning Report.pdf	2023/09/07, 3:41:54 PM	George Awad	-
V1 TMV Commissioning Report.pdf	2023/09/07, 3:41:53 PM	George Awad	-
TMV REGISTER IATC.pdf	2023/09/07, 3:41:55 PM	George Awad	-
V5 TMV Commissioning Report.pdf	2023/09/07, 3:41:53 PM	George Awad	-

7

Foran - Hydraulic services roughed in according to approved room layout drawings. *

Hold Point

As Per ITP

Thursday 07 September, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:42:02 pm

8

AV service roughened in according to approved room layout drawing. *

Hold Point



As Per ITP

Thursday 07 September, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:42:02 pm

9

Is fire stopping applied as per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:42:01 pm

<p>10</p> <p>Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *</p> <p>Hold Point</p>	<p>Yes</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:42:01 pm</p>																
<p>11 ZipClad - Water Test Conducted on Facade *</p> <p>Hold Point</p>	<p>N/A</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:42:01 pm</p>																
<p>12</p> <p>Are the noggings installed as required to suit fitments etc? Attach evidence *</p> <p>Hold Point</p>	<p>Yes</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:42:01 pm</p>																
<p>13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *</p> <p>Hold Point</p>	<p>Yes</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:42:01 pm</p>																
<p>14</p> <p>Are the mechanical works installed as per drawings? Attach evidence *</p> <p>Hold Point</p>	<p>Yes</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:42:01 pm</p>																
<p>Photos (0)</p>																	
<p>Files (3)</p> <table border="1" style="width: 100%; border-collapse: collapse;"> <thead> <tr> <th style="width: 35%;">Filename</th> <th style="width: 20%;">Date</th> <th style="width: 25%;">Attached by</th> <th style="width: 20%;">Comments</th> </tr> </thead> <tbody> <tr> <td>Lower Ground BMS Mark-up - 28.2.23.pdf</td> <td>2023/09/07, 3:41:59 PM</td> <td>George Awad</td> <td>-</td> </tr> <tr> <td>KERFOOT ITC - 14.2.23.pdf</td> <td>2023/09/07, 3:41:58 PM</td> <td>George Awad</td> <td>-</td> </tr> <tr> <td>GP-AR~1.PDF</td> <td>2023/09/07, 3:41:59 PM</td> <td>George Awad</td> <td>-</td> </tr> </tbody> </table>		Filename	Date	Attached by	Comments	Lower Ground BMS Mark-up - 28.2.23.pdf	2023/09/07, 3:41:59 PM	George Awad	-	KERFOOT ITC - 14.2.23.pdf	2023/09/07, 3:41:58 PM	George Awad	-	GP-AR~1.PDF	2023/09/07, 3:41:59 PM	George Awad	-
Filename	Date	Attached by	Comments														
Lower Ground BMS Mark-up - 28.2.23.pdf	2023/09/07, 3:41:59 PM	George Awad	-														
KERFOOT ITC - 14.2.23.pdf	2023/09/07, 3:41:58 PM	George Awad	-														
GP-AR~1.PDF	2023/09/07, 3:41:59 PM	George Awad	-														
<p>15</p> <p>Door Frames installed in plumb and have correct allowance for finish *</p> <p>Hold Point</p>	<p>Yes</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:42:01 pm</p>																

181 - Backflow & TMV Workshop - Pre Sheet ITP

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Thursday 07 September, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 3:42:02 pm

17 North Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 3:42:01 pm

Photos (1)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/09/07, 3:41:50 PM

18 East Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 3:42:01 pm

19 South Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 3:42:00 pm

20 West Image * Hold Point

Thursday 27 April, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 3:42:00 pm

Name

Signature


Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

147 - Gas Lab - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > 0.29 GAS LABS
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 3:56:01 pm
Modified by	Mark Zabica on Wednesday 18 October, 2023, 2:24:54 pm
Downloaded	Wednesday 18 October, 2023, 2:33:17 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

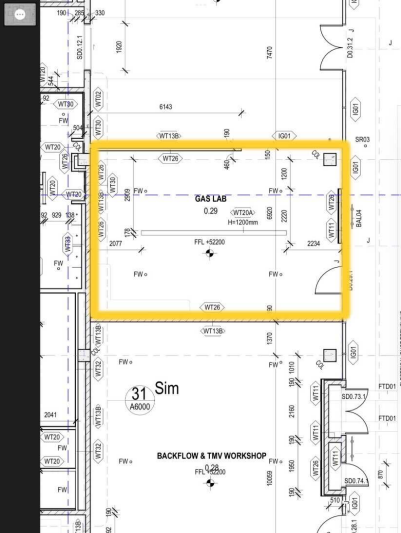Question	Response
<div>1</div> <div>Mark up plan of walls to be sheeted. *</div> <div>Hold Point</div>	<div>Yes</div> <div>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 14 March, 2023, 12:07:56 pm</div>
<div>Photos (1)</div> <div></div> <div>Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/03/14, 12:07:59 PM</div>	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:44:03 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Wall Mark UP LGF Latest.pdf	2023/08/24, 7:44:02 AM	George Awad	-
ITC & ITR Lighting & Power Rough in LGF.docx	2023/08/24, 7:44:00 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:44:03 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
ITC & ITR Lighting & Power Rough in LGF.docx	2023/08/24, 7:44:00 AM	George Awad	-
Wall Mark UP LGF Latest.pdf	2023/08/24, 7:44:02 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Thursday 24 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 7:44:03 am

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point



Yes

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 18 October, 2023, 2:19:12 pm

Photos (0)

Files (1)

Filename	Date	Attached by	Comments
aerial gas (GAS LAB) ITP.pdf	2023/10/18, 2:19:10 PM	Mark Zabica	-

<p>6</p> <p>Foran - Is the drainage installed as per drawings? Attached evidence *</p> <p>Hold Point</p>	<p>Yes</p> <p>Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 18 October, 2023, 2:19:12 pm</p>
<p>7</p> <p>Foran - Hydraulic services roughed in according to approved room layout drawings. *</p> <p>Hold Point</p>	<p></p> <p>Mark Zabica Wednesday 18 October, 2023</p> <p>Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 18 October, 2023, 2:19:12 pm</p>
<p>8</p> <p>AV service roughened in according to approved room layout drawing. *</p> <p>Hold Point</p>	<p></p> <p>Mark Zabica Wednesday 18 October, 2023</p> <p>Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 18 October, 2023, 2:19:12 pm</p>
<p>9</p> <p>Is fire stopping applied as per drawings? Attach evidence *</p> <p>Hold Point</p>	<p>N/A</p> <p>Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 18 October, 2023, 2:19:12 pm</p>
<p>10</p> <p>Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *</p> <p>Hold Point</p>	<p>N/A</p> <p>Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 18 October, 2023, 2:19:12 pm</p>
<p>11 ZipClad - Water Test Conducted on Facade *</p> <p>Hold Point</p>	<p>N/A</p> <p>Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 18 October, 2023, 2:19:11 pm</p>
<p>12</p> <p>Are the noggings installed as required to suit fitments etc? Attach evidence *</p> <p>Hold Point</p>	<p>Yes</p> <p>Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 18 October, 2023, 2:19:11 pm</p>

Photos (5)


147 - Gas Lab - Pre Sheet-ITP



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/10/18, 2:18:47 PM



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/10/18, 2:18:51 PM

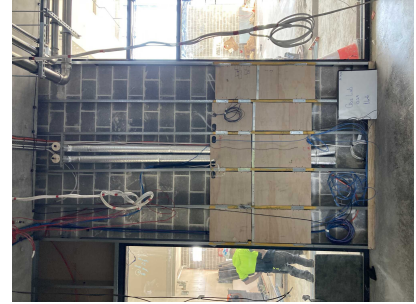

Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/10/18, 2:19:01 PM



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/10/18, 2:19:03 PM



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/10/18, 2:18:57 PM

13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *

Hold Point

Yes

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 18 October, 2023, 2:19:11 pm

14

Are the mechanical works installed as per drawings? Attach evidence *

Hold Point

Yes

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 18 October, 2023, 2:19:11 pm

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

Yes

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 18 October, 2023, 2:19:11 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point

WZ

Mark Zabica
Wednesday 18 October, 2023

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 18 October, 2023, 2:19:12 pm

17 North Image * Hold Point

Tuesday 02 May, 2023

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday 18 October, 2023, 2:19:11 pm

Photos (1)



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/10/18, 2:18:49 PM

18 East Image * Hold Point

Tuesday 02 May, 2023

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday
18 October, 2023, 2:19:11 pm

Photos (1)



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/10/18, 2:19:06 PM

19 South Image * Hold Point

Tuesday 02 May, 2023

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday
18 October, 2023, 2:19:11 pm

Photos (1)



Captured by: **Mark Zabica ADCO CONSTRUCTIONS PTY LIMITED**
Date: 2023/10/18, 2:18:59 PM

20 West Image * Hold Point

Tuesday 02 May, 2023

Mark Zabica - ADCO CONSTRUCTIONS PTY LIMITED., Wednesday
18 October, 2023, 2:19:10 pm

Photos (1)



Captured by: **Mark Zabica ADCO
CONSTRUCTIONS PTY LIMITED**
Date: **2023/10/18, 2:19:09 PM**

Name

Signature


Date

(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY

TAFE NSW, 12-44 O'CONNELL ST,
KINGSWOOD,
NSW Australia 2747

148 - IAT Space B - Pre Sheet-ITP

Details	
Project	(3547) TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY
Organization	ADCO CONSTRUCTIONS PTY LIMITED
Location	TAFE NSW INSTITUTE OF APPLIED TECHNOLOGY FOR CONSTRUCTION > LOWER GROUND FLOOR > 0.31 IAT SPACE B
Status	Closed
Due Date	
Created by	George Awad on Friday 03 March, 2023, 2:57:31 pm
Modified by	George Awad on Thursday 07 September, 2023, 3:47:05 pm
Downloaded	Thursday 07 September, 2023, 3:47:34 pm
Template	NSW TAFE IATC - Pre Sheet ITP
Description	Date: Room / Location:
Progress	100%

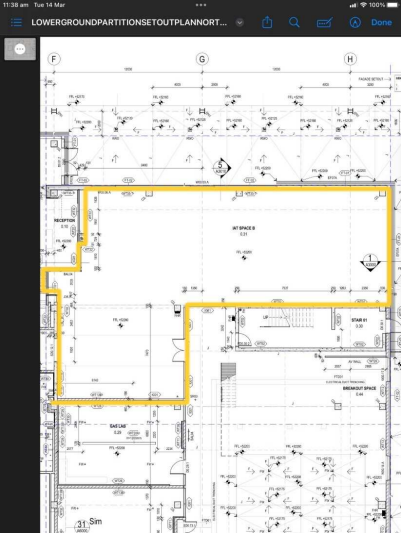Question	Response
<div>1</div> <div>Mark up plan of walls to be sheeted. *</div> <div>Hold Point</div>	<div>Yes</div> <div>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Tuesday 14 March, 2023, 11:09:00 am</div>
<div>Photos (1)</div> <div></div> <div>Captured by: George Awad ADCO CONSTRUCTIONS PTY LIMITED Date: 2023/03/14, 11:09:03 AM</div>	

2

Utech - Is the power installed per drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:51:41 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
ITC & ITR Lighting & Power Rough in LGF.docx	2023/08/24, 6:51:36 AM	George Awad	-
Wall Mark UP LGF Latest.pdf	2023/08/24, 6:51:39 AM	George Awad	-

3

Utech - Are the communications and security cabling installed as per the drawings? Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:51:41 am

Photos (0)

Files (2)

Filename	Date	Attached by	Comments
Wall Mark UP LGF Latest.pdf	2023/08/24, 6:51:39 AM	George Awad	-
ITC & ITR Lighting & Power Rough in LGF.docx	2023/08/24, 6:51:36 AM	George Awad	-

4

Utech - Electrical services roughed in according to approved room layout drawings. *

Hold Point



George Joannou
Thursday 24 August, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:51:41 am

5

Foran - Is the potable water installed as per drawings? Attach evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:51:40 am

6

Foran - Is the drainage installed as per drawings? Attached evidence *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:51:40 am

<p>7</p> <p>Foran - Hydraulic services roughed in according to approved room layout drawings. *</p> <p>Hold Point</p>	<p>N/A</p> <p>Thursday 24 August, 2023</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 24 August, 2023, 6:51:41 am</p>
<p>8</p> <p>AV service roughened in according to approved room layout drawing. *</p> <p>Hold Point</p>	<p></p> <p>As Per ITP</p> <p>Thursday 07 September, 2023</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:46:50 pm</p>
<p>9</p> <p>Is fire stopping applied as per drawings? Attach evidence *</p> <p>Hold Point</p>	<p>Yes</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:46:50 pm</p>
<p>10</p> <p>Vapour barrier installed as per installation guide. All penetration sealed with tape and or sealant. *</p> <p>Hold Point</p>	<p>Yes</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:46:50 pm</p>
<p>11 ZipClad - Water Test Conducted on Facade *</p> <p>Hold Point</p>	<p>Yes</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:46:50 pm</p>
<p>12</p> <p>Are the noggings installed as required to suit fitments etc? Attach evidence *</p> <p>Hold Point</p>	<p>Yes</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:46:50 pm</p>
<p>13 Is the acoustic insulation installed as per specification/drawings? Attache evidence *</p> <p>Hold Point</p>	<p>Yes</p> <p>George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:46:50 pm</p>

14

Are the mechanical works installed as per drawings?

Attach evidence *

Hold Point

Yes

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 3:46:50 pm

Photos (0)

Files (3)

Filename	Date	Attached by	Comments
KERFOOT ITC - 14.2.23.pdf	2023/09/07, 3:46:48 PM	George Awad	-
GP-AR~1.PDF	2023/09/07, 3:46:47 PM	George Awad	-
Lower Ground BMS Mark-up - 28.2.23.pdf	2023/09/07, 3:46:47 PM	George Awad	-

15

Door Frames installed in plumb and have correct allowance for finish *

Hold Point

N/A

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 3:46:51 pm

16 Dunrite Accepts walls are ready for sheet *

Hold Point



Hills Pan

Thursday 07 September, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 3:46:52 pm

17 North Image * Hold Point

Tuesday 30 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 3:46:50 pm

Notes

Northern Elevation is glazing. No pre-sheet required

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday 07 September, 2023, 3:46:50 pm

18 East Image * Hold Point

Tuesday 30 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 3:46:50 pm

Photos (1)

Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED

Date: 2023/09/07, 3:46:46 PM

19 South Image * Hold Point

Tuesday 30 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 3:46:49 pm

Photos (2)



Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/09/07, 3:46:42 PM




Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/09/07, 3:46:44 PM

20 West Image * Hold Point

Tuesday 30 May, 2023

George Awad - ADCO CONSTRUCTIONS PTY LIMITED., Thursday
07 September, 2023, 3:46:49 pm

Photos (1)

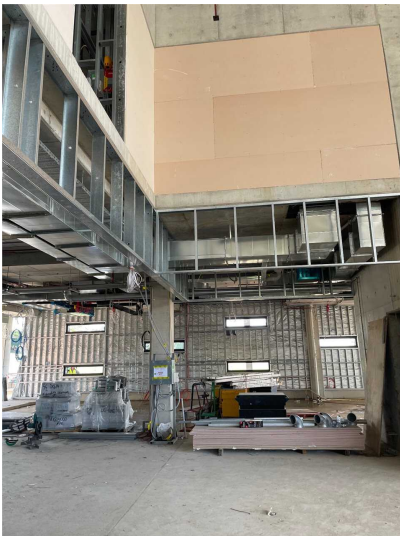

Captured by: George Awad ADCO
CONSTRUCTIONS PTY LIMITED
Date: 2023/09/07, 3:46:40 PM

Name

Signature

Date
